

SELECTION AND IMPLEMENTATION OF ALTERNATIVES REPORT

Camden County Municipal Utilities Authority
City of Camden
Gloucester City



NJPDES Permit Nos.

NJ0026182

NJ0108812

NJ0108847

September 2020

Revised September
2023



Table of Contents

Intermunicipal Agreements

N.J.A.C. 7:14A-4.9 Certification Forms [updated forms pending NJDEP review of draft revisions and municipal approvals]

Glossary of Terms Used in this Selection and Implementation of Alternatives Report

Executive Summary

E1	Introduction	E-1
E2	Long Term Control Strategy	E-1
E3	Additional Controls Likely Will be Necessary	E-4
E4	Getting to 85% System-Wide Capture	E-5
E5	Preliminary System-Wide Cost Estimates	E-11
E6	Cost-Performance Considerations	E-11
E7	Cooper River Designated Use Reclassification	E-13
E8	Affordability & Financial Capability	E-14
E9	Selected Long Term Control Plan	E-18
E10	Implementation Schedule and Adaptive Management	E-20

1.0 SIAR INTRODUCTION

1.1	Regulatory Context and Objectives	1-1
1.2	Overview of the Combined Sewer system	1-4
1.3	Previous Studies	1-7
1.4	Overview of Control Alternatives in the DEAR	1-7
1.5	Organization of the Report	1-9
1.6	Stakeholder Involvement in the SIAR Development	
1.6.1	Introduction	1-10
1.6.2	Completed Outreach Activities	1-12
1.6.3	CSO Supplemental Team	1-17
1.6.4	Additional Municipal Coordination	1-19

2.0 MAXIMIZING FLOWS TO WPCF # 1

2.1	CCMUA'S WATER POLLUTION CONTROL FACILITY # 1	2-1
2.2	Regulator Context	2-3
2.3	Wet Weather Capacity Expansion Beyond 220 MGD	2-3
2.4	Impacts of Capacity Expansion to 185 MGD on Wet Weather Capture	
2.4.1	CCMUA Water Pollution Control Facility #1	2-4
2.4.2	City of Camden's Arch Street Pump Station	2-6

3.0 GREEN STORMWATER INFRASTRUCTURE IMPLEMENTATION

3.1	GSI Implementation Target	3-1
-----	---------------------------------	-----

3.2	Wet Weather Benefits of GSI	3-1
3.3	GSI Implementation Strategy	3-2
3.4	Draft GSI Implementation Program Framework	3-3
3.5	GIS Activities Since the September 2020 SIAR Submittal	3-7
4.0	MITIGATION OF STREET FLOODING	
4.1	Problem Overview	4-1
4.2	Street Flooding Benefits of CSO Controls	4-3
4.3	Street Flooding Mitigation Program	4-4
4.4	Street Flooding Mitigation Activities Since the September 2021 SIAR Submittal	4-5
5.0	ADDITIONAL CONTROL REQUIREMENTS	
5.1	Additional Control Requirements	5-1
5.2	Overview of Recommended Control Technologies	
5.2.1	Satellite Treatment	5-3
5.2.2	Satellite Storage	5-4
5.2.3	Reduction of Inflow and Infiltration	5-5
5.3	Control Alternatives	
5.3.1	Summary Assessment of Control Options	5-6
5.3.2	Storage and Treatment Cost Estimation	5-6
5.3.3	Permittee Specific Cost Estimates	5-6
5.4	Cost / Performance Considerations	5-11
5.5	Site Considerations	5-14
5.6	Section Conclusions	5-17
6.0	FINANCIAL & INSTITUTIONAL CAPABILITY	
6.1	Affordability Assessment	
6.1.1	Purpose	6-1
6.1.2	Estimated Current Wastewater Costs per Household	6-2
6.1.3	Affordability Impacts of CSO Control Alternatives	6-5
6.1.4	Methodology and Underlying Assumptions	6-7
6.2	Financial Capability Assessment	6-8
6.2.1	Bond Ratings – Indicator 1	6-9
6.2.2	Overall Net Debt – Indicator 2	6-10
6.2.3	Unemployment Rate – Indicator 3	6-10
6.2.4	Median Household Income – Indicator 4	6-10
6.2.5	Tax Revenues as a Percentage of Full Market Property Value – Indicator 5	6-11
6.2.6	Property Tax Collected Rate – Indicator 6	6-11
6.2.7	Financial Indicator Score	6-11

6.3	Financial Capability Matrix.....	6-12
6.4	Additional Economic Factors	
6.4.1	Cost of Living Index	6-14
6.4.2	Housing Costs.....	6-15
6.4.3	Local Tax Burden	6-15
6.4.4	Poverty Rate.....	6-15
6.4.5	Income Growth Trends	6-15
6.4.6	New Jersey Municipal Revitalization Index.....	6-16
6.5	Institutional Context	
6.5.1	System Ownership, Operation and Maintenance.....	6-18
6.5.2	Legal Framework.....	6-18
6.6	Potential Impact of the COVID 19 Pandemic on Affordability	
6.6.1	Potential Wastewater System Revenue Impacts	6-20
6.6.2	Potential Median Household Income Impacts.....	6-21
6.6.3	Implications for the Long Term Control Program	6-21
6.7	USEPA Proposed Revisions to the Financial Capability Assessment Methodology	6-22
7.0	SELECTION OF LONG TERM CONTROL ALTERNATIVES	
7.1	Selected Long Term Control Program Overview.....	7-1
7.2	Program Element 1 – Completion of Current Controls	
7.2.1	Treatment Plant Capacity Expansion	7-3
7.2.2	Hydraulic Capacity Restoration.....	7-4
7.3	Program Element 2 – Efficacy Evaluation	7-6
7.4	Program Element 3 – Formalized Green Infrastructure Program.....	7-6
7.5	Program Element 4 – Street Flooding Remediation Program	7-7
7.6	Program Element 5 – Cooper River Regional Water Quality Optimization	7-7
7.7	Program Element 6 – Sub-System Structural Controls to Achieve 85% Capture.....	7-10
7.8	Implications of the Financial Capability Assessment	
7.8.1	Problem Statement.....	7-12
7.8.2	Impacts of Inflation	7-13
7.8.3	Alternative Implementation Schedules	7-14
7.8.4	Annual Pay-As-You-Go Funding	7-15
7.8.5	External Funding Needs	7-15
7.9	Construction and Financing Schedule.....	7-16
8.0	IMPLEMENTATION SCHEDULE AND ADAPTIVE MANAGEMENT	
8.1	Implementation Scheduling Context	8-1
8.2	Proposed Implementation Schedule	8.1

8.3 Adaptive Management.....	8-2
------------------------------	-----

APPENDIX A – Documentation Of Stakeholder Participation

APPENDIX B – NJDEP Comment Letter of 5/7/21 and Joint Response of 7/7/21

APPENDIX C – NJDEP Comment Letter of 6/13/23 and Joint Response of 7/10/23

APPENDIX D – NJDEP Comment Letter of 8/9/23 and Joint Response of 9/8/23

LIST OF TABLES

E-1 Benefits of CSO Control Elements Before Satellite Facilities	E-4
E-2 Required Satellite Control Facilities Capacities	E-7
E-3 Potential Satellite Facilities Vicinity Information	E-8
E-4 System-Wide Rollup of Cost Estimates	E-12
E-5 EPA Residential Indicator	E-14
E-6 Calculated Costs per Typical Residential Wastewater User in 2019	E-15
E-7 Affordability Impacts of the 85% Control Program Capital Costs	E-15
E-8 Base Case Implementation Schedule for Affordability Analysis	E-16
E-9 Impacts of Implementation Scheduling on the Residential Indicators	E-17
E-10 Maximum Annual Expenditure Without Triggering 2.0% Residential Indicator	E-17
E-11 External Funding and/or Capital Cost Reduction Impacts on Residential Indicator	E-17
1-1 Proactive CSO Control Projects	1-2
1-2 Collection System Overview	1-5
1-3 System-Wide Characteristics Used for Control Alternatives Development	1-5
1-4 Previous Studies	1-7
1-5 Location of NJPDES Referenced Elements of the Long Term Control Plan	1-9
2-1 Delaware WPCF # 1 Effluent Limitations.....	2-1
2-2 Overall Comparison of Flow Rates	2-4
2-3 Frequency Distribution of Days With Peak Flows	2-5
2-4 Peak Daily Flow Rate by Month.....	2-5
2-5 Frequency of Arch Street PS Shutdowns During Wet Weather	2-6
3-1 Calculation of Target Control of Runoff from DCIA.....	3-1
3-2 GSI and Source Reduction Projects Undertaken Since 2017.....	3-7
4-1 Camden Sewersheds Associated with Street Flooding	4-1
4-2 Street Flooding Mitigation and Source Reduction Projects Undertaken Since 2020.....	4-5
5-1 Typical Year Capture Impacts of Controlling Runoff	5-1
5-2 Required Satellite Control Capacities.....	5-2
5-3 Qualitative Comparison of EHRC and Storage.....	5-6
5-4 Camden CSO 85% Typical Year Wet Weather Control Cost Estimates	5-7
5-5 City of Camden CSO Controls Estimated Annual O&M and Lifecycle Costs.....	5-8

5-6	Gloucester City CSO Control Cost Estimation	5-9
5-7	Gloucester City CSO Control Estimated Annual O&M and Lifecycle Costs	5-9
5-8	CCMUA Capital Cost Estimates	5-10
5-9	CCMUA CSO Control Incremental O&M and Lifecycle Costs	5-11
5-10	System-Wide Rollup of Estimated Costs	5-12
5-11	Potential Satellite Facilities Vicinities Information	5-14
6-1	USEPA Residential Indicator	6-3
6-2	Calculated Cost per Typical Residential Wastewater Account	6-3
6-3	Analysis of Current Residential Indicator for Camden	6-4
6-4	Analysis of Current Residential Indicator for Gloucester	6-5
6-5	Affordability Impacts of the Evaluated CSO Controls – Camden	6-5
6-6	Affordability Impacts of the Evaluated CSO Controls – Gloucester	6-6
6-7	Affordability Impacts of the Evaluated CSO Controls – CCMUA	6-6
6-8	Affordability Model Key Inputs & Assumptions	6-8
6-9	Permittee Financial Capability Indicator Benchmarks	6-9
6-10	Median Household Incomes	6-11
6-11	Permittee Financial Capability Indicator Benchmarks	6-11
6-12	The Financial Capability Matrix – Camden	6-13
6-13	The Financial Capability Matrix – Gloucester	6-13
6-14	The Financial Capability Matrix – CCMUA	6-13
6-15	Municipal Renewal Index for CCMUA Municipalities	6-16
7-1	Projected Cumulative CSO Control Levels as the Program is Implemented	7-2
7-2	Ongoing Wet Weather Control Capital Investments	7-5
7-3	Initial Cooper River Water Quality Sampling	7-9
7-4	Control Facility Sizing Implications of Zero DCIA Reductions	7-11
7-5	Financial Capability and Control Program Capital Costs	7-12
7-6	Affordability Analysis Base Case Implementation Schedule	7-14
7-7	Impacts of Scheduling on the Residential Indicator	7-14
7-8	Maximum Annual Expenditures Without Triggering a 2.0% Residential Indicator	7-15
7-9	External Funding / Capital Cost Reduction Required	7-15

LIST OF FIGURES

Figure E-1 – Camden and Gloucester Sewer System Base Map	E-2
Figure E-2 – Combined Sewer System – Five Sub-Systems	E-6
Figure E-3 – Example 25 MGD Enhanced High Rate Clarification Treatment Facility	E-8
Figure E-4 – Example of Satellite Storage Facility	E-8
Figure E-5 – Vicinity of Gloucester City Regulators G-4 and G-5	E-9

Figure E-6 – Vicinity of Camden C-22 / C-22A Outfalls	E-10
Figure E-7 – Vicinity of Camden C-27 and Thorndyke St. Outfalls	E-10
Figure E-8 – Vicinity of Camden C-17 Regulator, Netting Facility and Outfall	E-11
Figure E-9 – Cost / Performance Relationship	E-13
Figure E-10 – Eastern Pond Mussel.....	E-13
Figure 1.1 – Camden and Gloucester Sewer System Base Map.....	1-6
Figure 1-2 – Combined Sewer System – Five Sub-Systems.....	1-8
Figure 2-1 – Delaware WPCF # 1 Process Flow Schematic.....	2-2
Figure 2-2 – Plan View of WPCF # 1	2-4
Figure 4-1 – Locations Associated With Street Flooding.....	4-2
Figure 5-1 – Enhance High Rate Clarification	5-3
Figure 5-2 – Examples of Satellite Storage Facilities.....	5-5
Figure 5-3 – Correlation Between Overflow Frequencies and Volume	5-13
Figure 5-4 – Cost / Performance Relationship Between Frequency and Volume Based Control Strategies.....	5-14
Figure 5-5 – Relationship Between Frequency and Volume Based Control Strategies – Remaining CSO Volume After Implementation	5-14
Figure 5-6 – Vicinity of Gloucester City Regulators G-4 and G-5	5-15
Figure 5-7 – Gloucester City CSO Control Potential Alternative Site Vicinity	5-15
Figure 5-8 – Vicinity of Camden Regulators C-22 / C-22A.....	5-16
Figure 5-9 – Vicinity of Camden Regulator C-27 & Thorndyke Outfall	5-16
Figure 5-10 – Vicinity of Camden C-17 Regulator	5-17
Figure 7-1 – Cooper River Water Quality Sampling Locations	7-9
Figure 7-2 – Comparison of Rates of Growth.....	7-13
Figure 8-1 – Proposed LTCP Implementation Schedule.....	8-6

Resolution of

THE CAMDEN COUNTY MUNICIPAL UTILITIES AUTHORITY

Authorizing the Executive Director to Submit the CCMUA Component of the Revised CCMUA, Camden City and Gloucester City Long Term Control Plan

R-23:10-178

Whereas, on September 21, 2020, the CCMUA's Board of Commissioners authorized its Executive Director, via Resolution #R-20:8-126, to submit the CCMUA component of the CCMUA, Camden City and Gloucester City (the permittees) long term control plan Long-Term Control Plan (LTCP) to the New Jersey Department of Environmental Protection (NJDEP); and

Whereas, subsequent to the submission of the LTCP in October of 2020, the NJDEP issued technical comment letters and, at various times, requested other information which the permittees provided; and

Whereas, the permittees received a letter on August 9, 2023, which stated in part "Given that the Department is moving forward with the NJPDES Permit, an updated LTCP is needed to amend the Administrative Record"; and

Whereas, the amended LTCP does not provide for major changes in the scope of the plan, but does provide for firmer scheduling commitments; and

Whereas, the permittees, the NJDEP, and the permittees' consultant CDM Smith, have tentatively agreed on the schedule as described in the revised LTCP; and

Whereas, the Executive Director recommends CCMUA approval of the revised LTCP.

Now, Therefore Be it Resolved by the CCMUA Board of Commissioners that it authorizes its Executive Director to submit to the New Jersey Department of Environmental Protection, the CCMUA component of the revised CCMUA, Camden City and Gloucester City Long-Term Control Plan.

ADOPTED: October 16, 2023



Kim Michelini, Secretary

I certify that the above is a true copy of the resolution adopted by the members of the Camden County Municipal Utilities Authority at a meeting held on October 16, 2023.



**Camden County Municipal Utilities Authority
NJPDES Permit NJ0026182 Submittal
N.J.A.0 7:14A-4.9 Certification Form**

Pursuant to the requirements under NJPDES Permit NJ0026182, the Camden County Municipal Utilities Authority, Camden County New Jersey is submitting the following document(s):

Selection and Implementation of Alternatives Report

(Title of Document)

As required under Part IV - Combined Sewer Management Paragraph D.1(c) (Submittals), the Authority is providing the following certification:

"I certify under penalty of law that this document and all attachments were prepared either: (a) under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted; or (b) as part of a cooperative effort by members of a hydraulically connected system, as is required under the NJPDES Permit, to provide the information requested. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for purposely, knowingly, recklessly, or negligently submitting false information".

Name: Scott Schreiber, Title: Executive Director
Camden County Municipal Utilities Authority



Signature

October 2, 2024
Date

**Camden County Municipal Utilities Authority
NJPDES Permit NJ0026182 Submittal
N.J.A.C 7:14A-4.9 Certification Form**


Pursuant to the requirements under NJDPDES Permit NJ0108812, the City of Camden, New Jersey is submitting the following document(s):

Selection and Implementation of Alternatives Report

As required under Part IV – Combined Sewer Management Paragraph D.1(c) (Submittals), the Authority is providing the following certification:

“I certify under penalty of law that this document and all attachments were prepared either : (a) under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted; or (b) as part of a cooperative effort by members of a hydraulically connected system as is required under the NJPDES Permit, to provide the information requested. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there is significant penalties for submitting false information, including the possibility of fine and imprisonment for purposely, knowingly, recklessly, or negligently submitting false information”.

Name: Victor G. Carstarphen , Title: Mayor
City of Camden



Signature

10-15-2024

Date

**Camden County Municipal Utilities Authority
NJPDES Permit NJ0026182 Submittal
N.J.A.C 7:14A-4.9 Certification Form**


Pursuant to the requirements under NJPDES Permit NJ0108847, Gloucester City, New Jersey is submitting the following document(s):

Selection and Implementation of Alternatives Report

As required under Part IV - Combined Sewer Management Paragraph D.1(c) (Submittals), the Authority is providing the following certification:

"I certify under penalty of law that this document and all attachments were prepared either: (a) under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted; or (b) as part of a cooperative effort by members of a hydraulically connected system, as is required under the NJPDES Permit, to provide the information requested. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for purposely, knowingly, recklessly, or negligently submitting false information."

Name: Dayl R. Baile, Title: Mayor
Gloucester City, New Jersey


Signature

10-17-2024
Date

Executive Summary

Executive Summary Revised September 2023

E.1 Introduction

This document constitutes Camden County Municipal Utilities Authority's (CCMUA) *Revised Selection and Implementation Report* (SIAR) developed on behalf of CCMUA, the City of Camden and Gloucester City (the Cities). Submitted to the New Jersey Department of Environmental Protection (NJDEP) in September of 2020, the original SIAR was the third of the three NJPDES required documents which comprise the Authority's and the Cities' combined sewer overflow (CSO) draft Long Term Control Plan (LTCP). This revised version of the SIAR incorporates responses to NJDEP's review comments on the 2020 report and updates the 2020 report to reflect progress to date on the implementation of the LTCP since September of 2020.

The 2018 System Characterization Report documented the physical nature and baseline performance of the combined sewer system. The 2019 Development and Evaluation of Alternatives (DEAR) evaluated approaches to controlling combined sewer overflows. This SIAR documents the selection of a long term strategy, schedule and institutional framework for implementation of CSO controls. This SIAR maintains the CSO control target of capturing for treatment 85% of the combined sewage generated during precipitation events occurring over the Typical Year. A Typical Year is a statistically determined historical year that is representative of typical weather and other conditions driving the behavior of a sewer system. The combined sewer system addressed by this report is shown on Figure E-1 on the following page.


Due to the unique and challenging circumstances facing Camden and Gloucester, it was apparent to CCMUA, the City of Camden and Gloucester City from the outset that the communities and the environment will be best served by leveraging a coordinated and collaborative approach combining regulatory compliance, sustainable redevelopment and environmental justice. Towards these ends, the program outlined in this SIAR focuses on near term community benefits through:

- Sustainable community redevelopment using green stormwater infrastructure (GSI);
- Reduce street and basement flooding of combined sewage during storms; and
- The optimization of and reinvestment in existing community assets such as the restoration of the Camden sewer system through comprehensive cleaning.

E.2 Long Term Control Strategy

The proposed long term control strategy is the following:

- ***Optimizing the Current System*** – which is well underway. CCMUA has completed the capacity expansion of its Delaware Water Pollution Control Facility #1 (WPCF) from 150 million gallons per day (MGD) to 185 MGD. The wet-weather control benefits of the plant expansion experienced to date are documented in Section 2.4 of this revised SIAR. This project will also enable the potential expansion of wet weather treatment capacity to 220 MGD. Expansion to 220 MGD was determined to be not necessary or cost effective to meet the 85% system-wide typical year.

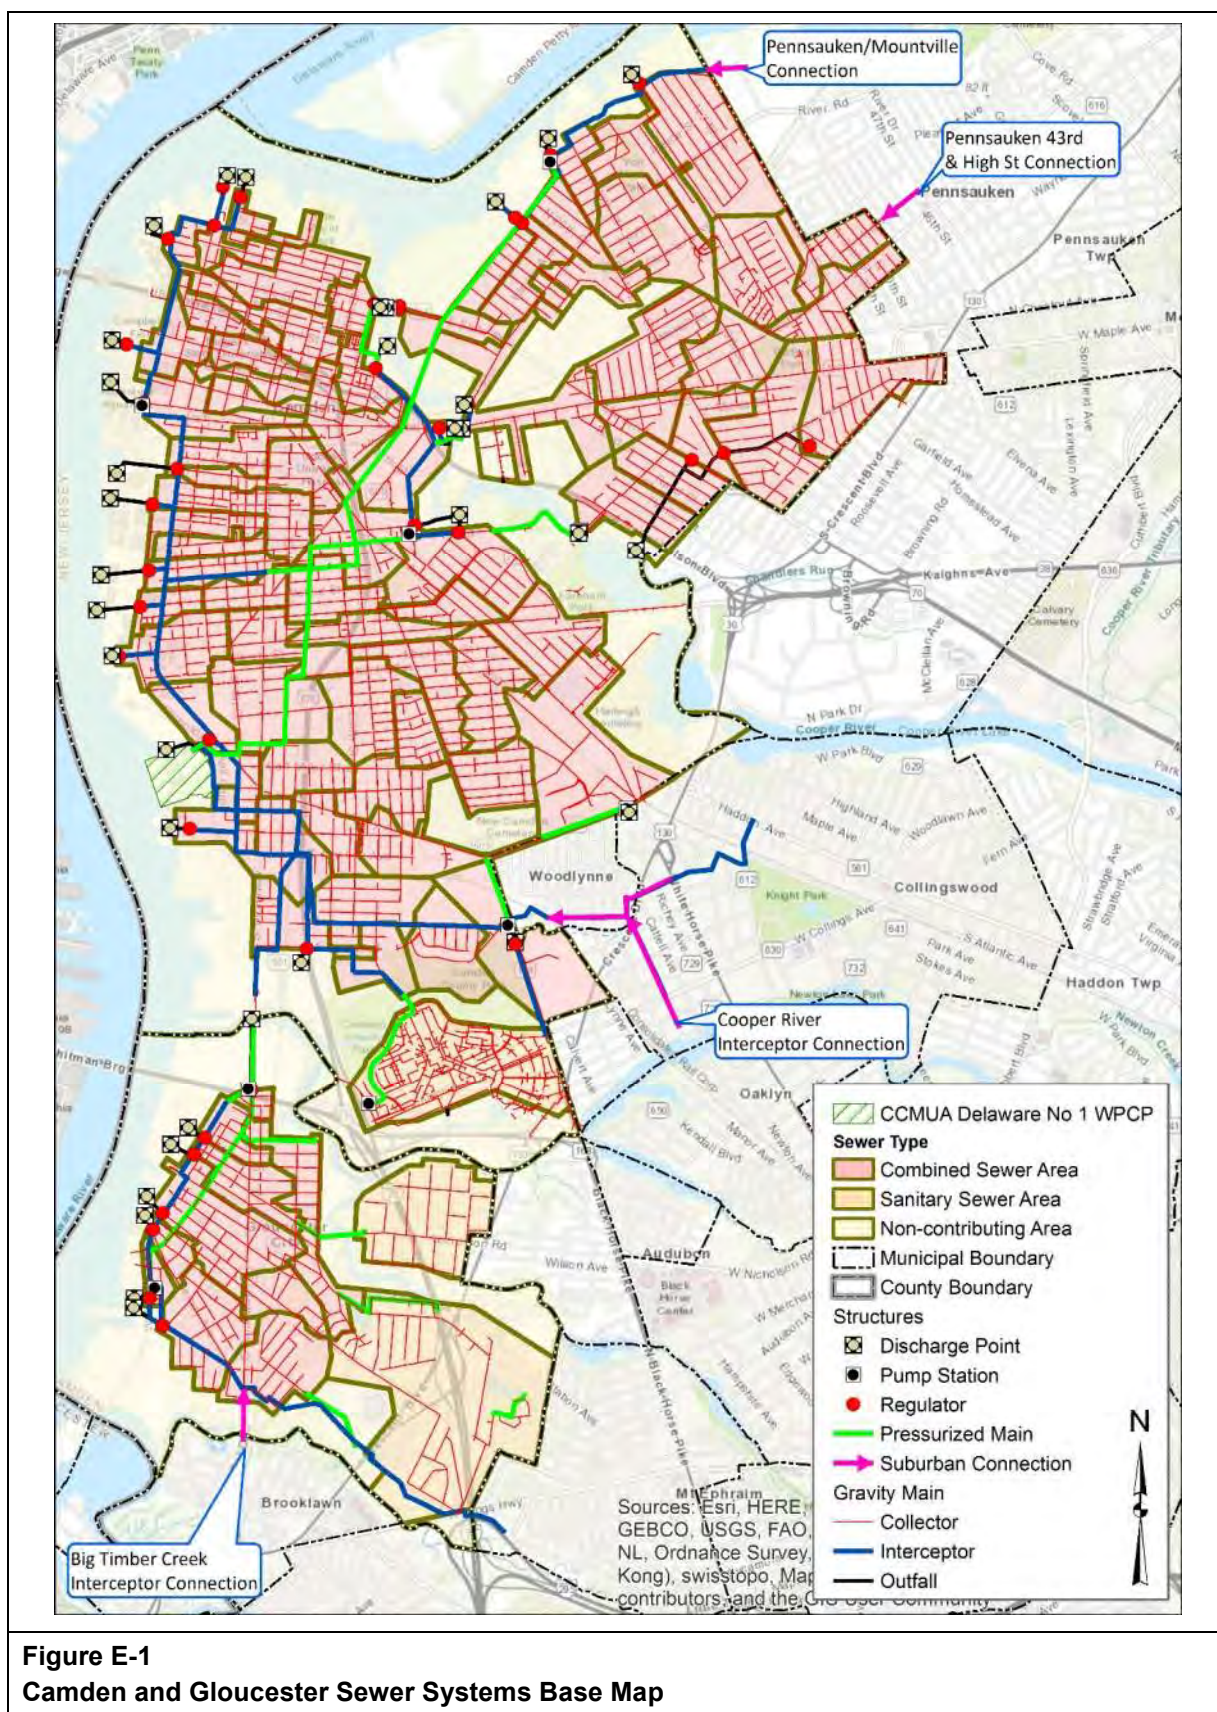

capture target however in the 2020 SIAR. If warranted, this option could be re-examined during the updating of the structural controls analysis anticipated in the 2027-2028 timeframe.

Meanwhile, the Cities are restoring the hydraulic capacity of ~~its~~ their combined collection sewer systems through the comprehensive remedial cleaning of their combined sewer system and combined sewer outfalls and have completed related capital improvements such as the upgrading of capacity of Camden's Arch Street pump station and the rehabilitation of Camden's twenty-eight regulator structures. CCMUA's and the Cities' proactive LTCP implementation projects pending NJDEP approval of the SIAR or issuance of the post 2021 NJPDES permit are listed on Table 1-1.

A detailed schedule for the completion of the system optimization projects during the forthcoming (2024 – 2028) NJPDES five-year permit cycle is provided in Section 8 of this revised SIAR and also summarized in Section E-10.

- ***Monitor and Evaluate before Building More Controls*** - This SIAR is based on the best available information. A comprehensive and iterative process of measuring and evaluating the efficacy of the on-going projects, GSI and street flooding mitigation will inform future decisions about the need for, size of and technical approaches to building structural (grey) control facilities. Initial flow monitoring in support of the development of the baseline hydrologic and hydraulic (H&H) model and its use to assess system performance was conducted in 2016 and augmented in subsequent years. Upon completion of the comprehensive system-wide remedial cleaning currently under way CCMUA and the Cities will recalibrate the H&H model to reflect then current conditions.
- ***Lead with Green*** - Camden's, Gloucester City's and CCMUA's acclaimed green stormwater infrastructure (GSI) and neighborhood redevelopment efforts will be formalized and expanded with an aggressive goal of a ten percent reduction in the directly connected impervious areas (DCIA) contributing stormwater runoff to the combined sewer system. Details are in Section 3. As of September 2023, green stormwater management projects for approximately 29 acres in the combined sewered areas of Camden and Gloucester City have been completed or are in planning and design since 2017. These projects are listed in Section 3.5.
- ***Address Street Flooding*** - A key control program element is a comprehensive Street Flooding Mitigation Program to serve as the basis for short and long term operational and capital improvements. Details are in Section 4. Street flooding mitigation projects and projects with street flooding benefits since September 2020 are listed in Section 4.4 of this revised SIAR.
- ***Cooper River Water Quality Optimization Program*** - While the Cooper River is a vital environmental, recreational and economic redevelopment asset, eliminating CSOs from the Cooper River is not financially feasible and would not result in water quality compliance. To optimize what is achievable, the development of a **Cooper River Water Quality Optimization Strategy** is proposed. Details are in Section 7. CCMUA implemented a prototype Cooper River sampling program in the summer of 2023. Six sampling locations were selected for 2023 with five along

Cooper River and one on the back channel of the Delaware River. Over the course of eight sampling events in May and June the E.-coli water quality standard of 235 CFU/ 100 ml for single samples and of 126 CFU/100 ml for the geometric means were exceeded in all of the locations upstream of CSO influence during dry weather sampling events.

- **Additional Structural Controls as Necessary** – structural controls (e.g., storage tanks) are necessary to raise the level of capture system-wide to no less than 85% of wet weather flows during the Typical Year. The sizing and scheduling of these facilities will be determined based upon the results of the green source water reduction, street flooding remediation and Cooper River optimization efforts described above. Details are in Section 5.

During the next five-year NJPDES permit cycle (2024 – 2028), based on the post-cleaning flow monitoring and H&H model update, CCMUA and the Cities will update the structural control alternatives analyses conducted to develop the 2020 SIAR. The updated alternatives will provide a more accurate projection of structural control types, costs and construction scheduling. The updated alternatives report will include detailed design and construction schedules. Scheduling is detailed in Section 8 of this revised SIAR.

E.3 Additional Controls Likely Will be Necessary

With the completion of the WPCF expansion, the restoration of the hydraulic capacity of the Camden sewer system, and the ramping up of GSI and flood mitigation efforts, the performance of the combined sewer system will be significantly improved as shown on Table E-1.

Table E-1 – Benefits of the CSO Control Elements Before Satellite Control Facilities

System Performance Metric	Baseline Condition	With System Optimized	Optimized + 10% Reduction in DCIA
WPCF Capacity (Millions of Gallons per Day)	150	185	185
Overflow Volume (Millions of Gallons per Year)	823	582	487
% Wet Weather Capture	69%	78%	81%
Range of Overflow Event Frequencies (min – max (median))	11-70 (47)	8 -71 (45)	6 - 67 (43)
Modeled Street Flooding (Millions of Gallons per Year)	80	33	24

Key benefits of optimizing the current system include:

- A reduction in annual overflow volumes of 243 million gallons per year;
- An increase in the system-wide rate of wet weather capture and treatment from 69% to 78%; and
- Modeled street flooding volume reduced by roughly 60%.

Despite these significant gains, optimizing the current system and the best case implementation of green infrastructure still leaves the system-wide wet weather capture rate at less than 85%. Therefore, over the long term additional controls will be required.

E.4 Getting to 85% System-Wide Capture

***Note:** This section is subject to refinement based on the results of the updated structural controls alternatives analyses during the next five-year NJPDES permit cycle (2024 – 2028) as described above.*


E.4.1 Control of CCMUA’s C-32 Combined Sewer Overflow

CCMUA proposes to achieve 85% capture in the Delaware River backchannel subsystem through the reduction of wet weather flows from Pennsauken Township and increasing the wet weather flow rates through the Baldwins Run pump station. Design work for the separation of combined sewer areas of Pennsauken Township is complete and pending construction permit approval. CCMUA is currently evaluating options for the conveyance of the separated Pennsauken stormwater for discharge to Delaware River back channel through or adjacent to CCMUA’s C-32 outfall structure. This conveyance strategy may involve targeted sewer separation in Camden neighborhoods adjacent to Pennsauken or a dedicated stormwater line for the removed Pennsauken stormwater. In either case, CCMUA is studying the optimization of stormwater inlet placement and configuration to mitigate street flooding in East Camden.

E.4.2 Satellite Control Facility Capacity Requirements

For purposes of developing control strategies, the 30 active outfalls within the combined sewer system have been divided into five hydraulically isolated sub-systems as shown on Figure E-2 (following page). While all of the sub-systems are ultimately connected to CCMUA’s WPCF, providing the conveyance capacities necessary to convey the required wet weather flows to the treatment plant from the Gloucester City, Cooper River, Delaware River Back Channel and Newton Creek sub-systems would be cost prohibitive. Moreover, site limitations at WPCF preclude expanding the wet weather treatment capacity to what would be needed if these flows could be conveyed cost-effectively (details in Section 2). Therefore, additional satellite controls will be needed for certain CSO discharges to the Cooper River in Camden and to the Delaware River in Gloucester City.

The capacities of additional controls needed to achieve 85% system-wide wet weather capture in all five sub-systems are shown on Table E-2. Either remote (satellite) storage tanks or remote (satellite) treatment facilities would be required. Table E-2 includes capacity requirements with and without the accomplishment of the targeted GSI source reduction. Decisions about the size,

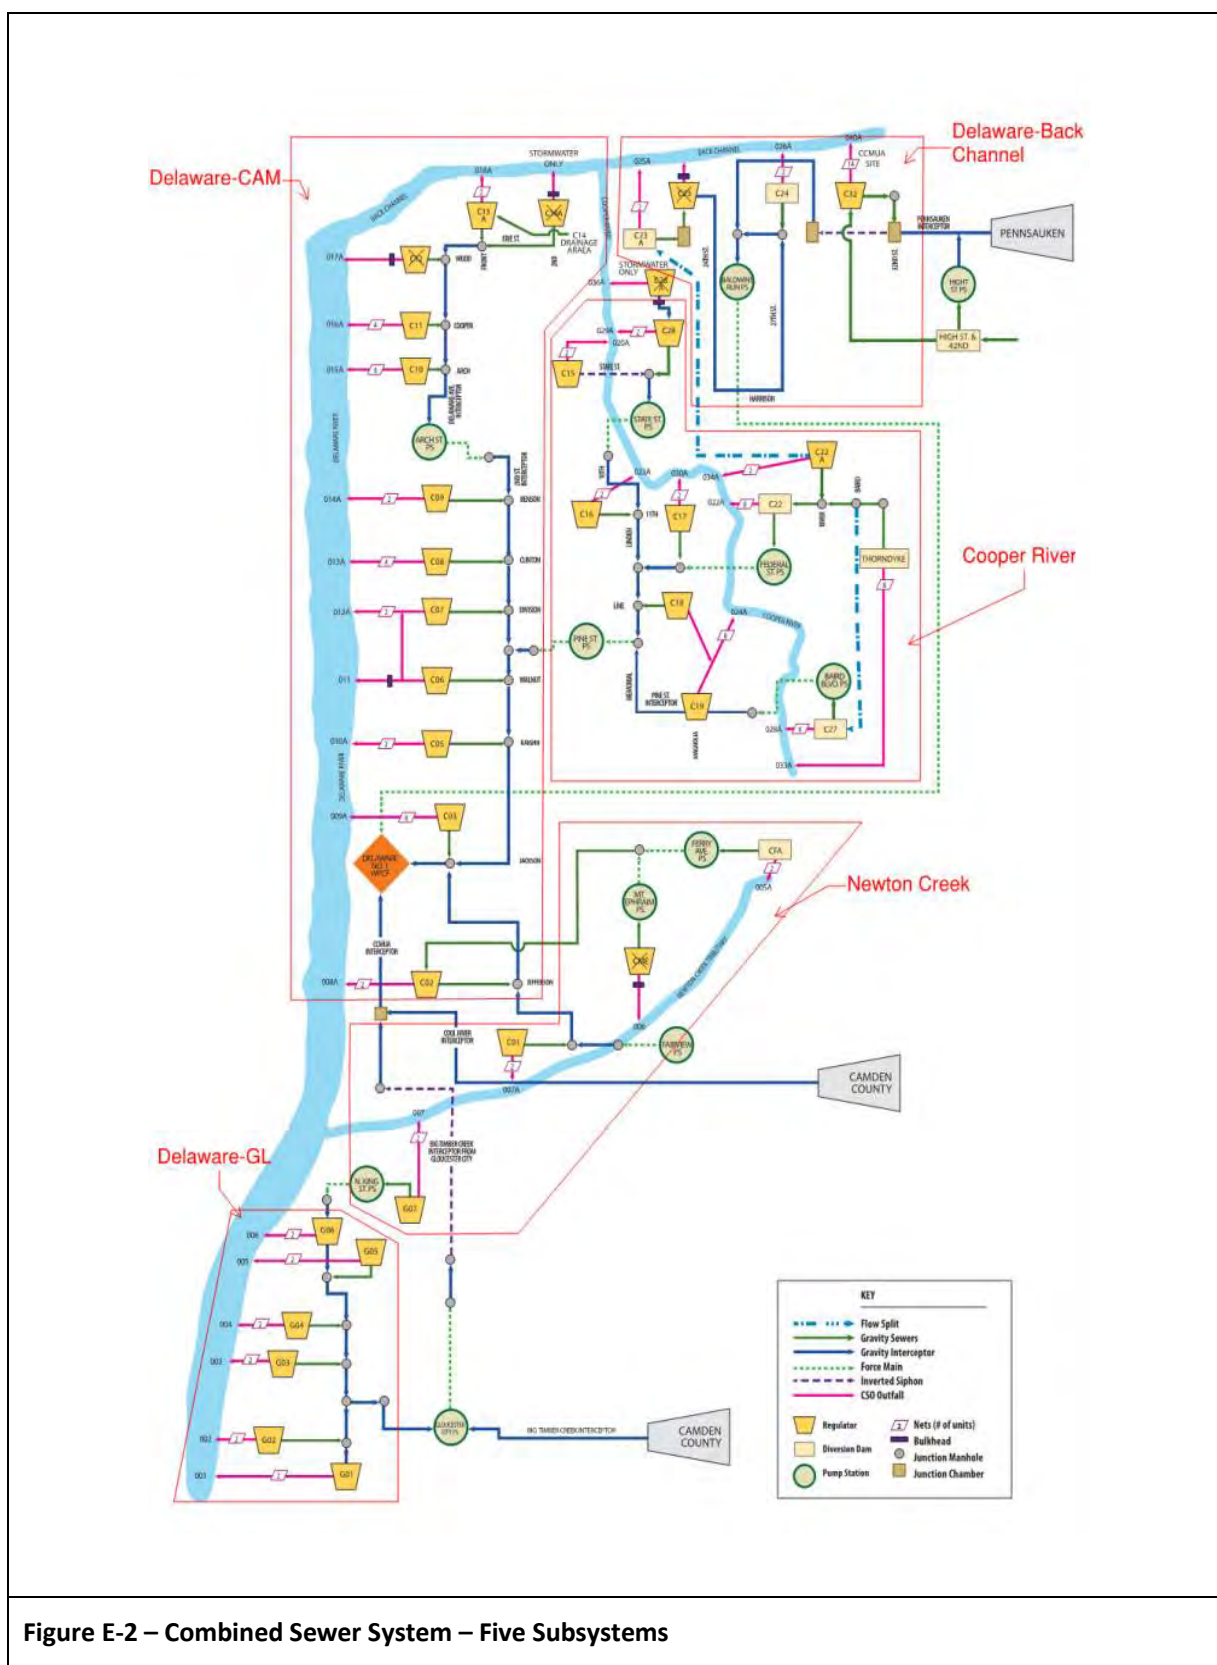

configuration and type of satellite facilities must be deferred until a long term determination as to the efficacy of GSI source reduction can be ascertained.

Table E-2 – Required Satellite Control Capacities

Sub-System	Serving Sewersheds	With a 10% DCIA Reduction		Without a 10% DCIA Reduction	
		Tanks (Million Gallons)	Treatment (Million Gallons / Day)	Tanks (Million Gallons)	Treatment (Million Gallons / Day)
Delaware River – Gloucester	G-1 and G-4 / G-5	1.1	6.4	1.9	11.2
Cooper River	C-22 / C-22A	1.3	20.0	2.6	21
	C-27 / Thorndyke	3.0	20.4	3.5	38.5
	C-17	NA	NA	0.4	4.8

Satellite facilities are not the ideal solution for CSO control since they pose significant siting, financial and operating burdens on the municipalities which they serve.

E.4.3 Overview of Satellite Control Technologies

Satellite Treatment

USEPA's CSO Policy requires that CSO treatment facilities provide the equivalent of primary clarification analogous to that provided at the WPCF and the disinfection of the treated effluent. The term Enhanced High-Rate Clarification (EHRC) is generally used to describe a physical-chemical process in which coagulants and polymers are added to wastewater to enhance the waste removal process and to reduce the treatment tank detention time, thereby reducing the required physical size of the facility. An example of this technology is shown on Figure E-3.

Satellite Storage

Off-line tank storage can be used to capture all or part of CSO discharge. When system capacity becomes available, flows are then released for conveyance to the treatment plant. When flow volumes exceed the storage capacity, flow will be discharged to CSO outfalls. A typical storage tank arrangement includes a regulator, bar screens, pumping facility and piping to and from the collection system. Design details such as flow distribution, tank flushing, and facility activation also are affected by the overall goals for and hydraulics of the specific site.

Storage tanks are generally fed by gravity and the stored flow is typically pumped back to the interceptor after the storm. This gravity-in / pump-out arrangement minimizes pumping costs (both capital and operating). However, if the existing combined sewers are deep, then the storage tank must be deep and construction becomes more expensive. An example of a typical storage tank under construction is shown on Figure E-4.



Figure E-3 – Example 25 MGD Enhance High Rate Clarification Treatment Facility



Figure E-4 – Examples of Satellite Storage Facility

E.4.4 Preliminary Site Considerations

The preliminary site requirements for the potential satellite treatment or storage facilities described above are shown on Table E-3. Approximate site vicinity and current land use maps for these potential satellite facilities are shown on Figures E-5 through E-8.

Table E-3 Potential Satellite Facilities Vicinity Information

Subsystem		Vicinity of Regulators	Approximate Area Required (acres)	Vicinity Notes
1	Delaware River – Gloucester	G1 or the CCMUA Gloucester City Pump Station	~1.5	A facility would be located either in the vicinity of the G-1 regulator or near the Gloucester City Pump Station. A new pipe would convey wet weather flows from regulators G-4 and G-5 and as needed G-1 to this facility. Current brownfield site.
2	Cooper River	C22 – C22A	~1.5	Brownfield (status unknown) private bus yard, Federal Street pump station.
		C27 - Thorndyke	~1.5	Grassed area of Gateway Park
		C17	~1.5	Only required if green control targets can't be met in the Cooper River sub-system.

Gloucester City – Satellite Facility for Wet Weather Flows from G4/G5 and G-1 Regulators

Additional controls are needed for Gloucester City’s volumetrically largest CSOs, namely regulator structures G-4 and G-5. From a technical perspective, the most effective approach would be a satellite facility capturing overflows from G-4 and G-5 in or in the vicinity of Proprietors Park as outlined in the 2019 DEAR report. While hydraulically efficient, this location is not acceptable to Gloucester City. As an alternative, wet weather flows from G-4 and G-5 that would otherwise overflow into the Delaware River could be conveyed by a new pipe to a downstream facility. This facility could be located either in the vicinity of regulator structure G-1 or a bit further upstream in the vicinity of CCMUA’s Gloucester City pump station (shown on Figure E-5).

The facility would receive wet weather flows from G-4, G-5 and G-1 and would be sized to achieve the 85% wet weather capture target for Gloucester City. During future facilities planning work that will be required to implement the LTCP, the cost-effectiveness of different options will be evaluated including the number of facilities, the preferred locations, the size and how flow is conveyed from G4/G5 to the facility.

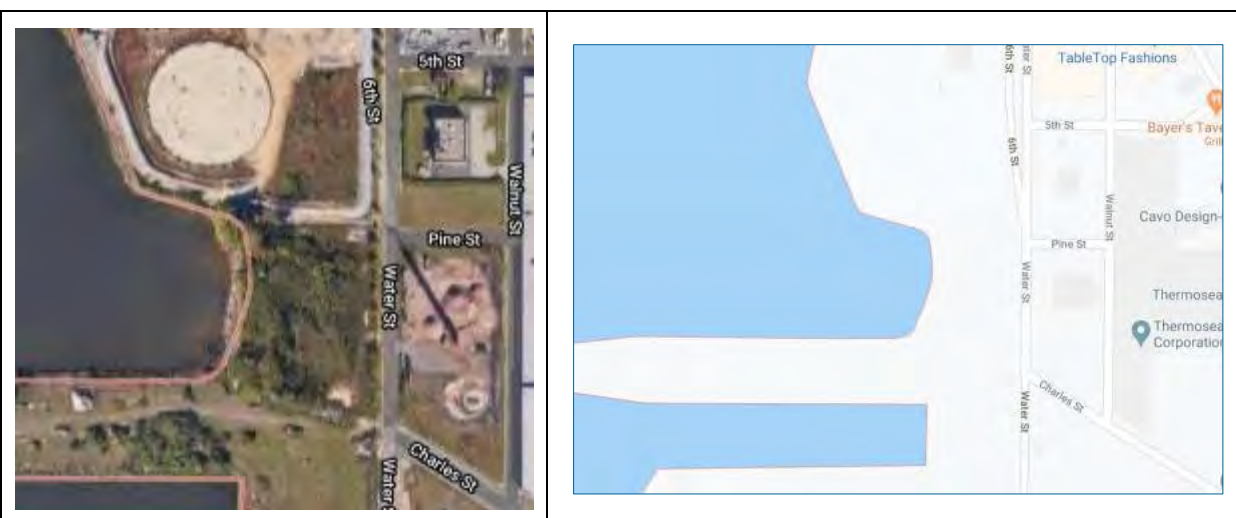


Figure E-5 – Vicinity of potential locations for a Gloucester Satellite CSO Facility and Adjacent Land Use

Cooper River – Camden C-22 /22A and C-27 / Thorndyke Regulators

These four regulators discharge to the Cooper River. C-22 and C-22A are adjacent to the Federal Street pump station and the Federal Street bridge over the Cooper River as shown on Figure E-6.

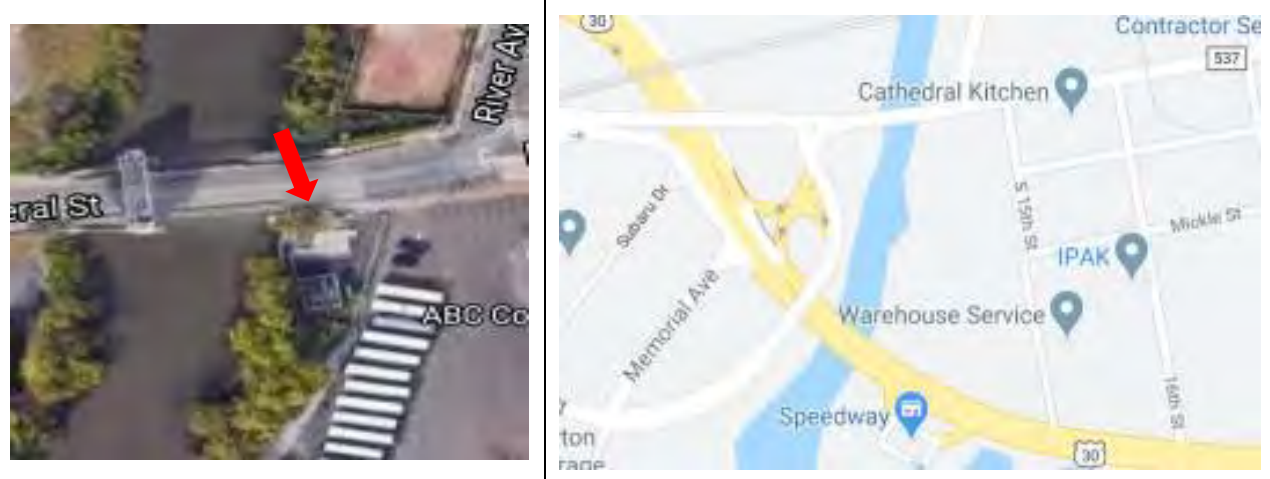


Figure E-6 – Vicinity of the Camden C-22 / C22-A Outfalls

The outfalls for C-27 and Thorndyke are the upstream most in the Camden combined sewage system that discharges to the Cooper River. The potential location for a satellite facility, adjacent to the existing Thorndyke Street netting facility is shown on Figure E-7.

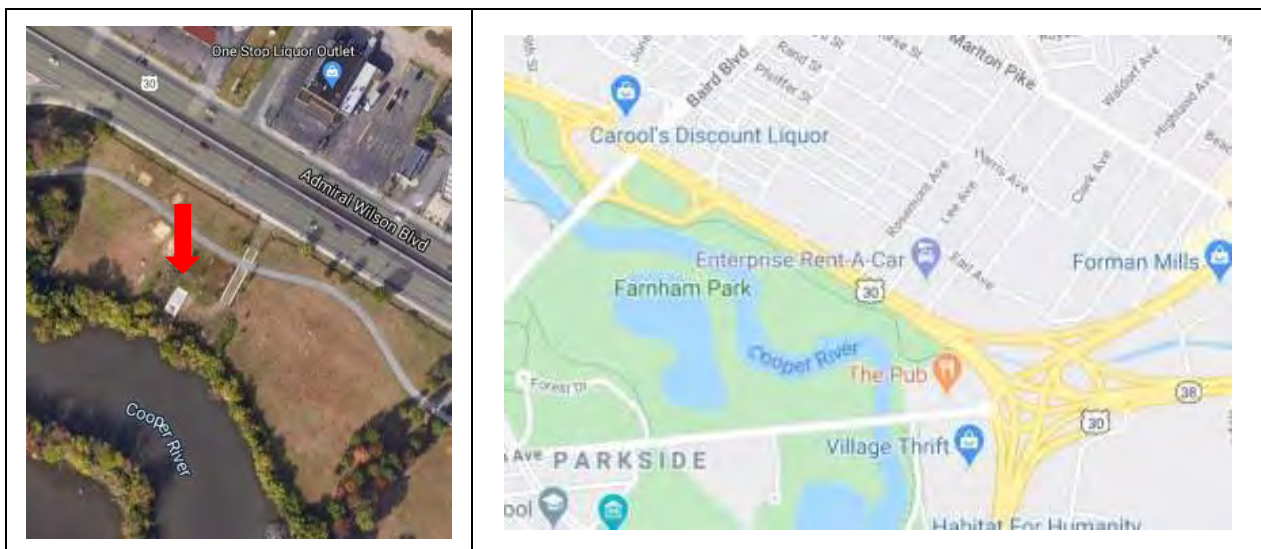


Figure E-7 – Vicinity of the Camden C-27 and Thorndyke St. Outfalls

Cooper River – Camden C-17 Regulator

If the long term goal of reducing runoff from directly connected impervious in the Cooper River sub-system is not met, an additional satellite treatment facility for the C-17 sewershed will be needed to meet the 85% control objective. The C-17 regulator structure is across the Cooper River and slightly upstream from the C-22 regulator (shown on Figure E-8). Should additional controls for C-17 prove to be necessary in the long term, the cost-effectiveness of upsizing and consolidating either the C-22 or the C-17 satellite facilities and conveying the wet weather flows across the river for treatment or storage could be evaluated.

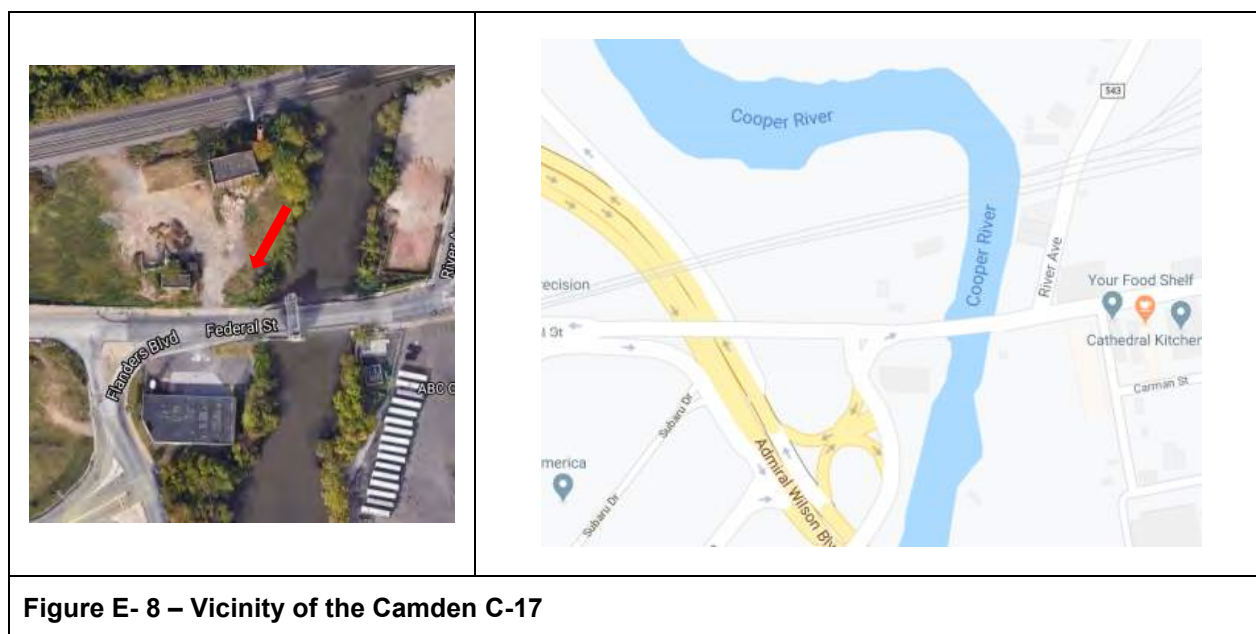


Figure E- 8 – Vicinity of the Camden C-17

E.4.5 Reduction of Inflow & Infiltration (I&I)

Part IV.F.1.h.1.ii of CCMUA's and the Cities' NJPDES permits require that I&I be identified and reduced to non-excessive levels as defined at N.J.A.C. 7:14A-1.2. It was stated in the approved June 2019 joint Development & Evaluation of Alternatives Report that I&I reduction will not play a major role in long term CSO control due to the high volumes of wet weather flow generated in the combined sewer areas relative to the volume of I/I contributed from the hydraulically connected sanitary sewer areas.

A revised baseline level of I&I in and contributing to the CCMUA / Camden / Gloucester combined sewer systems will be determined through the comprehensive flow monitoring and model update to be completed once the Camden and Gloucester sewers and outfall cleaning is completed. The results of this analysis will be integrated into the revised LTCP model and used in the revised control alternatives analysis to be completed in the 2027-2028 time frame.

E.5 Preliminary System-Wide Cost Estimates (in 2019 dollars)

The respective cost estimates for Camden, Gloucester and CCMUA are aggregated and summarized on Table E-4. Aggregated capital costs, including construction contingencies total \$208.9 million for the EHRC option and \$254.4 million for the storage option, a difference of about 22%. Combined annual incremental O&M costs are estimated to be \$2.1 million for treatment and \$1.4 million for storage.

E.6 Cost / Performance Considerations

The Cities of Camden and Gloucester and CCMUA have determined to use the Presumption Approach as the regulatory basis for their CSO control strategies and have established the control of 85% of wet weather flows generated during the Typical Year as the CSO control performance target. NJDEP requires that permittees utilizing the Presumption Approach analyze various levels of CSO controls to determine where the increment of pollution

reduction achieved in the receiving waters diminish compared to the increased costs. Such an evaluation is often referred to as a “knee of the curve” analysis.

For this analysis, CCMUA and the Cities initially evaluated the relationship between the frequencies of overflows during a Typical Year and the volumes of combined sewage discharged from the overflows. The use of an overflow-event based performance target, e.g. 4 to 6 overflows per year requires that controls be in place at every outfall that exceeds the target frequency under baseline conditions. Therefore, decisions as to where to allocate scarce resources may not be driven by the optimization of overflow reductions.


Table E-4 – System-Wide Roll Up of Cost Estimates

Permittee	Estimated CSO Control Costs*	
	Treatment	Storage
City of Camden		
Capital Costs		
Before Contingencies	\$73,654,000	\$93,597,000
With Contingencies	\$101,888,000	\$129,621,000
Annual O&M	\$1,183,000	\$753,000
Present Worth		
Present Worth of O&M	\$18,016,000	\$11,467,000
Total Present Worth (w/o Contingencies)	\$91,670,000	\$105,064,000
Gloucester City		
Capital Costs		
Before Contingencies	\$19,667,000	\$32,405,000
With Contingencies	\$27,135,000	\$44,849,000
Annual O&M	\$427,000	\$151,000
Present Worth		
Present Worth of O&M	\$6,504,000	\$2,300,000
Total Present Worth (w/o Contingencies)	\$26,171,000	\$34,706,000
CCMUA		
Capital Costs [excludes Incurred 185 MGD plant costs]		
Before Contingencies	\$57,605,600	57,605,600
With Contingencies	\$79,892,900	79,892,900
Annual O&M	\$500,000	500,000
Present Worth		
Present Worth of O&M	\$7,613,600	7,613,600
Total Present Worth (w/o Contingencies)	\$57,605,500	57,605,500
Rollup: Camden + Gloucester + CCMUA		
Capital Costs		
Before Contingencies	\$150,926,600	\$183,607,600
With Contingencies	\$208,915,900	\$254,362,900
Annual O&M	\$2,110,000	\$1,404,000
Present Worth		
Present Worth of O&M	\$32,133,600	\$21,380,600
Total Present Worth (w/o Contingencies)	\$175,446,500	\$197,375,500

* Excludes future costs for system renewal and replacement necessary to maintain design capacities.

** Excludes pipe costs for conveying wet weather flows from Gloucester G-4 / G-5 to a satellite facility near G-1 or the Gloucester City pump station.

The modeling done for this cost-performance analysis indicates that achieving 85% capture system-wide will reduce CSO volumes by roughly 485 million gallons per Typical Year. This level of CSO reduction approximates (and slightly better) that which would be accomplished with control levels resulting in about ten overflows per year at roughly one half of the capital cost. A cost-control level curve showing the CSO removal volumes at CSO frequency controls ranging from twenty overflows per year down to zero is presented in Figure E-9.

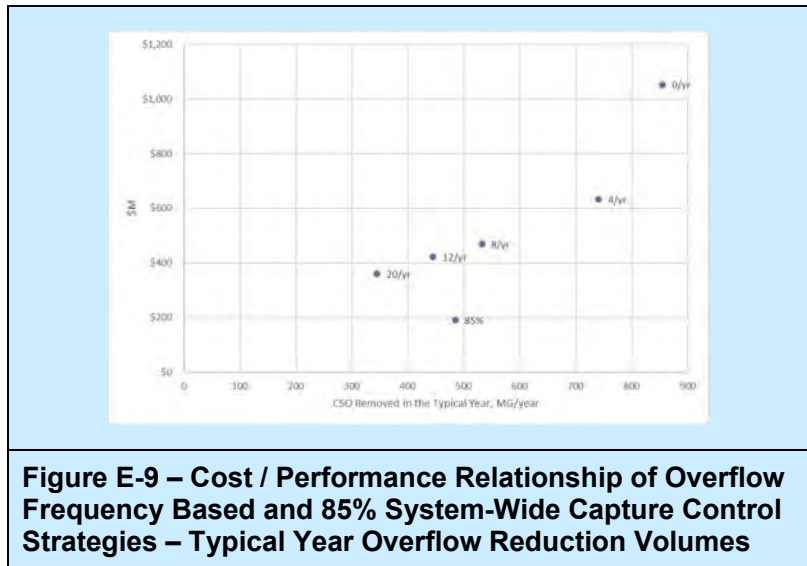

E.7 Cooper River Designated Use Reclassification

On April 6, 2020 NJDEP finalized a change the use designation of the segment of the Cooper River from the U.S. Route 30 crossing to the confluence with the Delaware River from FW-2NT (fresh-water non-trout) to Category 1 as having exceptional ecological significance due to the presence of the Eastern Pondmussel within this segment of the river.

The USEPA CSO Control Policy suggests that overflows to such areas be eliminated or relocated wherever physically possible and financially achievable. Six Camden CSO outfalls discharge into the Cooper River downstream of U.S. Route 30. These are shown on Figure E-11.

NOTE – subject to correction, it is the current understanding of CCMUA and the City of Camden that NJDEP does not anticipate requiring the elimination of the discharges from the Cooper River due to the reclassification.



Figure E-10 – Eastern Pondmussel (*Ligumia 'Nasuta'*) – photo source: Conserve Wildlife Foundation of N.J.

E.8 Affordability and Financial Capability

E.8.1 Overview

Note – The financial and institutional capability assessment presented below represents CCMUA’s, the City of Camden’s and Gloucester City’s best understanding of then current conditions and the impacts of implementing the long term control plan as presented in the September 2020 SIAR. This 2020 analysis will be rendered obsolete by the impacts of a number of subsequent developments:

- Potential changes in the use designations and related in-stream water quality standards for Zone 3 of the Delaware River that would result in new treatment plant effluent limits for nutrients (ammonia), currently under development by USEPA and the Delaware River Basin Commission (DRBC);
- The results of the updated CSO structural control alternatives analyses to be conducted during the forthcoming (2024 – 2028) NJPDES permit cycle upon the completion of system cleaning, flow monitoring, and subsequent revisions to the H&H model;
- USEPA’s issuance of revise financial capability guidance in February, 2023;
- Economic changes since 2020 including construction and borrowing cost inflation and an improved potential for federal funding assistance.

CCMUA and the Cities will update the financial and institutional capability assessments as a part of the updated alternatives analyses will occur in the 2027 – 2028 time frame.

Independent affordability and financial capability assessments were performed for Camden, Gloucester and CCMUA to identify the upper limits of what could constitute affordable future capital expenditures, including CSO controls. Lack of affordability does not excuse a permittee from complying with regulatory requirements but provides the basis for negotiating a workable implementation schedule for the LTCP.

The Financial Capability assessment is a two phased process. The residential indicator (RI) is the percentage of a permittee’s service area median household income (MHI) expended on wastewater (including stormwater) management. The upper limit of affordability for wastewater services within the Cities and CCMUA will be the point where total wastewater management costs for the typical residential user exceed 2.0% of their respective Median Household Incomes (MHI) based on the EPA metrics shown on Table E-5.

Table E-5 – EPA Residential Indicator

Residential Indicator	Cost per Household
Low Burden	Less than 1.0 percent of MHI
Mid-Range Burden	1.0-2.0 percent of MHI
High Burden	Greater than 2.0 percent of MHI

The financial capability indicator is an assessment of the permittee's debt burden, socioeconomic conditions, and financial operations. These two measures are subsequently entered into a *financial capability matrix*, suggested by EPA, to determine the level of financial burden placed on residential customers and the permittee by the existing and projected future expenditures to operate, maintain, and enhance the wastewater management system.

E.8.2 Current Costs and Residential Indicators

The estimated typical annual cost for wastewater services for a typical single family residential wastewater user account in 2019 for Camden was \$448 annually. The cost per residential account in Gloucester was \$724 and \$526 in the CCMUA service area as shown on Table E-6.

Table E - 6 – Calculated Costs per Typical Residential Wastewater User in 2019

Metric	Permittee		
	Camden	Gloucester	CCMUA
Wastewater Costs per Typical Residential User Account			
Municipal			
Service Charge	\$71.2 ^a	\$372	\$174 ^c
Collection System	\$158 ^b		
Subtotal Municipal	\$229		
CCMUA	\$219	\$352	\$352
Total	448	\$724	\$526
Median Household Income	\$26,105 ^d	\$51,152 ^d	\$69,283 ^c
Current Residential Indicator	1.7%	1.4%	0.76%

a Camden service charge of \$17.80 per quarter x 4

b Camden collection system charge of \$2.20 per 100 cubic feet of water consumption and an estimated monthly water consumption of 6.02 CCF.

c Average for the 37 CCMUA municipalities weighted by the number of Census households. Municipal costs were calculated based on total costs per household as presented in "Assessing the Affordability of Water and Sewer Utility Costs in New Jersey" by Daniel J. Van Abs (Rutgers University) and Tim Evans (NJ Future) published 2018.

d Source: US Census - American Community Survey (2013 - 2017)

E.8.3 Affordability Impacts of CSO Control Alternatives

The capital costs and resulting residential indicators to achieve 85% Typical Year wet weather capture are shown on Table E-7.

Table E-7 – Affordability Impacts of the 85% Control Program Capital Costs

Item	Permittee		
	Camden	Gloucester	CCMUA
<i>Estimated Total Capital Costs of 85% Capture Long Term Program by Permittee (in current million dollars)</i>			
Least Cost	\$101.9	\$27.1	\$79.8
Most Cost	\$129.6	\$44.8	
<i>Projected Residential Indicator After Full Implementation in 2042^a</i>			

Item	Permittee		
	Camden	Gloucester	CCMUA
	With Inflation		
Least Cost	4.8%	4.0%	0.80%
Most Cost	5.0%	4.7%	
	Without Inflation		
Least Cost	2.5%	3.0%	0.75%
Most Cost	2.6%	3.7%	

^a 2042 is used for example only. It is based on the approval of the SIAR in 2021 and implementation of the long term control program through 2041. These dates may not be appropriate for Camden and Gloucester.

Key observations about the data in these table include:

- Owing to its number of outfalls on three receiving streams, the projected least capital cost controls for Camden's CSOs are at \$102 million are roughly four times those estimated for Gloucester and 30% more than CCMUA.
- Camden's least cost controls would push the Camden residential indicator to at least 2.5% even if inflation is excluded.
- Gloucester's controls would likewise result in Gloucester's residential indicator being at least 3.0% with or without inflation.

As shown on Table E-8, there is a huge gap between the estimated costs of the selected long term control program and the economic and financial resources of the residents and municipal governments of Camden and Gloucester.

E.8.4 Potential Responses to the Affordability Conundrum

A variety of scheduling and financing options to improve on the affordability of the 85% capture program for Camden and Gloucester have been evaluated.

Scheduling Variations

The base case affordability / financial capability assessment assumes a 22 year implementation schedule based on the durations for facilities planning, design and construction shown in Table E-8.

Table E-8 – Base Case Implementation Schedule for Affordability Analysis

Start Date	2021
Facilities Planning	1
Design & Permitting	3
Construction	17
Total Years to Implement LTCP (inclusive)	21

The assumed start date is based on the submittal and approval of the SIAR in 2020 and coincides with the effective date of the next NJPDES permit. The impacts of extending the

implementation schedule on the residential indicators depend on whether or not inflation is considered as shown in Table E-9.

Table E-9 – Impacts of Implementation Scheduling on the Residential Indicators

Implementation Duration in Years	Camden Residential Indicator		Gloucester Residential Indicator	
	With Inflation	Without Inflation	With Inflation	Without Inflation
22	4.8%	2.5%	4.0%	3.0%
32	5.9%	2.2%	4.2%	2.2%
42	7.1%	2.1%	4.1%	2.1%

If as is assumed in the base-case affordability model that costs will continue to outpace income growth, affordability decreases as the implementation period is extended. If inflation is not included in the analysis, extending the implementation period does improve affordability, however even with an implementation period extending more than forty years, the residential indicators for both Camden and Gloucester are projected to remain well over the 2.0% high burden threshold.

Annual Pay-as-You-Go Funding

The amounts that each city could spend on an annual basis without causing their respective residential indicators to exceed 2.0% have also been calculated and are shown on Table E-10.

Table E-10 – Maximum Annual Expenditures Without Triggering a 2.0% Residential Indicator

Implementation Duration in Years	Camden		Gloucester Residential Indicator	
	With Inflation	Without Inflation	With Inflation	Without Inflation
22	None	~\$1.0 million	\$80,000	\$530,000
32	None		None	
42	None		None	

External Funding

As documented above, the least capital cost 85% control options would result in residential indicators of well over the 2.0% high burden threshold with or without factoring in inflation. A meaningful CSO control program is not feasible for Camden or for Gloucester without external funding that would effectively reduce the capital expenditures by the two cities. Shown on Table E-11 are the impacts of various levels of external capital funding and/or capital cost reduction on the residential indicators.

Table E-11 – External Funding and/or Capital Cost Reduction Impacts on Residential Indicators

Municipal Cost Reduction	Camden		Gloucester	
	With Inflation	Without Inflation	With Inflation	Without Inflation
0%	4.8%	2.5%	4.0%	3.0%
25%	4.4%	2.3%	3.6%	2.5%
50%	4.1%	2.1%	3.2%	2.2%

Municipal Cost Reduction	Camden		Gloucester	
	With Inflation	Without Inflation	With Inflation	Without Inflation
75%	3.7%	2.0%	2.8%	1.8%
100%	3.5%	1.9%	2.4%	1.6%

The combinations of implementation schedule and external funding or cost reductions that would result in a projected residential indicator of 2.0% or less are highlighted in green. No combinations of schedule and funding work if inflation is included.

E.9 Selected Long Term Control Program

E.9.1 Framework

Through the expansion of CCMUA's WPCF # 1 to 185 MGD, the restoration of the hydraulic capacity of Camden and Gloucester's collection system, flow reduction through green infrastructure and street flooding mitigation, the capture level is projected to reach 81% capture of combined sewage generated during wet weather. This falls short of the 85% capture target that CCMUA, Camden and Gloucester selected as the basis for LTCP compliance under the terms of their respective NJPDES permits.

Long term, additional controls will be necessary for the Cooper River, Delaware River back channel, and the Delaware River Gloucester City sub-systems to achieve 85% system-wide capture. The technical options for doing this have been refined. For purposes of long term control planning these options focus on storage through tanks or treatment and disinfection at remote (satellite) facilities. This September 2020 SIAR ~~is~~ did not make a recommendation between storage and treatment. The choice of control technologies will be determined based on the circa 2027 – 2028 updated control alternatives analyses and pending NJDEP approval, memorialized in the subsequent (2029 – 2033) NJPDES permit cycle.

Whatever the ultimate decision, **due to the extremely limited affordability and financial capabilities of the Cities of Camden and Gloucester, as demonstrated above and detailed in Section 6 of this report, these controls will require significant external funding and will likely need to be implemented over the 2034 – 2038 permit cycle or later as may be determined in coordination with NJDEP.**

E.9.2 Control Program Elements

The selected long term control program consists of six program elements that will have phased and overlapping implementation schedules (detailed in Section 8). These five elements are:

1. **Completion of Current Projects** – CCMUA has completed the capacity expansion of CCMUA's Delaware Water Pollution Control Facility # 1 to 185 MGD. Camden and Gloucester City are progressing towards the restoration of the hydraulic capacities of their respective combined collection sewer system through the comprehensive sewer and outfall cleaning. Camden has completed the rehabilitation of its 28 regulator structures and has expanded the capacity of its Arch Street Pump Station. CCMUA,

Camden and Pennsauken Township are designing and implementing the separation of combined sewer neighborhoods in Pennsauken and other improvements that will reduce street flooding in Camden’s Cramer Hill section and provide for CSO control from CCMUA’s C-32 overflow structure which discharges into the back channel of the Delaware River. A detailed list of proactive projects undertaken by CCMUA and the Cities is provided in Section 1 of this revised SIAR.

2. ***Iterative Efficacy Evaluation*** - The evaluation of the efficacy of these current improvements through comprehensive flow monitoring which will inform the refinement and recalibration of the existing hydrologic / hydraulic model to then current conditions. This will establish a new baseline of overflow statistics informed by the wet weather operating history with these capacity improvements in place. Similar evaluations may occur after other milestone projects such as the implementation of the formalized green stormwater infrastructure and the street flooding mitigation program elements. CCMUA has conducted targeted flow monitoring and model extent expansion since the initial SIAR submission in September of 2020 in support of ongoing projects.
3. ***Formalized Green Stormwater Infrastructure Program*** – Accelerating green stormwater infrastructure through a coordinated, formalized and expanded GSI Implementation Program with the goal of achieving a ten percent reduction in the directly connected impervious areas contributing stormwater runoff to the combined sewer system. GSI projects that have been completed or are under planning and design up to 2023 are described in Section 3.5 of this revised SIAR.
4. ***Street Flooding Mitigation Program*** – The development and rapid implementation of a comprehensive Street Flooding Mitigation Program will be developed within the City of Camden to provide an empirical understanding of the frequency, location and extent of street flooding remaining after the Camden sewer system is cleaned. This will serve as the basis for short and long term operational and capital improvements. Street flooding mitigation projects that have been completed or are under planning and design as of 2023 are described in Section 4.4 of this revised SIAR.
5. ***Cooper River Water Quality Optimization Program*** – The Cooper River is an important environmental, recreational and economic asset for the City of Camden’s economic redevelopment. Eliminating Camden’s CSOs from the Cooper River is not financially feasible and would not result in water quality compliance. CCMUA and the City of Camden are committing to work with the other Cooper River municipalities, stakeholders and NJDEP to develop a **Cooper River Water Quality Optimization Strategy** during the first NJPDES permit cycle after this SIAR is approved. As detailed in Section 7.6, the CCMUA has developed an initial sampling program for the summer of 2023 to evaluate sampling accessible sites and to start developing contemporary data. Results for Cooper River sampling conducted during the summer of 2023 are provided in Section 7.6.
6. ***Additional Structural Controls*** – Within the limitations imposed by affordability constraints, structural controls are needed in two of the five sub-systems that will raise the level of CSO capture in each sub-system and system-wide to no less than 85% of wet weather flows during the Typical Year.

E.10 Implementation Scheduling and Adaptive Management

The implementation scheduling strategy proposed in this SIAR was informed by the following:

- CCMUA and the Cities have already completed key projects focusing on providing significant near-term overflow and street flooding benefits such as the expansion of the WPCF # 1, upgrading the capacity of the Arch Street pump station and regulator rehabilitation by the City of Camden and substantial progress towards the cleaning of the Camden and Gloucester City collection systems and outfalls.
- Upon the completion of remedial system cleaning by the City of Camden and Gloucester City, CCMUA will undertake a comprehensive flow monitoring program and recalibration of the hydrologic / hydraulic model to establish a contemporary baseline of system performance.
- During the 2024 – 2028 NJPDES cycle, the recalibrated model will then be used for an updated evaluation of control alternatives to define the types, locations, and design standards for additional structural CSO controls needed to achieve 85% system-wide capture for the Typical Year. This evaluation will include an updated financial capability assessment and the proposed Construction and Financing Schedule for NJDEP approval and implementation in subsequent five-year permit cycles.
- The projected costs to fully implement the CSO control strategy are far greater than the financial resources currently available to the Cities of Camden and Gloucester ; and
- The complete implementation of the CSO control strategy presented in this SIAR will span multiple five-year NPDES permit cycles; and will be implemented in the midst of climate and other changes and uncertainties. Therefore, ongoing performance monitoring and adaptive management will be required to adjust the control program to match conditions.

The implementation schedule will synchronize projects, milestones and activities to coincide with the five year NJPDES permit cycles. In brief it includes:

First Five Year Permit Cycle (2024 – 2028)

1. Gloucester sewer cleaning completion by 12/31/23
2. Camden sewer cleaning completion by 10/31/24
3. Gloucester outfall cleaning completion in 2025 or early 2026 (dependent upon aquatic species protection requirements)
4. Flow monitoring of entire CCMUA, Camden Gloucester system (dependent on cleaning and weather conditions, anticipate spring and fall of 2025, or spring of 2026 as needed for adequate data)
5. Formalize Green Stormwater Infrastructure Program by 12/31/25 – implementation ongoing thereafter.
6. Formalize Street Flooding Mitigation Program by 12/31/25 – implementation ongoing thereafter.

7. Continue Cooper River water quality monitoring and develop a Cooper River Water Quality Strategy - through June 2028.
8. Update the hydrologic/hydraulic model – 2026.
9. Updated evaluation of structural control alternatives along with the proposed Construction and Financial Schedule and the updated FCA to be completed no later than June 30, 2028.

Second and Third Permit Cycles (2029 – 2033 and 2034 - 2038)

10. Planning, design, permitting, land acquisition, etc. – (NJPDES Cycle 2: 2029 – 2033)
11. Construction of additional structural controls – (NJPDES Cycle 3: 2034 – 2038)
12. Ongoing implementation of GSI and flood mitigation programs as well as periodic system performance and efficacy evaluation through flow monitoring and modeling.

It should be noted that the dates specified above are contingent on reasonable and timely regulatory approvals and other variables beyond the control of CCMUA and the Cities. Detailed design and construction schedules will be included in the updated structural control alternatives analysis.

The implementation schedule outlined above includes an evaluation at the completion of each five year NJPDES permit cycle. Based on these evaluations, CCMUA and the Cities will revise the LTCP as necessary with NJDEP's coordination and approval. This process exemplifies the concept of adaptive management.

Adaptive Management, as defined by the EPA, is “the process by which new information about the health of a watershed is incorporated into the watershed management plan.”^{E-1} In the context of the SIAR adaptive management assumes that while the CSO control goals will remain constant, the tactical approaches to achieving the goals must be adjustable.

CCMUA and the Cities will also be subject to a variety of other future conditions beyond their controls which may materially affect the benefits, feasibility and scheduling of the CSO controls described in this SIAR, thereby triggering a need to revise the LTCP. Examples of such triggering conditions include:

- External changes requiring modifications to the fundamental planning bases used in the development of the LTCP or in subsequent design due to changing demographics, municipal collection system conditions, climate change and other external changes, etc.;
- Emergent regulatory requirements specific to the receiving streams (e.g. TMDLs) or in general (e.g. the promulgation of a National SSO Policy);
- Emergent economic and other developments and trends that could materially affect the affordability and CCMUA's and the Cities' abilities to finance the CSO controls;
- Changes to water quality standards and guidance that could affect the types and levels of wet weather controls necessary to meet the program objectives;

E-1 Watershed Analysis and Management Guide for Tribes (2000) EPA Watershed Analysis and Management Project. Step 5 page 1.

- Innovative and alternative technologies that could enhance water quality and/or reduce costs thereby enabling expanded control efforts.
- The unavailability of supplies, materials, contractors or labor necessary to implement the LTCP as scheduled in the LTCP due to conditions beyond CCMUA's and the Cities control such as a natural disaster or other emergency; and
- Local, state or federal legal impediments to the timely or orderly implementation of the LTCP e.g. lengthy litigation over land acquisition or inability to obtain required permits.

CCMUA and the Cities will inform NJDEP upon becoming aware of circumstances such as those listed above as to:

- An analysis of the issues and implications posed by the condition;
- An analysis of the impacts on the implementation of the LTCP or the efficacy of the controls; and
- A proposed plan of action to address the adverse conditions that will preserve CCMUA's and the Cities' compliance with their NJPDES permits and the requirements of the CSO Control Policy.

1

SIAR Introduction

The first version of this SIAR was submitted to NJDEP on September 30, 2020. It was anticipated that the CSO control alternatives and implementation schedules contained herein would be incorporated into the 2021-2025 NJPDES permits. Due to emergent state-wide regulatory issues, the permit renewals for the 21 combined sewer system permittees in New Jersey were delayed; CCMUA and the Cities anticipate that the renewed permits will be issued later in 2023.

1.1 Regulatory Context and Report Objectives

This document constitutes Camden County Municipal Utilities Authority's (CCMUA) *Selection and Implementation of Alternatives Report* (SIAR) developed by CCMUA on behalf of CCMUA, the City of Camden and Gloucester City (the Cities) for the required "Evaluation of Alternatives" under Part IV Section G.4 of CCMUA's New Jersey Pollutant Discharge Elimination System (NJPDES) permit action (Permit number NJ0026182). The scope of this includes the Cities of Camden (Permit NJ0108812) and Gloucester (Permit NJ0108847).

The SIAR constitutes the third and final NJPDES deliverable addressing the control of wet weather overflows from their collective combined sewer systems. The *System Characterization Report* (2018) documented the physical characteristics and baseline performance of the combined sewer system. The 2019 *Development and Evaluation of Alternatives Report* (DEAR) documented the evaluation of combined sewer overflow (CSO) control alternatives that meet the water quality-based requirements of the Clean Water Act. The SIAR builds upon the DEAR and presents CCMUA's and the Cities' selected control strategy and preliminary implementation schedule. These three reports collectively comprise a complete Long Term Control Plan (LTCP) as required in the NJPDES permits.

Due to the unique and challenging circumstances facing Camden and Gloucester, it was apparent to CCMUA, the City of Camden and Gloucester City from the outset that the communities and the environment will be best served by leveraging a coordinated and collaborative approach combining regulatory compliance, sustainable redevelopment and environmental justice. Towards these ends, the program outlined in this SIAR focuses on near term community benefits through:

- Sustainable community redevelopment using green stormwater infrastructure (GSI);
- Reduce street and basement flooding of combined sewage during storms; and
- The optimization of and reinvestment in existing community assets such as the restoration of the Camden sewer system through comprehensive cleaning.

Despite the permitting delay, CCMUA and the Cities have continued to implement projects with near term benefits. These projects as of September, 2023 are shown on Table 1-1. Additional information is provided in Appendix C to this revised SIAR.

Table 1-1 – Proactive CSO Control Projects

Projects	Permittee Lead (NJPDES Responsible Party)	Project Partners	Status	Project Synopsis
Cleaning of Camden CSO outfalls	Camden	CCMUA	Estimated ~ 90% complete, projected completion 2023	<ul style="list-style-type: none"> • 2016 AW inspection report indicated 17 outfalls required dredging, 10 downstream of CSO regulators and 7 storm waters. • Camden City and CCMUA implemented two parallel cleaning and dredging projects to expedite restoring the hydraulic capacities of the affected outfalls.
Camden regulator mechanism rehabilitation	Camden	CCMUA	Completed 2022	<ul style="list-style-type: none"> • 28 regulators were rehabilitated. • C-1 to C-9 all new mechanical equipment installed. All remaining regulator equipment was removed, and chambers were cleaned and coated.
Arch Street Pump Station capacity expansion	Camden		Completed 2020	<ul style="list-style-type: none"> • 3 new 100 hp motors • 3 new 24.25" impellers (upsized) • Increased firm capacity from 7,000 GPM per pump to 11,000 GPM per pump.
Initial remedial Camden collection system cleaning	Camden		~ 76% completed (linear footage)	<ul style="list-style-type: none"> • Ongoing system cleaning to address deferred maintenance prior to 2016. • 179 miles of combined and sanitary collection sewers. • 146 miles (82%) cleaned to date. • Tons removed per mile have increased significantly in recent years, slowing linear progress.
Gloucester System Cleaning	Gloucester City	CCMUA		<ul style="list-style-type: none"> • Approximately 18 out of 39 miles of sewers have been cleaned and jetted. Gloucester City anticipates that the system-wide cleaning will be completed within 2023. • In August of 2023 CCMUA conducted an inspection of the Gloucester outfall structures and of the regulator structures, resulting in the identification of outfall structures with obstructions. These are expected to be cleaned in 2025 and into 2026 (cleaning schedule subject to aquatic species protection requirements).

Projects	Permittee Lead (NJDES Responsible Party)	Project Partners	Status	Project Synopsis
Completion of the expansion of CCMUA's WPCF # 1 to 185 MGD	CCMUA		Completed	<ul style="list-style-type: none"> • Reconfiguration of influent chamber to separate the Camden and County interceptor sewers (2020) • Upgraded influent pumps & related power supply equipment.(2021) • Optimization of existing tankage & equipment and removed hydraulic bottlenecks (2020)
Development and Implementation of Green Stormwater Infrastructure (GSI) Program Plan – target reduction of 2% (30 acres).	Camden	CCMUA / Camden Co.	Design	Port Road improvements
		CCMUA	Planning / Design	Harrison Avenue / State Street - Complete Streets Project(s)
		CCMUA, Camden SMART	2017 – 2020 Completed	Various Camden SMART GSI projects totaling 2.75 acres
			2021 - 2023	Various GSI projects totaling 6 acres .
	CCMUA	Camden	Planning / conceptual design	C-32 sewershed green stormwater infrastructure
	Gloucester City		Design / planning	<ul style="list-style-type: none"> • Conceptual design for 4 acre GSI target area completed in dense older area subject to street flooding bounded by Monmouth, Ellis, ,Mercer and King Streets. • Johnson Blvd. Park improvements to include rain gardens. • Repairs to the rain gardens at the water treatment facility have been completed.
Develop and implementation of Camden Street Flooding Mitigation Program	Camden	CCMUA	Design	Harrison Avenue street flooding mitigation project . Also see flood mitigation under C-32 project.

Projects	Permittee Lead (NJPDES Responsible Party)	Project Partners	Status	Project Synopsis
Develop the Cooper River Regional Water Quality Optimization Strategy	CCMUA		on-going	CCMUA developed Cooper River water quality sampling plan and program started May 2023.
Reduction of wet weather flow from Pennsauken into the Camden combined sewer system in sewershed C-32.	CCMUA	Pennsauken, Camden	design	C-32 Program Elements: <ul style="list-style-type: none"> • Implementation of Pennsauken Sewer Separation projects. • Conveyance of separated Pennsauken stormwater to Delaware back channel in new dedicated pipe and/or • Targeted sewer separation in East Camden to synch with Pennsauken separation. • Includes catch basin location and configuration optimization.

1.2 Overview of the Combined Sewer System

The Combined Sewer System that this SIAR addresses consists of the respective collection systems owned and operated by the Cities of Camden and Gloucester and the portion of the CCMUA's regional conveyance interceptor system that is located within the Cities of Camden and Gloucester. The Camden and Gloucester sewer systems are shown on Figure 1-1.

There are 34 sewersheds within the Camden and Gloucester combined sewer collection systems. These include twenty-seven within the City of Camden and seven in Gloucester City. Each of these sewersheds drain to a regulator structure controlling the amount of wet weather flow that enters into the CCMUA interceptors from the Camden and Gloucester trunk sewers. As of 2018, there are a total of 30 active CSO outfalls located within the two cities, with several outfalls serving more than one regulator structure. Overflows from CSO outfalls discharge into three receiving streams: the Delaware and Cooper Rivers and Newton Creek. Each active outfall has an overflow netting facility controlling the discharge of solids and floatables. Dry weather flows and captured wet weather flows are treated at CCMUA's Delaware No.1 Water Pollution Control Facility (WPCF). The general characteristics of the combined sewer system are summarized on Table 1-2.

Table 1-2– Collection System Overview

Permittee	# Sewer-sheds	Collection System Pipe in Miles ¹⁻¹	Appurtenances				Contributing Area (square miles)
			Active Regulators	Active Outfalls	Pump Stations	Overflow Netting Facilities	
Camden	27 ¹⁻²	173	24	22	8	22	6.6
Gloucester	7	39	7	7	7	7	1.6
CCMUA			<u>1</u>	<u>1</u>	<u>2</u>	<u>1</u>	
Totals	34	212	32	30	17	30	8.2

Improvements completed in 2020 by CCMUA and the City of Camden have resulted in the expansion of CCMUA's Delaware No. 1 WPCF wet weather treatment capacity from 150 (wet weather) to 185 MGD and the restoration of the hydraulic capacities of the Camden and Gloucester City sewer systems, including stormwater inlets and CSO outfalls to current design capacities through comprehensive cleaning. The restoration of the hydraulic capacities is critical to Camden's efforts to reduce street flooding which can occur during wet weather.

The results of these ongoing improvements are summarized on Table 1-3. The projected reduction in CSO volume, increased capture rates and reduction in surface flooding resulting from these early implementation steps may be noted.


Table 1-3 – System Wide Performance Characteristics Used for Control Alternatives Development

System Wide Performance Metrics		Baseline Condition	Upon Completion of Current Improvements*
		<i>Camden Hydraulic Capacity not Restored</i>	<i>Camden Hydraulic Capacity Restored</i>
WPCF # 1 Capacity		150 MGD	185 MGD
1	% Capture	66%	76%
2	Overflow Volume (million gallons)	900	618
3	Range of Overflow Frequencies (events)	10-69	10-69
4	Modeled Surface Flooding (million gallons)	94	44

*WPCF # 1 capacity at 185 MGD + Camden collection system hydraulic capacity restoration

¹⁻¹ Source: Table 2-2 from the Sewer System Inventory and Assessment / Facilities Inventory and Assessment Analysis Final Report prepared by CH2MHill, November 1999-69

¹⁻² Includes Camden sewersheds flowing to the C-32 regulator for which CCMUA is the permittee.

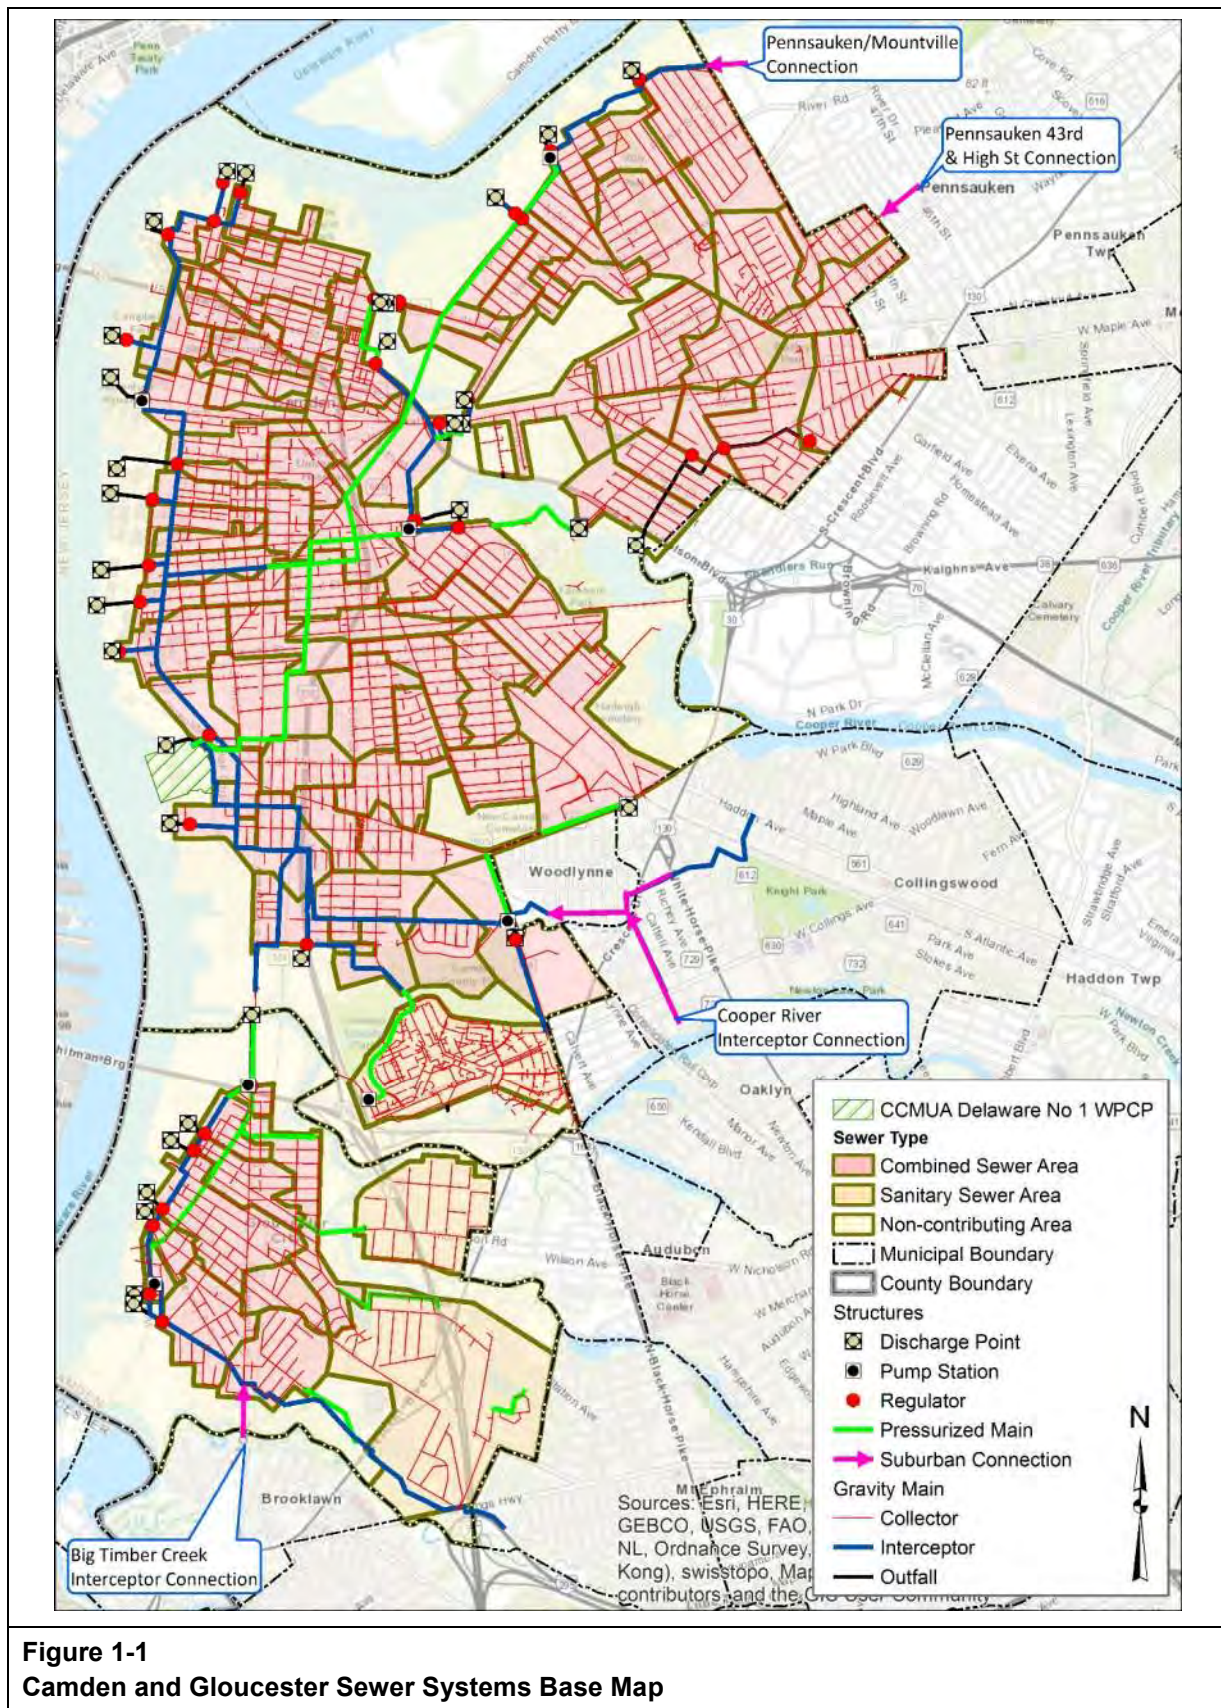

1.3 Previous Studies

This report builds upon the information provided in the previous studies required under the Cities' and the CCMUA's respective NJPDES permits as well as other studies and documents prepared for the Cities and for CCMUA. These are listed in Table 1-3 1-4.

Table 1-4 – Previous Studies

Title		NJDEP Approval Date
1	System Characterization Report (SCR)	Jan. 2019
2	Baseline Compliance Monitoring Report	Feb. 2019
3	Baseline Consideration of Sensitive Areas	Jan. 2019
4	Development & Evaluation of Alternatives Report (DEAR)	Nov. 2019

1.4 Overview of Control Alternatives in the DEAR

This Selection and Implementation of Alternatives Report (SIAR) builds upon and incorporates the findings of the 2019 DEAR that:

- The control performance target will be system-wide 85% capture of wet weather combined sewer flow during the typical year;
- All control strategies assume that the hydraulic capacity of the Camden collection system will be restored through the ongoing cleaning of the pipes and the CSO outfalls and that regularly scheduled cleaning will occur to maintain the restored hydraulic capacity;
- All control alternatives will incorporate a target controlling runoff from no less than 10% of the directly connected impervious area within the combined sewer system through green stormwater infrastructure;
- CCMUA's WPCF No. 1 wet weather treatment capacity can be expanded further from the soon to be completed 185 MGD capacity of up to 220 MGD;
- Achieving a 10% reduction in directly connected impervious areas along with the expansion of wet weather treatment capacity up to 185 MGD is projected to bring the system-wide capture rate to 81%. Further expansion to 220 MGD would bring the capture rate to 82%; just short of the 85% target. Moreover, the capture rates in three out of the five sub-systems (Delaware River - Gloucester City, Cooper River and Delaware River-Back Channel) will be well below the 85% capture target without additional controls. The five sub-systems are shown schematically on Figure 1-2.
- Therefore, satellite facilities to raise wet weather capture rates to no less than 85% using storage tanks or enhanced high rate clarification treatment facilities were evaluated.



1.5 Organization of Report

Table 1-5 provides the locations of the elements referenced under the NJPDES permit within this SIAR. This SIAR combined with the SCR and the DEAR together comprise a complete long term control plan (LTCP) the requirements for which are set forth in Part IV Section G of the NJPDES permits. To verify that all of the Section G requirements have been addressed in the LTCP, references to all relevant Section G requirements are provided.

Table 1–5 – Location of NJPDES Referenced Elements of the LTCP

Permit Section	Permit Requirement	Section Location
Part IV G.1.a	“The permittee, as per D.3.a and G.10, shall submit an updated characterization study that will result in a comprehensive characterization of the CSS developed through records review, monitoring, modeling and other means as appropriate to establish the existing baseline conditions, evaluate the efficacy of the CSO technology based controls, and determine the baseline conditions upon which the LTCP will be based. The permittee shall work in coordination with the combined sewer communities for appropriate Characterization, Monitoring and Modeling of the Sewer System.”	Entire SCR
Part IV G.1.b	“The characterization shall include a thorough review of the entire collection system that conveys flows to the treatment works including areas of sewage overflows, including to basements, streets and other public and private areas, to adequately address the response of the CSS to various precipitation events”	SCR Section 2
Part IV G.1.b	“The characterization shall identify the number, location, frequency and characteristics of CSOs”	SCR Section 7
Part IV G.1.b	“The characterization shall identify water quality impacts that result from CSOs”	SCR Section 4
Part IV G.1.d.i	Rainfall Records Analysis	SCR Section 6
Part IV G.1.d.iii	CSO Monitoring	SCR Section 5
Part IV G.1.d.iv	System Hydrologic & Hydraulic Modeling	SCR Sections 3 & 5

Permit Section	Permit Requirement	Section Location
Part IV G.1.d.ii	Combined Sewer System Characterization	SCR - all
G.4.b	<ul style="list-style-type: none"> • Ensure CSO controls will meet water quality requirements of the CWA; • Protect existing and designated uses; • Prioritize sensitive areas 	SIAR Section 7.0
G.4.c	The permittee shall select either the Demonstration or Presumption Approach for each group of hydraulically connected CSOs and identify each CSO group and its individual discharge location.	DEAR 3.0
G.4.d	The Evaluation of Alternatives Report shall include a list of control alternative(s) evaluated for each CSO.	DEAR 5.3
G.4.e	<p>The permittee shall evaluate a range of CSO control alternatives:</p> <ul style="list-style-type: none"> i. Green infrastructure ii. Increased storage capacity iii. STP expansion, CSO related bypassing and/or storage iv. I/I reduction v. Sewer separation vi. Treatment of the CSO discharge vii. CSO related bypass 	DEAR 4.4
G.4.f	The Presumption Approach – documentation of conformance with one of the three criteria.	DEAR 5.4
G.4.g	The Demonstration Approach – Documentation of conformance with all of the four criteria.	Not Applicable
G.5.a	Cost-Performance Considerations – Conduct “Knee of the Curve” analysis for a range of overflow event control levels.	SIAR 5.0

1.6 Stakeholder Involvement in the SIAR Development

1.6.1 Introduction

The City of Camden and Camden County Municipal Utilities Authority (CCMUA) actively and consistently work together to engage, inform and educate the public on the following key issues:

1. Combined Sewage Flooding;
2. Combined Sewage Overflows; and
3. The development of a long term control plan.

Actively engaging with the community predates the start of the Long Term Control Plan (LTCP) process. The Camden SMART (Stormwater Management and Resource Training) Initiative, a voluntary collaboration among the City of Camden, CCMUA, Cooper’s Ferry Partnership, Rutgers Cooperative Extension Water Resources Program, New Jersey Tree

Foundation and the NJ Department of Environmental Protection, was formed in 2011 to protect human health, improve conditions for economic development, improve water quality and enhance the quality of life for the residents of Camden City through the use of green and grey infrastructure. The Camden SMART Initiative also has a robust public outreach component.

The creation of the Camden SMART Initiative began an era of public outreach and education on the combined sewage flooding and overflow issue that continues to grow and thrive. The goals of the Camden City and CCMUA public outreach and education program are as follows:

1. **Inform** – bring awareness to the public health threat of combined sewage flooding, water quality issues associated with combined sewage overflows, and the LTCP process.
2. **Educate** – delivering basic knowledge on why combined sewage flooding and overflows occur and the steps entities like Camden City and the CCMUA can take to correct these problems.

Camden City and the CCMUA meet the goals of informing and educating in the following ways:

1. Passive, General Public Outreach – websites, flyers, posters;
2. Targeted, General Public Outreach – providing flyers, posters, pamphlets and other educational materials at public events like environmental fairs and through bill inserts;
3. Educational/Workforce Programs – The PowerCorps and Green Ambassador Programs
4. Demonstration Projects – Implementation of Green Infrastructure sites throughout Camden City;
5. Mitigation Projects – The Camden City Rain Barrel Installation Program and water conservation kits; and
6. Forums and Summits – events which gather together stakeholders and interested parties to discuss combined sewage flooding and overflow issues.

The need for engagement, outreach and education varies greatly across the service areas of Camden City and CCMUA and is dictated by the type of sewer system which services the geographic location of a customer's home or business.

Nearly all the residents and business owners of Camden City make up the affected public due to the public health concerns associated with combined sewage flooding. It is important to not only inform the Camden City public that combined sewage flooding exists (so they can avoid if possible) but to educate them on ways (green infrastructure, rain barrels, water conservation) to minimize inputs to the system to minimize the volume during flooding events.

Except for Gloucester City, the rest of the CCMUA customers are from 35 suburban municipalities that have separated sewer systems. The CCMUA has concentrated its LTCP public outreach efforts on informing the public of the combined sewage system issues in Camden and Gloucester Cities. The CCMUA has also worked with local officials from the suburban municipalities to educate them on infiltration and inflow (I&I) issues.

The desired outcome of the Camden City and CCMUA public outreach and education effort is to bring attention to the public health hazard of combined sewage flooding and the detrimental effects of combined sewage overflows on the quality of the receiving water body until the responsible entities can eliminate combined flooding in its entirety and effectively control overflows.

1.6.2 Completed Outreach Activities

A description of outreach activities that have been completed prior to and during the development of this SIAR is provided below. The materials referenced are provided in the Appendix to this document and are labeled as appendix item A-1, etc.

1) *Camden SMART and Green Infrastructure Sites*

Camden SMART (Stormwater Management And Resource Training) Initiative was founded in 2011 by a coalition of six entities - Cooper's Ferry Partnership (CFP), the City of Camden (City), Camden County Municipal Utilities Authority (CCMUA), Rutgers Cooperative Extension Water Resources Program (RCE), New Jersey Tree Foundation (NJTF), and the NJ Department of Environmental Protection (NJDEP)- the Camden SMART Initiative is a community-driven movement to protect human health, improve conditions for economic development, improve water quality, and enhance the quality of life for Camden City, its residents, and the Delaware River watershed through the broad use of green and grey infrastructure techniques for stormwater management.

Because of Camden's aging and overtaxed combined sewer system, a one-inch rainstorm can leave major roads impassable, turn parking lots into stagnant lakes, and send sewage into parks, homes, and waterways. Not only is this a nuisance, it is a public health crisis that degrades the quality of life of Camden's residents and negatively impacts the City's economic viability and environmental quality. The objective of the Camden SMART is to develop a comprehensive network of green infrastructure programs and projects to solve the combined sewer problem in the City of Camden.

The "Camden SMART Green Infrastructure Sites" (A-1) lists the projects which manage stormwater in Camden City. These sites have signs developed by Rutgers Water Resources Staff that explain the stormwater features to the public. The sites provide a visual reminder of the need to manage storm water in this combined sewer overflow community. The selection and design of these sites involve engaging the community throughout the process. Meetings and site visits are conducted throughout the process. Site 63 is currently in the design phase with The Trust for Public Land whose process involves extensive public outreach. Construction will begin this year on Sites 62, 64, 65 and 66.

2) *PowerCorps Camden*

PowerCorps Camden is an AmeriCorps direct service program focused on improving Green Infrastructure in the City of Camden. In partnership with Camden County Municipal Utilities Authority (CCMUA) and the City of Camden under the National Governor and Mayor's Initiative, Center for Family Services launched the program in December 2015, with the goals

to improve outcomes for opportunity youth and improve green infrastructure in Camden City.

Over the last five years, PowerCorps Camden has aimed to increase economic opportunity through job training and readiness for up to 60 youth each year. Since inception, 171 Camden City residents have served and over 730 acres of land have been treated by PowerCorps members in Camden. Through projects focused on Camden's green infrastructure network, PowerCorps members play a key role in maintaining green infrastructure installations including rain gardens, city and county parks, vacant lots, and stormwater inlets that comprise Camden City's network. The members are all familiar with the issues of combined sewer systems and help to maintain the sites listed in the appendix "Camden SMART Green Infrastructure Sites". Through knowledge and skills training, some which is provided by Camden SMART and Camden Collaborative Initiative partners, PowerCorps Camden develops and nurtures young adults into environmental stewards and strong candidates for the workforce. In addition, at the beginning of each cohort, our Camden SMART partners from Rutgers University provide a day of education to teach each member about the combined sewer issues that Camden faces and the benefits of green infrastructure.

The service projects PowerCorps Camden members take part in are often in collaboration with CCMUA, the Camden SMART partners and many of the Camden Collaborative Initiative partners. In addition to general green infrastructure maintenance, members take part in environmental trainings, group service learning trips and in varied innovative projects, including repurposing concrete/rubble from construction sites to create barriers that protect existing rain gardens within the city. These collaborations allow for members to expand their environmental knowledge while also having a real and lasting impact on the City.

3) *Green Infrastructure Maintenance Activities*

Periodically, environmental stewardship events are held in the city so that all stakeholders including local citizens, local workers, non-profits, and governmental entities can be educated about, and actively participate in, the green infrastructure projects addressing combined sewer flooding and overflows. Since May of 2015, over 600 people have actively participated in such events.

On 5/04/2018 and 5/11/2018 the CCMUA and the Center for Family Services organized an event for 20 Subaru staff that work in Camden City. The staff maintained and planted at five Camden SMART rain gardens. On both days the combined sewer flooding issues were discussed. Rutgers staff and Rutgers Environmental Stewards, New Jersey Tree Foundation, Camden PowerCorps, Coopers Ferry Partnership, New Jersey Conservation Foundation and CCMUA staff all helped at the rain gardens.

On 4/16/2018 the New Jersey Tree Foundation and Coopers Ferry Partnership organized 50 people who planted 20 trees at Gateway Park. Urban Promise students, Camden PowerCorps, Coopers Ferry Partnership, New Jersey Conservation Foundation, Delaware Riverkeeper and CCMUA staff all helped with the planting which was attended by Camden's Mayor Frank Moran.

On 4/11/2018 the Authority staff organized a renovation of the Camden SMART rain garden at the Urban Promise School, 3700 Rudderow Street. The students in the school's environmental program worked with the Camden PowerCorps and installed a new rubble border to protect the rain garden. The CSO flooding issues in the City were discussed with the group. Rutgers Environmental Stewards assisted with the project which involved 35 people.

On 10/12/2017 Camden Public School, Brimm Medical Arts hosted "Imagine a Day Without Water" (A-2). Camden SMART presented to 90 students and faculty. The presentation is attached. It included; Combined sewer system & Green infrastructure, Camden SMART, Camden Reports, Impact of development on local water sources, Water pledge and rain barrel painting, Rain garden re-fresh.

On 9/20/2017, our Authority hosted Camden City's Aramark Building Communities Day. 45 Aramark employees worked at three sites to maintain Camden SMART rain gardens and associated green infrastructure. Rutgers, New Jersey Tree Foundation, New Jersey Conservation Foundation, Coopers Ferry Partnership and CCMUA staff all helped by instructing the volunteers and describing the CSO issues these features work to mitigate.

On 9/17/2017 Jeremiah Bergstrom, LLA, ASLA, Senior Research Project Manager, Rutgers Cooperative Extension Water Resources Program, Rutgers, The State University of New Jersey conducted a site visit for 30 Rutgers Environment Stewards.

On 8/20/17 Camden SMART staff worked with 30 New Jersey American Water employees to maintain the 29th Street Rain Gardens. The gardens were weeded, cleaned up and new plants were added.

On 6/07/2017 Camden SMART held the Camden Environmental Summit and 250 people attended this day-long event held at Rowan University. Panel discussions were held on the following topics: Voices of Camden's Aspiring Green Leaders, Don't Waste Our Open Space, Resilient and Healthy Futures for New Jersey's Environmental Justice Communities, Building Healthy Environments for Food Access and were followed by a CCMUA Facilities Tour. The CCMUA Executive Director, Andrew Kricun, lead 50 people on a tour of the Regional Sewer Treatment plant. The summit was organized by the members of Camden SMART.

On 4/28/2017 the New Jersey Tree Foundation held an Arbor Day celebration. At the Camden Day Nursery volunteers planted street 10 trees. The Arbor Day event was attended by Rutgers University, New Jersey Tree Foundation, New Jersey Department of Environmental Protection, Camden City, Coopers Ferry Partnership and CCMUA staff.

On 9/15/2015, 16 volunteers from Stantec along with the New Jersey Tree Foundation, Rutgers Water Resources, Coopers Ferry Partners, Camden County Soil Conservation District and CCMUA staff planted the Union field rain garden.

On 5/13/2015, 21 Home Depot volunteers along with the New Jersey Tree Foundation, Rutgers Water Resources, Coopers Ferry Partners and CCMUA staff maintained the

Waterfront South Rain Gardens. The gardens were weeded, mulch and plants were added to the rain gardens.

4) *Camden Rain Barrel Installation Program*

This program, modeled after a successful Philadelphia Water Department Program, began in late June 2017. Community Rain Barrel Meetings are set up throughout Camden City. City residents who attend a one-hour meeting are then eligible to have a free rain barrel installed at their home. The one-hour meeting describes how the rain barrel functions and the problem with combined sewer systems. This educational program is presented by the Pennsylvania Horticulture Society. PHS staff make the arrangements with a contractor to install the rain barrels at the homes in Camden City. Camden SMART Partners are responsible for the promotion of the program and make the arrangements for the meetings. Flyers are printed and distributed by the Camden PowerCorps and by the host organization. The “List of CSO Supplemental Information Distributed” (A-3) has the date and number of flyers distributed for each rain barrel meeting. 16 rain barrel meetings have been held in most of the city’s neighborhoods. Online or phone registration is accepted for the meeting. 190 people have attended the meetings and 110 rain barrels have been installed since the program began.

In conjunction with the Camden PowerCorps, an informational video promoting rain barrel use and their purpose in a community with a combined sewer system. The video was posted online and an additional 30 city residents participated in the installation program. The link to the video can be found in the “List of CSO Supplemental Information Distributed”.

5) *Customer Mailings*

CCMUA has 160,000 customers that are charged every three months for sewer service. Our customers are the properties in Camden County that are connected to the sewer system. The “List of CSO Supplemental Information Distributed” has the date and number of educational flyers distributed to our customers by mail.

6) *Brochures at Public Events*

The CCMUA has several brochures available in the lobby of our administration building designed to inform our rate payers of various stormwater-related issues that affect the county. The Appendix includes a sample of each of these brochures: 7 SMART Steps (A-4a) to reduce neighborhood flooding and improve stormwater management; How to Prevent Stormwater Pollution (A-4b); Camden SMART Initiative; Camden County Conserves - Saving Water, Saving Money (A-4c); Toilets Are Not Trashcans(A-4d). These valuable sources of information are also given out at the various summits, festivals, school and community events, county fairs and public education events that the Authority participates in. At each of these events, a representative of the CCMUA staffs a table to engage with the public, answering questions and providing information about the Authority and its initiatives. These information table events attract and educate hundreds of families each year and include:

- The Camden Environmental Summit – 6/14/17
- Camden Jam: Arts and Music Festival – 9/9/17

- Camden River Days – 9/23/17
- The VietLead Harvest Moon Festival – 10/7/17
- National Community Development Week: Cramer Hill – 4/3/18
- National Community Development Week: Fairview – 4/5/18
- St. Anthony’s of Padua School Art Show – 4/19/18
- The Camden Environmental Summit – 6/6/18
- The Camden Environmental Summit – 11/21/19

In addition to Camden City, brochures and information on the broader wastewater system of the County is made available at various annual county events such as:

- Collingswood May Fair
- Mt. Ephraim Night Out
- Blackwood Pumpkin Festival
- Camden County Fair
- Collingwood Green Festival
- International Day
- Gloucester Township Day

7) *Media Outreach*

The LTCP team has conducted extensive outreach through conventional media and the CCMUA web site. Media coverage of the team’s actions in reducing combined sewer overflows and activities in promoting public awareness of CSO problems and solutions has been extensive and is listed in “Media Mentions” (A-5). Each press mention was posted on the CCMUA web site. The reported news fell into one or more of the following categories:

- Water conservation efforts, including green infrastructure and rain barrel programs
- Impact of combined sewer overflows on environmental justice communities
- Reduction of combined sewer overflows as a best management practice for wastewater utilities
- Benefits of public investment in infrastructure
- Public and organizational recognition of CCMUA/Camden SMART/Camden Collaborative Initiative efforts
- Contribution of green space and parks to stormwater management
- Impact of climate change on water infrastructure planning
- Wastewater treatment as a resource (e.g., for energy generation and process cooling)
- Publicization of innovative financing for infrastructure and other techniques to support stormwater reduction

8) *CCMUA Website Information*

The CCMUA Web site (<http://www.ccmua.org>) provides a central resource for relevant information available to the general public, including:

- Home page
 - Brief description of Camden County’s regional sewer system and the impact of being connected to combined municipal sewer systems

- News Archive page
 - Links to each of the news items described above and listed in the Appendix
- Green Initiatives page
 - Link to Camden SMART web site (<http://www.CamdenSMART.com>)
 - Rain Gardens and other green infrastructure projects
 - Climate change information
 - Water Conservation
 - Energy Self-Sufficiency
 - Environmental Management System
 - Camden Collaborative Initiative
 - Living shorelines
- Education page offers informational material on
 - Opportunities for tours
 - Wastewater treatment plants processes
 - Keeping harmful materials out of the system
 - Wastewater industry best practices
 - Strengthening water and wastewater infrastructure
 - Pollution in waterways
 - Other material prepared by partners, distributed as inserts with CCMUA's quarterly bills, including:
 - River and watershed information
 - Stormwater and steps to reduce flooding
 - Water conservation
- Contact information for Authority officials and staff

9) *Green Ambassadors Summer Internship Program*

In 2014 the Green Ambassadors Summer Internship Program began with 10 Camden City high school students. The purpose of the program is to create a group of local young people who can serve as ambassadors of the environment to the people of Camden. The interns participate in hands-on work experience and classroom-style environmental education that introduces them to environmental issues, solutions, and careers. By participating in this program students work to transform the city into a greener, cleaner, safer community while experiencing meaningful employment and environmental education.

The program maintains a special focus on the environmental issues that impact Camden specifically, chief among which is the problems of combined sewer flooding and overflows. Each summer the interns tour our facility and green infrastructure sites and are educated about the causes and effects of the combined sewer issues in the city. To date, 80 youth have completed the program and have gone back to their neighborhoods to spread the word about Camden's environmental issues, as well as the steps being taken to address them. A description of the Green Ambassadors program can be found in the appendix (A-6).

1.6.3 CSO Supplemental Team

Camden City and the CCMUA used the *Forming and Utilizing Your Supplemental CSO Team* guidance document (A-7) and worked with the NJDEP via email correspondence (A-8) in creating the CSO Supplemental Team (CSOST). The result of those efforts is a CSO

Supplemental Team made up of more than 20 individuals representing more than 15 entities and was considered to be representative of the area and its needs (see Appendix A-9 for a complete listing of invitees). Camden City and the CCMUA understand that there is a likelihood there are other interested parties whom they are not aware of but that should be part of the CSOST. To compensate for this likelihood, all CSOST invitees were asked, and have been continued to be encouraged, to identify and invite people and/or entities they feel should be involved in the LTCP process.

All individuals that were identified as potential CSOST members were sent a letter via email on or around April 7, 2018 (see sample in Appendix A-10) which explained the LTCP, the public participation component of the LTCP and asked them if would join the CSOST. It also conveyed the stated purpose of the CSOST as follows: Through the CSO Supplemental Team, the City and the CCMUA will gain a public perspective on CSOs, local water quality issues and sewer system problems including flooding.

The first convening of the CSOST took place on May 25, 2017. The goal of the meeting was to bring together the team and give an overview of combined sewer systems and the LTCP. The PowerPoint used in that meeting is provided (A-11).

The second convening of the CSOST took place on December 13, 2017. The goal of the meeting was to gain feedback from the team regarding Sensitive Areas in the combined sewer system area, especially primary contact recreation waters. Representatives from the CCMUA, the City of Camden, and the DEP met with community members and local organizations to discuss and determine which sections of the waters affected by CSO overflows require special consideration because of the possibility of direct or indirect contact through recreational activities. A list of the attendees and the organizations they represented can be found in appendix A-12.

A presentation was given by the Executive Director of the CCMUA to explain the combined sewer issue as a whole, the goals of the Long Term Control Plan, and the importance of identifying Sensitive Areas. Slides from the presentation (appendix A-13). Subsequent discussions with the attending members of the CSO Supplemental Team revealed which areas of the Cooper River, Newton Creek and Delaware River back channels are frequently canoed upon. A map of these locations can be found in appendix A-14. The magnitude of the recreational activities was estimated through the Urban Promise Ministries' Urban Trekkers Program representatives; In a given year, over 500 participants canoed these waters through the Urban Trekkers program.

The third Supplemental Team Meeting was held on July 17th, 2018 to examine the findings of the System Characterization Report. The then-current condition of the combined sewer systems of Camden and Gloucester City was discussed as the basis for future green and grey strategies for reducing the volume of overflows into the waterways of the community.

The fourth Supplemental Team meeting took place on June 18th, 2019, the invitee list can be found in appendix A-15. The various partners, stakeholders and community leaders discussed the elements of the DEAR including the CSO control goals for each receiving water segment the types of control alternatives identified as potential solutions to meet the LTCP requirements.

The fifth Supplemental Team meeting was held on January 16th, 2020, the sign in sheet for the meeting can be found in appendix A-16. This meeting focused on the effects of increasing the treatment plant capacity would have on the CSO control goals, and projected effects of 10% DCIA disconnection. The effects on specific sewershed subsystems were discussed, focusing on the probable need for new capital projects at C32 and the C27/Thorndyke Outfalls. The group discussed the various options at each location that would be required, and how each would impact the community in which they were placed. The presentation given to the group at this meeting can be found in appendix A-17.

1.6.4 Additional Municipal Coordination

During the development and finalization of this SIAR, CCMUA held the following coordination meetings (virtual after January) with the City of Camden and Gloucester City:

- Meeting with Camden and Gloucester engineers, attorneys and public works officials (January 29, 2020)
- Distributed draft SIAR to the City of Camden and Gloucester City
- Discussion of draft SIAR with Cities' administrative and technical officials (June 1 and June 8)
- Presentation of the SIAR to the Mayors and executive teams of the Cities (Week of August 9th)
- Presentation of the SIAR to the Cities' Councils (Weeks of August 30th and September 7th).

2

Maximizing Flows to WPCF # 1

2.1 CCMUA's Water Pollution Control Facility # 1

CCMUA treats approximately 53 million gallons of sewage per day at its wastewater treatment plant, which is referred to as the Delaware No. 1 Water Pollution Control Facility (WPCF), or simply "the plant." The plant was expanded in the 1980s to a secondary treatment facility with a capacity of 150 MGD. The WPCF operates under NJPDES Permit No. NJ 0026182, with primary year-round permit limits shown below in Table 2-1. The average influent CBOD and TSS concentrations are approximately 187 and 208 mg/L respectively, which is representative of a medium strength wastewater.


Table 2-1 – Delaware WPCF #1 Effluent Limits

Parameter	Monthly Average	Weekly Average
Flow Through Treatment Plant	Monitor & Report	
Total Suspended Solids	30 mg/l	45 mg/l
	85% removal	
Carbonaceous Biochemical Oxygen Demand	25 mg/l	40 mg/l
	85% removal	
Ammonia	35 mg/l	
Fecal Coliform	200 geometric mean #/100 mL	400 geometric mean #/100 mL

The four (4) raw sewage pumps together can provide a firm capacity (largest pump out of service) of 150 mgd, which is the maximum wet weather capacity at the plant. The treatment plant processes train³⁻¹ include preliminary treatment, primary sedimentation, aeration, final sedimentation, and disinfection. The process train flow is diagramed on Figure 2-1.

In 2017 CCMUA completed a study of alternatives for the upgrading of its WPCF #1. The study recommended a two phase program for the treatment plant. Under phase 1 the plant would be expanded to provide 185 MGD in full secondary treatment capacity. This expansion was completed in 2020. The study also determined that it is feasible to further increase wet weather treatment capacity up to 220 MGD using CSO related bypassing. The potential increase in wet weather treatment capacity up to 220 MGD would provide the equivalent of primary treatment and effluent disinfection prior to discharge into the Delaware River in accordance with CCMUA's NJPDES permit. A schematic process train schematic is shown in Figure 2-1.

³⁻¹ Excerpted from: Wet Weather Upgrades at the Delaware No. 1 WPCF – Concept Study of Alternatives Draft May 2017 prepared by Greeley & Hansen for CCMUA.

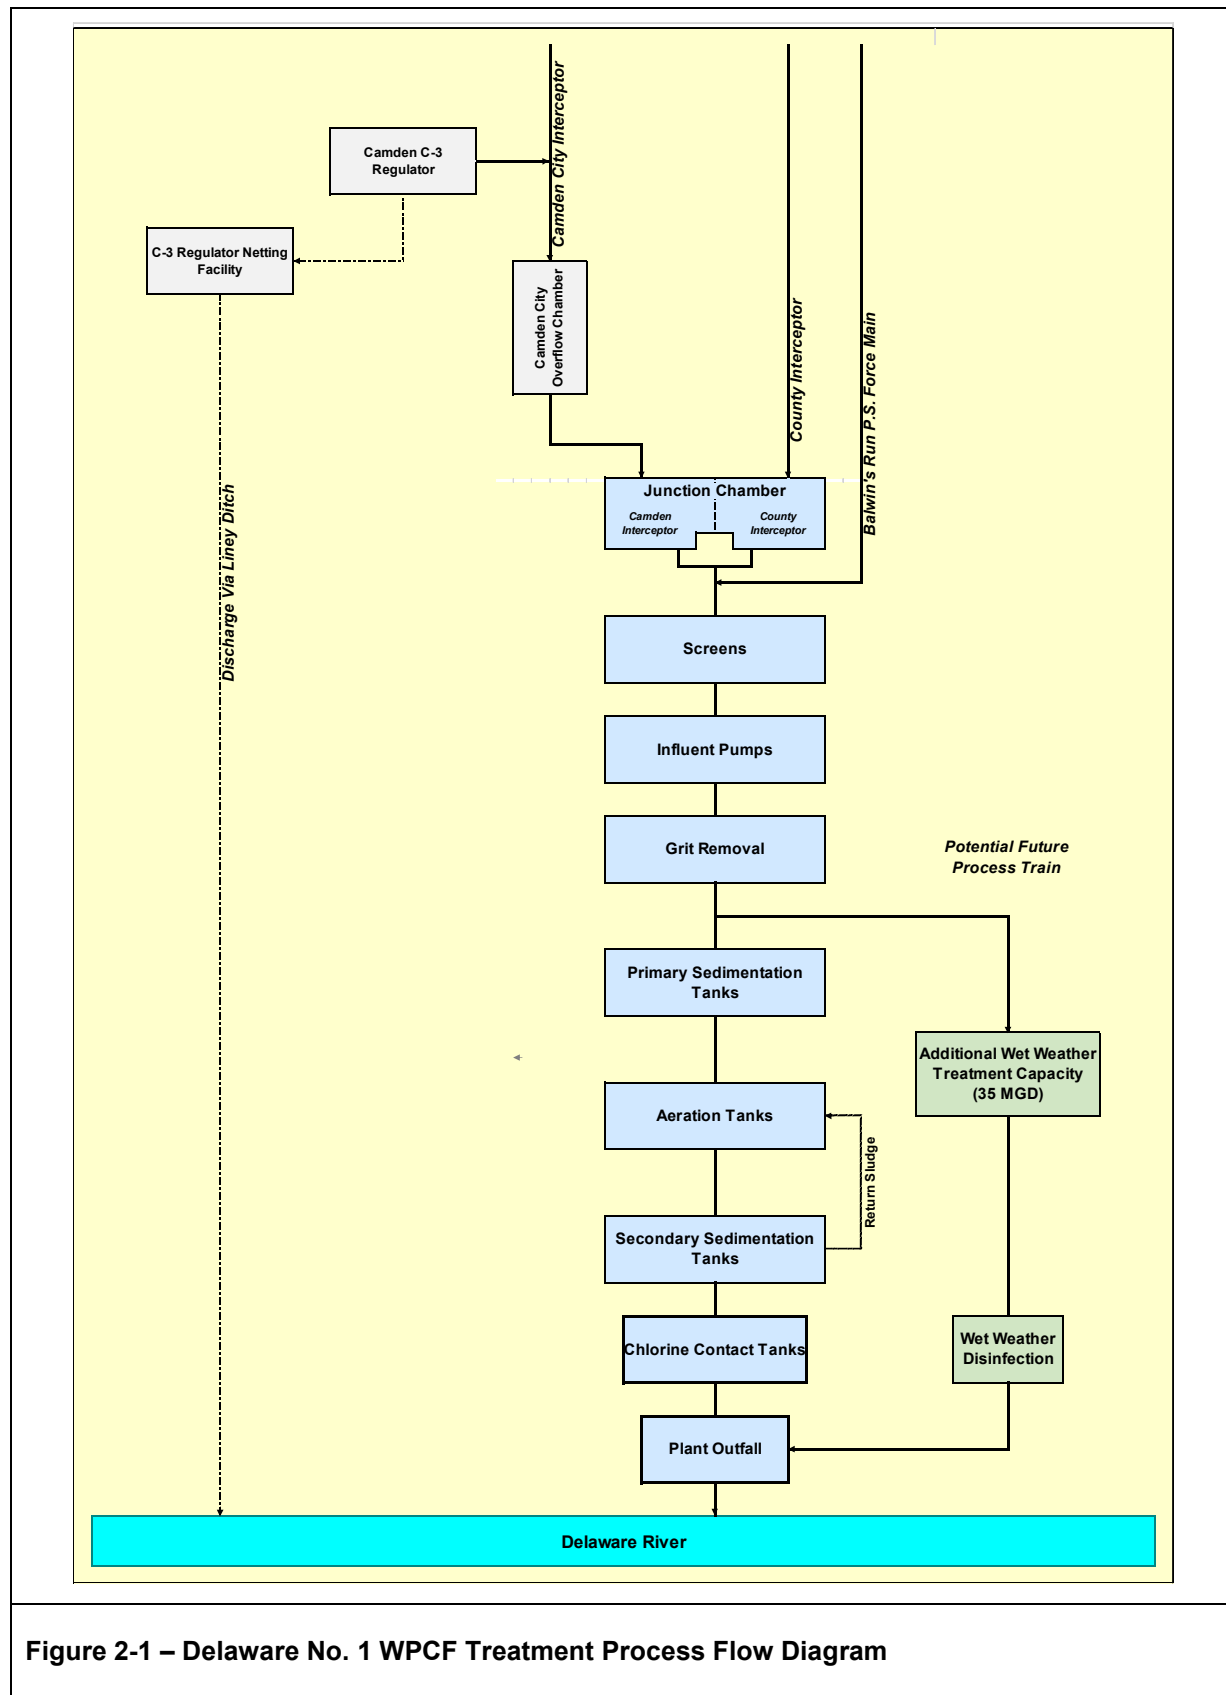

2.2 Regulatory Context

The regulatory basis for CCMUA's potential expansion of wet weather treatment capacity through a CSO related bypass of the secondary treatment process train is based on the 1994 CSO Control Policy:

"In some communities, POTW treatment plants may have primary treatment capacity in excess of their secondary treatment capacity. One effective strategy to abate pollution resulting from CSOs is to maximize the delivery of flows during wet weather to the POTW treatment plant for treatment. Delivering these flows can have two significant benefits: first, increasing flows during wet weather to the POTW treatment plant may enable the permittee to eliminate or minimize overflows to sensitive areas; second this would maximize the use of available POTW facilities for wet weather flows and would ensure that combined sewer flows receive at least primary treatment prior to discharge."²⁻²

The utilization of primary treatment capacities at treatment plants that exceed secondary treatment capacities is one of the options that combined sewer system permittees are required to evaluate under their respective NJPDES permits.³⁻³ CCMUA's NJPDES permit was modified in July of 2019 to reflect the expansion of full secondary treatment capacity to 185 MGD. In it, NJDEP notes an expectation that CCMUA will consider CSO related bypassing options at WPCF # 1 in the SAIR.²⁻⁴ The expansion of wet weather treatment capacity to up to 220 MGD using a CSO related bypass is one potential component of the CSO control strategy. It was determined to be not necessary or cost effective to meet the 85% system-wide typical year capture target however in the 2020 SIAR. If warranted, this option could be re-examined during the updating of the structural controls analysis anticipated in the 2027-2028 timeframe.

2.3 Wet Weather Capacity Expansion Beyond 220 MGD

It has been determined that additional controls beyond the expansion of WPCF # 1 of up to 220 MGD plus flow reduction through the use of green stormwater infrastructure will not achieve the system-wide control target of 85% wet weather capture during the typical year. To increase the targeted capture rate to 85%, additional controls will be needed for the Gloucester City CSO discharges on the Delaware River, the City of Camden discharges to the Cooper River and to the City of Camden and CCMUA discharges to the backchannel of the Delaware River.

CCMUA has determined that a wet weather treatment facility at or in the vicinity of WPCF #1 is not feasible due to site constraints. Land is not available at WPCF # 1 as evidenced by the already tight configuration of facilities at WPCF # 1 shown on Figure 2-2 on the following page. Moreover, the acquisition of additional land in the vicinity of WPCF # 1 is not realistic. The plant is bounded by the Delaware River, an active railroad, a recently completed

²⁻² 59 FR 18693

²⁻³ Part IV-G.4-e(vii)

²⁻⁴ "Overview of Wet Weather Upgrades of Delaware WPCF # 1" included in the July 18, 2019 Final Surface Water Minor Modification Permit Action for Delaware WPCF #1 NJPDES number NJ0026182.

brownfield to public park, expanding shipping and cargo businesses and a residential neighborhood. Therefore, it is not feasible to provide wet weather treatment beyond 220 MGD at or in the vicinity of WPCF #1.

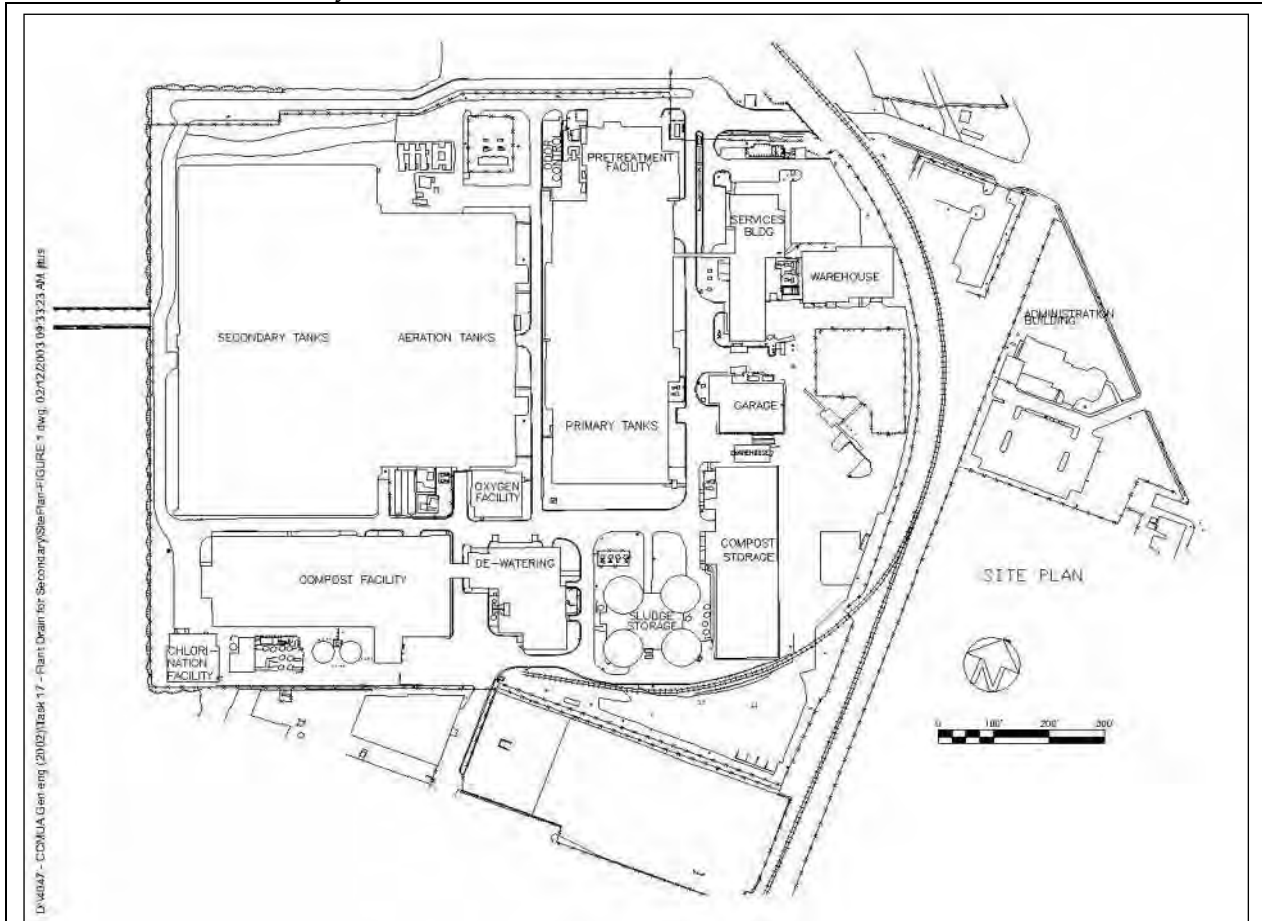


Figure 2-2 – Plan View of CCMUA Delaware Water Pollution Control Facility #1

Source [Wet Weather Operating Manual for CCMUA Delaware No. 1 WPCF 2003 WRc/D&B, LLC](#).

2.4 Impacts of Capacity Expansions to 185 MGD on Wet Weather Capture

2.4.1 CCMUA Water Pollution Control Facility # 1

As noted above, CCMUA completed the expansion of full secondary treatment capacity at its WPCF # 1 to 185 MGD in 2020. The wet weather capture benefits of the plant expansion are shown on Tables 2-2 through 2-4 through the increase in total plant influent flow:

- Table 2-2 – *Overall Comparison of Flow Rates* shows average total daily and peak daily flow rates from January 2016 through April 2020, and from May 1, 2020 through August 30, 2023. It also shows the peak flow rates for these periods.

- Table 2-3 – *Frequency Distribution of Days With Peak Flows* in 25 MGD increments from 100 MGD to 250 MGD.
- Table 2-4 – *Peak Daily Flow Rate by Month* shows the peak daily flow rate for each month from 2016 through August 2023.

Table 2-2 – Overall Comparison of Flow Rates

Time Period	Average		Peak Flow Rate (MGD)
	Total Daily Flow (MGD)	Peak Daily Flow Rate (MGD)	
Jan 2016 - April 2020	54.9	75.7	157.4
Plant Expansion (May 2020 forward)	51.8	84.6	237.8

Table 2-3 – Frequency Distribution of Days With Peak Flows

Days With Peak Rates (MGD) Between:	100	126	151	176	201	226	Number of Days
	125	150	175	200	225	250	
Prior to Plant Capacity Expansion	171	39	13	0	0	0	223
	77%	17%	6%	0%	0%	0%	
	77%	94%	100%	100%	100%	100%	
Plant Expansion (May 2020 forward)	212	79	45	23	5	1	365
	58%	22%	12%	6%	1%	0%	
	58%	80%	92%	98%	100%	100%	

Table 2-4 – Peak Daily Flow Rate by Month

Month	2016	2017	2018	2019	2020	2021	2022	2023	Average 2016- 2019	2022	% Change (2016 - 2019 .v. 2022)
January	112.2	120.6	109.6	141.1	124.7	166.3	186.3	123.5	120.9	186.3	54%
February	139.8	122.7	154.7	131.1		181.5	177.7	180.3	137.1	177.7	30%
March	146.1	136.1	140.0	140.0		173.6	130.0	166.9	140.6	130.0	-8%
April	113.3	141.0	152.8	134.7	125.4	187.1	177.6	178.2	135.5	177.6	31%
May	145.7	131.4	90.7	155.3	158.2	138.0	237.8	127.1	130.8	237.8	82%
June	115.1	105.6	140.9	157.4		200.1	177.9	179.2	129.8	177.9	37%
July	144.1	130.7	101.3	136.6	176.0	175.3	176.1	160.2	128.2	176.1	37%
August	101.5	127.6	123.9	132.0	174.9	140.1	120.3	168.9	121.3	120.3	-1%
September	110.1	101.4	130.3	104.2	183.0	179.8	174.7		111.5	174.7	57%
October	125.0	151.0	123.0	131.7	176.0	214.0	203.4		132.7	203.4	53%
November	136.8	103.7	156.4	57.2	181.2	156.6	107.5		113.5	107.5	-5%
December	151.8	120.0	154.1	127.9	181.7	126.6	201.8		138.5	201.8	46%
Average	128.5	124.3	131.5	129.1	164.6	169.9	172.6	160.5	128.3	172.6	34%
Maximum	151.8	151.0	156.4	157.4	183.0	214.0	237.8	180.3	140.6	237.8	

Plant Expansion (May 2020 forward)

2.4.2 City of Camden Arch Street Pump Station

The City of Camden's Arch Street pump station conveys flows from Camden sewersheds C-10 through C-13A via the Camden Interceptor. The City completed upgrades to the Arch Street pump station in 2020 which included increasing the motor horse-power on the three pumps from 75 to 100 each and increasing the size of the pump impellers from 22.25" to 24.25". Prior to the expansion of CCMUA's treatment capacity Camden needed to throttle back the pumping rates at Arch Street during significant storm events to protect the interceptor downstream and the treatment plant. With the expanded treatment plant capacity of 185 MGD and increased pumping capacity at Arch Street, the frequency of the need to temporarily shut down Arch Street pump station has been greatly reduced since 2020 as shown on Table 2-5.

Table 2-5 – Frequency Arch Street Pump Station Shut-Downs During Wet Weather

Year	Rainfall	Arch St. Shut-Downs	C10 CSO Events
2018	69.12	22	112
2019	54.02	28	73
2020	46.60	14	59
2021	43.04	3	54
2022	43.70	2	71
2023 (through July)	19.21	0	29

https://cdmsmithonline.sharepoint.com/sites/255047CSOAnnualConsultingCCMUARegulatorySupport/Shared Documents/General/CSO Program & NJPDES Permits/LTCP/LTCP 2023/2023 LTCF Revisions/Texts in WORD/CIAR 2.0-WWTP_09-19-23 redline.docx

3

Formalized Green Stormwater Infrastructure Program

3.1 GSI Implementation Target

Green stormwater infrastructure is a foundational component of CCCMUA's and the Cities' control strategy due to the many environmental, community, aesthetic, economic and community health benefits intrinsic in green stormwater infrastructure (GSI).

CCMUA and the Cities of Camden and Gloucester are targeting a 10% reduction in impervious areas that are directly connected to the combined sewer system (DCIA) through the installation of GSI. Directly connected impervious areas such as paved streets, parking lots, building roofs, etc. from which stormwater runoff flows into the combined sewer system through a catch basin or other appurtenance.

The 10% target equates to approximately 145 controlled acres as shown in Table 3-1.

Table 3-1 – Calculation of Target Control of Runoff from DCIA

Combined Sewer Area	Acreage
Total	4,499
Directly Connected Impervious Area	1,446
Less 10% Reduction in DCIA	-145
Remaining Uncontrolled DCIA	1,302

The 10% directly connected impervious area reduction target reflects the upper limit of feasible GSI implementation during a twenty to forty-year implementation timeframe typical of CSO control programs. Over a longer timeframe, redevelopment and the renewal and replacement of the currently uncontrolled impervious areas represented by current buildings, roads, etc. will occur and the impervious area would be expected to decline as building and zoning codes and practices integrate GSI.

3.2 Wet Weather Control Benefits of GSI

Reducing stormwater runoff to the combined sewer system from directly connected impervious areas in Camden and Gloucester will have significant CSO control and street flooding reduction benefits. A ten percent decrease in stormwater runoff from impervious areas throughout the combined sewer area would result in a system-wide wet weather capture rate during the Typical Year of 81% coupled with the expansion of WPCF # 1 to 185 MGD and the restoration of the hydraulic capacity of the Camden and Gloucester collection system. This is a 5% improvement compared to 76% for the Control Alternatives Baseline conditions. Volumetrically, removing 10% (145 acres) of the system-wide DCIA would reduce the flow to the combined sewer system by approximately 90 million gallons during the Typical Year .

3.3 GSI Implementation Strategy

By its nature, the ability to implement and the responsibility for the implementation of green stormwater infrastructure is diffuse. The directly connected impervious areas to be addressed using GSI are owned and controlled by all levels of government and private entities ranging from interstate highways and commercial redevelopment to church parking lots. CCMUA and the Cities have limited control over the location, timing and scale of green stormwater projects on private properties or on properties owned by county, state or federal agencies.

Given these institutional constraints, CCMUA and the Cities are proposing the establishment of a framework for the implementation of GSI that would formalize, expand upon and support the current efforts of groups such as the Camden SMART initiative. The intent is to maximize the implementation of GSI whenever feasible in coordination with:

- Development and redevelopment projects;
- Transportation and related public works (e.g. road work);
- Renewal and replacement projects (collection system or other work requiring street openings); and
- Opportunities for neighborhood enhancements (e.g. new or improved neighborhood parks or playgrounds).

CCMUA and the Cities will work with the current neighborhood and economic development groups, neighborhood groups, civic and economic leaders and county and state officials to develop the technical and institutional framework for implementing an aggressive and sustainable GSI program that will be an integral part of the implementation of the LTCP and other public and private projects and programs. The initial deliverable of these efforts will be a GSI Implementation Framework document that will include:

- A) Specify technical criteria for identifying potential areas for DCIA reduction:
- B) Determination of the potential for DCIA reduction:
 - 1) Identify technical feasibility criteria, e.g.
 - (a) Contributing area runoff characteristics
 - (b) Accessible work sites
 - (c) Etc.
- C) Methodology for identifying and supporting project stakeholders
- D) Institutional Opportunities and Impediments
 - 1) Municipal code issues & opportunities (e.g. GSI requirements for redevelopment over a threshold size);
 - 2) Existing institutional support structures & organizations; and
 - 3) County, state and federal regulatory issues or opportunities.
- E) Institutional and financial responsibilities for the ongoing maintenance of green stormwater management facilities

- F) Funding mechanisms
 - 1) Current
 - (a) State and federal programs
 - (b) Private sources
 - 2) Potential
 - (a) Stormwater fees
 - (b) Other
- G) Iterative planning, implementation, evaluation processes;
 - 1) Coordinate with municipal
 - (a) Planning and redevelopment plans
 - (b) Public Works capital improvement program cycles
 - 2) Coordinate with NJDOT

The framework would be targeted for completion during 2025, with work to commence upon NJDEP approval of this SIAR. The framework will include specific performance targets for GSI implementation e.g., 30 acres per five year NJPDES permit cycles. An evaluation of GSI implementation and flow reduction efficacy will occur at the end of each permit cycle to inform decisions as to the need for program modifications and to set priorities during the subsequent five year permit cycle. A preliminary outline of the framework is provided on the following pages.

3.4 Draft GSI Implementation Program Framework

I) Framework Details:

- A) Inventory of Potential DCIA Runoff Capture Locations – categorized by:
 - 1) Consolidated Geographic Information System (GIS) data base of areas meeting the technical definition of DCIAs.
 - (a) Using municipal / county block & lot parcel mapping
 - (b) Evaluation / estimation of DCIA area by parcels to an appropriate level of detail necessary for an informed planning level understanding of the DCIA.
 - 2) Land Use
 - (a) Current
 - (i) Actual
 - (ii) Zoned
 - (b) Future Land Use
 - (i) Announced redevelopment;
 - (ii) Land use & redevelopment plans.

- 3) Land Ownership & Control
 - (a) Public Land and Rights of Way (ROW)
 - (i) Municipal
 - Streets, roads, mass transit;
 - Parks, etc.;
 - Building & facilities;
 - Parking lots
 - (ii) Schools & universities
 - (iii) State & Federal
 - Buildings, facilities & structures;
 - Roads, bridges, mass transit, etc.
 - (b) Private lands
 - (i) Private businesses by zoned usage
 - (ii) Non-profits – e.g.
 - Churches
 - Hospitals, clinics;
 - Etc.
- 4) Categorization of the above data by sewershed.
- B) Technical Evaluation Criteria – How will target projects be identified and evaluated in terms of:
 - 1) Spatial Scale
 - (a) By parcel
 - (b) Sewershed
 - (c) Neighborhood
 - (d) Etc.
 - 2) DCIA Runoff Capture Potential
 - (a) Contributing area
 - (b) Site availability & conditions
 - (i) Accessibility
 - (ii) Conflicts & obstructions (e.g. utility lines)
 - (iii) Captured flow discharge opportunities
 - (c) Site appropriate controls
 - (i) Neighborhood fit

- (ii) Cost
 - (iii) O&M effort and responsibilities
- C) Institutional Evaluation – impediments and opportunities relating to GSI under the current legal and institutional framework – e.g.:¹
 - 1) Zoning – in terms of siting GSI facilities
 - 2) Municipal & County codes – e.g. plumbing, building, stormwater management.
 - (a) Encourage GSI
 - (b) Discourage GSI
 - (c) Mandate GSI upon redevelopment or repairs?
 - 3) Road design standards
 - 4) Tax codes
 - 5) Liabilities
- D) Implementation Roles and Responsibilities [who's doing what]
 - 1) Actors
 - (a) Municipalities
 - (i) Current and potential roles & responsibilities
 - (ii) Level of interest
 - (iii) Resource needs (staffing, technical expertise, etc.)
 - (b) County / CCMUA
 - (c) State
 - (d) Current property owners
 - (e) Non-Profit / Civic Organizations and Stakeholders
 - 2) Activities:
 - (a) Project sponsors / champions
 - (i) Identifying potential projects
 - (ii) Identifying project owners
 - (iii) Rallying support
 - (b) Financial support
 - (c) Technical / legal reviews & permitting
 - (d) Technical support
 - (i) Design standards

¹ All of these have been dealt with in Philadelphia and elsewhere but a local assessment is warranted and may have been undertaken already by / for Camden.

(ii) O&M BMPs

(iii) “Hands on” technical support

E) Requirements and Incentives

- 1) Should GSI be mandatory and under what circumstances? e.g.:
 - (a) Redevelopment supported by public funding
 - (i) Direct funding
 - (ii) Indirect funding (government improvement of off-site infrastructure)
 - (b) Upon redevelopment or significant alternation?
 - (c) How to balance the desire for GSI with need for re-investment and the implicit unequal negotiating positions therein?
- 2) Responsibilities for ongoing maintenance of GSI facilities
 - (a) Institutional responsibilities
 - (b) Financial responsibilities
- 3) Funding incentives and resources:
 - (a) Current state or federal programs
 - (b) Tax incentives?
 - (c) Stormwater Utility / Fee
 - (i) As revenue source
 - (ii) As incentive – through fee avoidance by reducing impervious area.

F) Estimating the likely public / private mix of GSI

- 1) Based on other cities’ experiences
- 2) Over various timeframes

III) Action Plan for Cycle 1 (NPDES permit cycle 2021 – 2025)

A) Stakeholder involvement and engagement

- 1) Stakeholder identification
- 2) Strategy for developing stakeholder support, buy-in and ownership?

B) (Strategy for) Identifying Project Priorities

- 1) CSO control potential
- 2) Feasibility / resources
- 3) Community interest
- 4) Etc.

C) Project Identification and Operation

- 1) Identifying and Committing Project Owners & Operators

- (a) Ownership qualifications & responsibilities
 - (b) Operator qualifications & responsibilities
- 2) Implementation Support Structures
 - (a) Planning & design technical supports
 - (b) Construction delivery and management supports
 - (c) O&M supports – including potentials for DBE, training programs, etc.
- 3) Project Operation & Maintenance
 - (a) Standards of operation & maintenance
 - (b) Performance monitoring
- D) Schedule and Performance Metrics
 - 1) Target implementation schedule
 - 2) Program evaluation metrics:
 - (a) DCIA acres removed per unit of time
 - (b) Estimated flow reduction
 - (c) Anecdotal information – e.g. flooding events.

3.5 GSI Activities Since September 2020 SIAR Submittal

Green stormwater infrastructure and other wet weather source reduction projects that have been undertaken proactively by CCMUA, Camden and Gloucester City are summarized on Table 3-1. A total of 28.75 acres of drainage area are or will be controlled by GSI projects completed since 2017 or which are currently under planning / design. 2017 is used as the base year since it was base-year for the current conditions documented in the 2018 System Characterization Report.

Table 3-2 – GSI and Source Reduction Project Undertaken Since 2017

Projects	Permittee Lead (NJPDES Responsible Party)	Project Partners	Status	Project Synopsis
Development and Implementation of Green Stormwater Infrastructure (GSI) Program Plan – target reduction of 2% (30 acres).	Camden	CCMUA / Camden Co.	Design	Port Road improvements
		CCMUA	Planning / Design	Harrison Avenue / State Street - Complete Streets Project(s)
		CCMUA, Camden SMART	2017 – 2020 Completed	Various Camden SMART GSI projects totaling 2.75 acres
			2021 – 2023	Various GSI projects totaling 6 acres .

Projects	Permittee Lead (NJPDES Responsible Party)	Project Partners	Status	Project Synopsis
	CCMUA	Camden	Planning / conceptual design	C-32 sewershed green stormwater infrastructure
	Gloucester City		Design / planning	<ul style="list-style-type: none"> • Conceptual design for 4 acre GSI target area completed in dense older area subject to street flooding bounded by Monmouth, Ellis, Mercer and King Streets. • Johnson Blvd. Park improvements to include rain gardens. • Repairs to the rain gardens at the water treatment facility have been completed.

4

Mitigation of Street Flooding

4.1 Problem Overview

City of Camden


Street flooding during wet weather remains a major public health and environmental concern within the City of Camden. There are twenty sewersheds that have been associated with the reported street flooding hot spots identified in Camden's 2016 Flood Mitigation Plan. The number of locations where flooding has been reported Table 4-1 and locations are shown on Figure 4-1.

Table 4-1 – Camden Sewersheds Associated with Street Flooding

Sewershed / Regulator	# of Reported Flooding Locations	Sewershed / Regulator	# of Reported Flooding Locations
Name		Name	
C1	5	C16	1
C3	21	C17	0
C5	5	C22	8
C6	5	C22A	1
C7	4	C23	0
C8	2	C24	1
C9	1	C27	4
C10	2	C28	1
C11	5	CFA	2
C13 / 13A	0	C32	12

The approved LTCP Baseline Model indicates about 90 million gallons of street flooding in the Typical Year as the result of capacity limitations of the combined sewer system within the model extent.⁴⁻¹ This is premised on the full capacity of the Camden collection sewer system having been restored and maintained through regular cleaning and required repairs. The contributions of stormwater that can't get into the combined sewer system due to current blockages or capacity limitations have not been calculated as part of this study. It should be noted that the relative roles of structural capacity limitations within the sewer system and of non-structural causes such as blockages is not well understood. Therefore, as outlined in this section of the SIAR, a comprehensive program to understand and address the causes of street flooding is proposed.

⁴⁻¹ It should be noted that the hydraulic model is primarily intended to assess the performance of the regulator structures, interceptor sewers and WPCF capacity in relationship to flow rate and volume of combined sewage arriving at the regulator structures. The geographic extent of the model is limited in terms of the upstream collection sewers that send the combined sewage to the regulator structures and cannot simulate the performance of these un-modeled pipes. Therefore, the street flooding volumes shown must be viewed as indicative but imprecise.

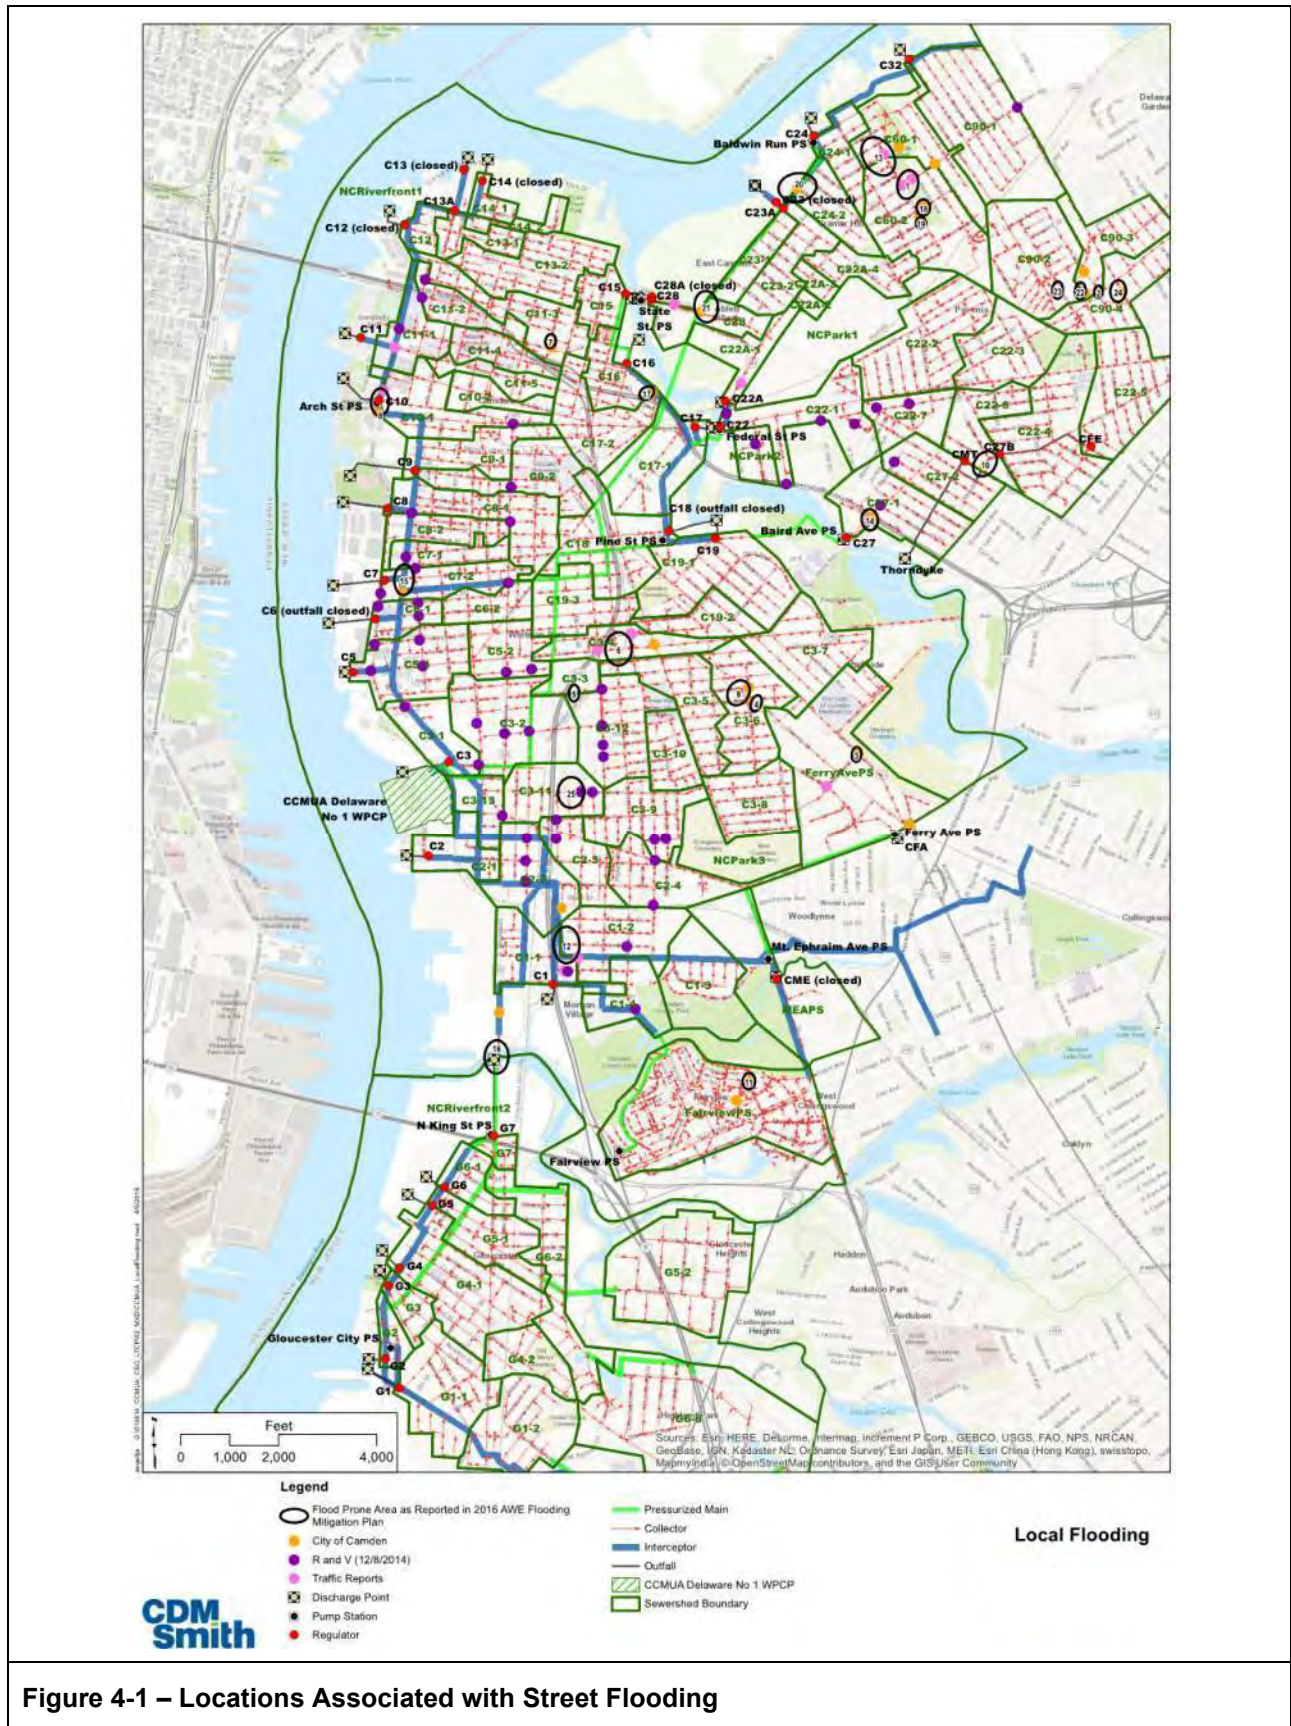

The City of Camden and CCMUA have undertaken a number of steps to address street flooding subsequent to the September 2020 SIAR; these are listed in Table 4-2.

Gloucester City

Street flooding can occur in Gloucester City during storm events occurring between two hours before and after high tides. Flooding has occurred near the King Street pumping station which is the low point of the combined system and along Water Street.

Gloucester City has a flood pump installed at the King St. pump station and another portable pump available to pump excess combined sewage when tidal conditions preclude normal drainage by gravity. In addition, Gloucester City and CCMUA coordinate the operation of CCMUA's Gloucester City pump station during high tide storm events to minimize flooding conditions.

Street flooding can have a number of causes, including:

- Stormwater not being able to enter the combined sewer system due to clogged catch basins;
- The hydraulic capacity of collection sewers being reduced by accumulated sediment;
- Clogged CSO outfalls;
- The hydraulic gradient of sewer segments being below that of the receiving stream during high tide; and
- Inherent capacity limitations of existing sewer segments.

The current understanding as to the proximate causes of street flooding at the known flooding locations is limited. Flooding event information such as flooding events dates, events per reported location, flooding duration, approximate sizes and depths of street floods and antecedent weather conditions are not currently available.

Gloucester City and CCMUA have undertaken a number of steps to address street flooding subsequent to the September 2020 SIAR; these are listed in Table 4-2.

4.2 Street Flooding Reduction Benefits of CSO Controls

The CSO controls outlined in this SIAR will reduce the volumes of combined sewer overflow that is discharged through collection sewer backups significantly. Increasing the treatment capacity at CCMUA's WPCF # 1 from 150 MGD to 185 MGD is projected to reduce the simulated volume of street flooding in the Typical Year by around 58% from 90 million gallons per year to 33 million gallons. This remaining street flooding volume is due to capacity limitations within the Camden sewer system. Expanding the plant up to 220 MGD wet weather capacity will enable a significant increase in the capture rate from the large Camden C-3 regulator structure but would not significantly reduce street flooding further upstream in the Camden system.

Given the informational constraints as to the nature and causes of street flooding it is difficult to ascertain the street flooding reduction benefits of the satellite wet weather storage or treatment facilities needed to achieve 85% capture in the Cooper River, Gloucester and (if needed) Delaware Backchannel sub-systems. Regardless, these facilities will be sized to achieve 85% capture of wet weather flows generated in their respective sub-systems.

The analyses performed using the LTCP model indicate that with the WPCF # 1 capacity upgrade to at 185 MGD, capacity limitations within the regulator structures and the interceptor sewers downstream of the regulator structures will not be a significant cause of street flooding. Wet weather flow arriving at the regulator structure that cannot enter the interceptor should be fully discharged through the combined sewer overflow pipe, (assuming that the outfall pipes are maintained and open). Future analysis may reveal the need for the pumping of wet weather flows during high tides at certain locations. If necessary for CSO control purposes, satellite facilities would capture wet weather flows that would otherwise be discharged through the outfall pipes necessary to meet their performance standard (e.g., 85% capture).

A better understanding as to the causes of street flooding within the sewersheds that contribute to the potential satellite facilities is needed. If it were to be determined that street flooding in a sewershed is caused by hydraulic limitations in the collection system, then consideration of increasing the capacity and the implications of the resulting additional flow to the regulator structure and into the satellite facility could then be considered. Street flooding will be better understood and quantifiable after the collection system cleaning program is completed and prior to the design and construction of any satellite facilities.

4.3 Street Flooding Mitigation Program

It is proposed that a Comprehensive Street Flooding Mitigation Program be developed by each city and CCMUA as an early long term CSO control plan implementation action. The objective is to establish a framework for a comprehensive program to mitigate street flooding.

Key program elements could include:

- Establish flood location mitigation priorities and the criteria for prioritization;
- Development of System Performance Goals
- Documenting the implementation of the 2016 Wastewater System Flood Mitigation Plan for Camden;
- Identification and involvement of stakeholders and the identification of an institutional structure for the development and implementation of the mitigation program;
- Coordination with or working within existing green stormwater and sustainable redevelopment groups and programs;
- Establishing a GIS based street flooding event data base. This would involve establishing a flood event spotting and reporting system to track the occurrence, duration, approximate size and depth, preceding weather conditions and tides and integrating these data into a geo-referencing data base;
- Evaluate the principal causes of street flooding by location including but not limited to system hydraulic limitations, situational hydraulic limitations (e.g., pipe or catch basin clogs, not enough inlets), changes in run-off characteristics, etc.;
- Targeted flow monitoring and the extension of the H&H model by Camden in flood prone segments of the Camden collection system within reasonable proximity to a regulator structure. This could be implemented after the restoration of the hydraulic

capacities through cleaning and the observation as to the impacts of this restoration on the occurrences of street flooding;

- Identify design standards and best practices for flooding mitigation for use on public and private redevelopment projects;
- Evaluate and develop a suite of mitigation alternatives;
- Identification and involvement of stakeholders and the identification of an institutional structure for the development and implementation of the mitigation program; and
- The identification and establishment of program funding sources.

4.4 Street Flooding Mitigation Activities Since September 2020 SIAR Submittal

Street flooding and other wet weather source reduction projects that have been undertaken proactively by CCMUA, Camden and Gloucester City are summarized on Table 4-2.

Table 4-2 – Street Flooding Mitigation and Source Reduction Project Undertaken Since 2020

Projects	Permittee Lead (NJDES Responsible Party)	Project Partners	Status	Project Synopsis
Develop and implementation of Camden Street Flooding Mitigation Program	Camden	CCMUA, Camden County	Design	<ul style="list-style-type: none"> • Harrison Avenue street flooding mitigation project. • Camden County's Port Road Improvement Project includes drainage improvements, sewer separation and where feasible GSI along portions of Second Street, Ferry Avenue, Broadway Street and Atlantic Avenue which will reduce local street flooding in the area. • Flood mitigation under C-32 project. • The ongoing outfall cleaning program has resulted in significant reductions in street flooding based on anecdotal information.
Reduction of wet weather flow from Pennsauken into the Camden combined sewer system in sewershed C-32.	CCMUA	Pennsauken, Camden	Design	<p>C-32 Program Elements:</p> <ul style="list-style-type: none"> • Implementation of Pennsauken Sewer Separation projects. • Conveyance of separated Pennsauken stormwater to Delaware back channel in new dedicated pipe and/or • Targeted sewer separation in East Camden to synch with Pennsauken separation. • Includes catch basin location and configuration optimization.

Projects	Permittee Lead (NJPDES Responsible Party)	Project Partners	Status	Project Synopsis
G-1 regulator – remedial cleaning May 2023	Gloucester City	CCMUA, Camden County	On-Going	<ul style="list-style-type: none"> • CCMUA has been evaluating the impact of allowing flow rates greater than 4.5 MGD from Gloucester City into CCMUA's Gloucester City pump station. Flows are being controlled through pump wetwell set-points pending the long term installation of VFD. • Gloucester City and CCMUA are proceeding with the cleaning of CSO outfalls. An inspection of current conditions was completed in August of 2023 and work is proceeding on the design, permitting and implementation of outfall cleaning analogous to the ongoing work on Camden's outfalls. Scheduling is detailed in Section 8 of this Revised SIAR. • Inspection & remedial cleaning of the G-1 regulator which has resulted in a significant reduction in street flooding in the G-1 sewershed. • Gloucester City is one of five small municipalities included in CCMUA's "River Town" street flooding mitigation study.⁴⁻² Phase 1 is complete and includes short term recommendations e.g., backflow preventors and a proposed Phase 2 for detailed planning and preliminary design of longer term mitigations.

<https://cdmsmithonline.sharepoint.com/sites/255047CSOAnnualConsultingCCMUARegulatorySupport/Shared Documents/General/CSO Program & NJPDES Permits/LTCP/LTCP 2023/2023 LTCP Revisions/Texts in WORD/SIAR 4 - flooding 09-27-23 Redline.docx>

⁴⁻² Bellmawr Borough, Brooklawn Borough, Gloucester City, Mt. Ephraim Borough and Westville Borough (Gloucester County)

5

Section 5

Additional Structural Controls Revised September 2023

5.1 Additional Control Requirements

The system wide control target of 85% capture cannot be met through the wet weather treatment capacity increase and source reduction alone, therefore sub-system level controls using satellite control facilities was evaluated in the approved 2019 DEAR. The anticipated levels of CSO controls with the expansion of CCMUA's WPCF # 1 to 185 MGD plus a system-wide 10% reduction in DCIA are shown in Table 5-1.

Table 5-1 – Typical Year Capture Impacts of Controlling Runoff from DCIA by 10%

System / Sub-System	WPCF # 1 @ 185 MGD, Camden Hydraulic Capacity Restored	Add 10% Control of Runoff in DCIA
System-Wide	78%	81%
Sub-System		
Delaware R. – Camden	89%	91%
Delaware R. – Gloucester	69%	74%
Delaware R. - Back Channel	69%	72%
Cooper River	70%	75%
Newton Creek	85%	87%

Additional CSO controls were evaluated for three of the five sub-systems to achieve the control objective of 85% system-wide wet weather capture during the Typical Year. It should be noted that the controls evaluated to achieve 85% system-wide wet weather capture will be sized to also achieve 85% capture in each individual sub-systems. Upon completion of the remedial system-wide sewer cleaning efforts by the City of Camden and Gloucester City, CCMUA will undertake a comprehensive flow monitoring program to provide data for the updating of the LTCP model which will provide updated capture rate data and refine the understanding of additional controls necessary to achieve 85% system-wide wet weather capture during the Typical Year. This will enable CCMUA and the Cities to update control alternatives analysis which will lead the final selection of additional controls needed to achieve 85% system-wide typical year wet weather capture.

The 85% capture target for the Delaware River – Camden subsystem will be achieved through the expansion of the wet weather treatment capacity at WPCF # 1 to 185 MGD (completed in 2020) along with modification to the C-3 regulator structure and its operating rules. The expansion of the WPCF#1 will also help the Newton Creek subsystem in achieving 85% capture.

Due to their hydraulic isolation (varies pump stations) from the WPCF #1, the Delaware River – Gloucester City, the Delaware River Back Channel and the Cooper River sub-systems would not achieve increased capture with the expansion of the plant treatment capacity. The hydraulic

limitations in the existing Camden and Gloucester interceptor sewers preclude the conveyance of additional wet weather flows to WPCF #1. Moreover, the additional conveyance option is mooted by the infeasibility of expanding the wet weather capacity at the WPCF beyond 220 MGD (see Chapter 5.3.2 of the DEAR report).

There are four broad options for controlling combined sewer overflows:

1. Source reduction – through the removal or reduction of stormwater through green stormwater infrastructure or sewer separation;
2. Conveyance of wet weather flows to a central treatment facility;
3. Satellite storage of wet weather flows until they can be bled back into the combined sewer system for centralized treatment; or
4. Satellite treatment at or near the CSO outfall to provide at least the equivalent of primary treatment and disinfection.

CCMUA proposes to achieve 85% capture in the Delaware River backchannel subsystem through the reduction of wet weather flows from Pennsauken Township and increasing the wet weather flow rates through the Baldwins Run pump station. Design work for the separation of combined sewer areas of Pennsauken Township is complete and pending construction permit approval. CCMUA is currently evaluating options for the conveyance of the separated Pennsauken stormwater for discharge to Delaware River back channel through or adjacent to CCMUA's C-32 outfall structure. This conveyance strategy may involve targeted sewer separation in Camden neighborhoods adjacent to Pennsauken or a dedicated stormwater line for the removed Pennsauken stormwater. In either case, CCMUA is studying the optimization of stormwater inlet placement and configuration to mitigate street flooding in East Camden.

Satellite storage or treatment will be required to achieve 85% capture in the Cooper River and Gloucester City sub-systems. The required capacities for these facilities are shown on Table 5-2. Capacity requirements are bracketed based on the achievement of 0% and 10% reductions in DCIA. A ten percent reduction in DCIA is the target established by CCMUA and the Cities as noted in Section 3 of this report. Zero percent reduction reflects the baseline current conditions and is used as a worst-case scenario. After the green stormwater program outlined in Section 3 has been underway for a while, the achievability of the 10% DCIA reduction goal can be re-evaluated.

Table 5-2 – Required Satellite Control Capacities

Sub-System	Locations	With 10% DCIA Reduction		Without 10% DCIA Reduction	
		Storage Volume in Million Gal.	Treatment Capacity in MGD	Storage Volume in Million Gal.	Treatment Capacity in MGD
Delaware River – Gloucester	G-4 / G-5	0.6	4.1	1.2	6.8
	G-1	0.5	2.3	0.7	4.4
Cooper River	C-22 / C-22A	1.3	20	2.6	21
	C-27 / Thorndyke	3	20.4	3.5	38.5
	C17	NA	NA	0.4	4.8

5.2 Overview of Alternative Control Technologies Evaluated

5.2.1 Satellite Treatment

Treatment Process Overview

Enhanced high-rate clarification (EHRC) has been used as the satellite treatment process for planning purposes. The term EHRC is generally used to describe a physical-chemical process in which coagulant and polymer are added to wastewater to remove solids from the stream.


The intent of EHRC treatment is to remove solids from and to disinfect the captured combined sewage. This provides effluent with total suspended solids concentrations that are similar or less than the effluent from the primary clarifiers at the wastewater plant. The removed solids then need to be conveyed to the main treatment plant for treatment.

The coagulant aggregates the suspended solids in the flow into a floc. The resulting floc particles adsorb onto either very fine sand added to the wastewater, or recirculated solids with the aid of a polymer. The fine sand and recirculated solids act as ballast and increases the settling rate of the adsorbed floc, removing the solids from the flow stream. The process is also known as “ballasted flocculation.” EHRC systems can be operated intermittently during storm events.

A typical ballasted flocculation system consists of addition of ferric chloride, polymer, and “microsand” (sand approximately 100-microns in diameter) to wastewater. The wastewater and additives are rapidly mixed (flash mixing), then slowly stirred in a maturation tank before settling in a clarifier. The sludge from the settling process is passed through a hydrocyclone, where the microsand is removed from the sludge and recycled.

Several suppliers provide enhanced high-rate clarification systems as proprietary products, including: Kruger’s Actiflo® process, which uses microsand as ballast, and Degremont Technologies’ DensaDeg® process, which uses recirculated solids as ballast. Cross-sectional diagrams of the two technologies are shown on Figure 5-1

Whichever process is selected, BOD and TSS removal rates associated with high-rate clarification have been shown to be roughly double those of traditional clarification. BOD removal is between

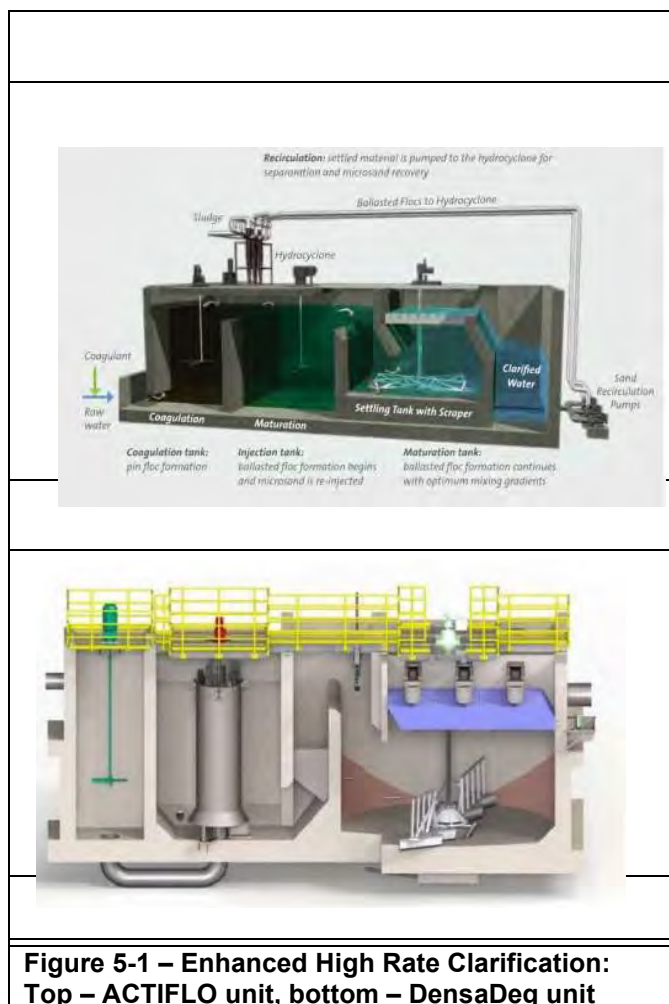

65- and 80-percent and TSS removal is between 70- and 95-percent, according to the USEPA's August 2004 "Report to Congress on the Impacts and Control of CSOs and SSOs". These reductions clearly meet (and even exceed) those of conventional primary treatment processes, and thus satisfy the requirement to provide the "equivalent of primary clarification" per the EPA CSO Policy. Other benefits of this process include:

- Footprint area requirements are only one-tenth of traditional clarification area requirements (5 to 15-percent of the space required for conventional primary treatment);
- Can handle high hydraulic loading rates and treat rapidly varying flows; and
- Able to achieve secondary treatment effluent standards for TSS and approach these standards for BOD.

EHRC also has some disadvantages, including:

- Higher capital costs than less complex processes such as simple settling or screening technologies;
- Higher operating costs relative to conventional clarification due to chemical and floc media requirements;
- 15 - 30 minute start-up time before significant removal occurs;

Solids removed through the satellite treatment process range in concentration from around 0.1% to 1.0% with an average of around 0.3% and are typically discharged to the interceptor sewer for transport and treatment at the wastewater treatment plant. While high in solids concentration (1,000 mg/l to 10,000 mg/l) the volume generated relative to total interceptor sewer flows are typically low enough to not pose operating problems. The feasibility of this being acceptable in Camden or Gloucester would need to be confirmed during a later detailed facilities planning phase of LTCP implementation.

Disinfection

As documented in the System Characterization Report, pathogens pose the primary water quality impact of the CSOs into the Delaware and Cooper Rivers and Newton Creek. Therefore, disinfection of effluent from satellite treatment facilities is assumed. Three disinfection technologies were considered:

- Sodium Hypochlorite;
- Ultraviolet (UV); and
- Peracetic Acid

Detailed descriptions and evaluations of these disinfection technologies were included in Appendix A of the approved Development and Evaluation of Alternatives Report. For purposes of this long term control planning document, disinfection using sodium hypochlorite is assumed. Regulations have required most wastewater treatment plants and CSO facilities to add a dechlorination process that uses sodium bisulfite to remove chlorine before it enters the receiving water. On average, dechlorination will add about \$0.30 per gallon of treatment capacity to the cost of chlorination.

5.2.2 Satellite Storage

Off-line surface storage can be used to capture all or part of CSO discharge. When system capacity becomes available, flows are then released for conveyance to the treatment plant. When flow volumes exceed the storage capacity, flow will be discharged to CSO outfalls. Two different

approaches can be used to handle these discharges: either (1) flow can be diverted around the storage tank when full, or (2) flow can pass through the tank and overflow at the downstream end of the tank, at which point the storage tank effectively becomes a high-rate settling tank. In either case, the size of a surface storage tank depends upon the capture goals set for each site.

A typical storage tank arrangement includes a regulator, bar screens, pumping facility and piping to and from the collection system. Design details such as flow distribution, tank flushing, and facility activation also are affected by the overall goals for and hydraulics of the specific site. Examples of storage tanks are shown on Figure 5-2.



Figure 5-2 – Examples of Satellite Storage Facilities. Left: below grade facility under construction. Right: retention treatment basin in Inkster Michigan.

Storage tanks are generally fed by gravity and the stored flow is typically pumped back to the interceptor after the storm. This gravity-in / pump-out arrangement minimizes pumping costs (both capital and operating). However, if the existing combined sewers are deep, then the storage tank must be deep and construction becomes more expensive.

5.2.3 Reduction of Inflow & Infiltration (I&I)

Part IV.F.1.h.1.ii of CCMUA's and the Cities' NJPDES permits require that I&I be identified and reduced to non-excessive levels as defined at N.J.A.C. 7:14A-1.2. It was stated in the approved June 2019 joint Development & Evaluation of Alternatives Report that I&I reduction will not play a major role in long term CSO control due to the high volumes of wet weather flow generated in the combined sewer areas relative to the volume of I/I contributed from the hydraulically connected sanitary sewer areas.

A revised baseline level of I&I in and contributing to the CCMUA / Camden / Gloucester combined sewer systems will be determined through the comprehensive flow monitoring and model update to be completed once the Camden and Gloucester sewers and outfall cleaning is completed. The results of this analysis will be integrated into the revised LTCP model and used in the revised control alternatives analysis to be completed in the 2027-2028 time frame.

5.3 Control Alternatives

5.3.1 Summary Assessment of Control Option

Satellite facilities can pose significant siting, financial and operating burdens on the municipalities in which they are located which must be considered in the alternatives selection process. A qualitative summary of the two approaches' pros and cons is provided on Table 5-3.

Table 5-3 – Qualitative Comparison of EHRC and Storage

	Enhanced High Rate Clarification (Ballasted Flocculation)	Storage Tanks
Pro	<ul style="list-style-type: none"> • High levels of treatment and treated effluent quality (meets / exceeds primary treatment). • Proven technology. • Process equipment relatively compact. • Not affected by precursor storm events. 	<ul style="list-style-type: none"> • Relative operating simplicity. • Proven technology • Only discharges to receiving streams during storm events exceeding storage capacities • Captured flow is sent back to the wastewater treatment plant for full treatment
Con	<ul style="list-style-type: none"> • Operating complexity. • Requires post event cleaning and maintenance. • Requires on-site hypochlorite and other chemical storage • Likely point-source performance standards. • Capital and O&M costs 	<ul style="list-style-type: none"> • Utilizes interceptor and treatment plant capacities during post storm drain downs. • Overflows when storage capacities are exceeded. • Required post event cleaning more difficult than for ballasted flocculation.

5.3.2 Treatment and Storage Cost Estimation (circa 2019)

Generic planning level capital, operation and maintenance (O&M) and life-cycle costs for Enhanced High Rate Clarification and for storage facilities have been developed utilizing process equipment manufacturer data as presented in the January 2018 PVSC Updated Technical Guidance Manual (TGM) that was included as Appendix A in the approved CCMUA / Camden / Gloucester Development and Evaluation of Alternatives Report.⁵⁻¹

5.3.3 Permittee Specific Cost Estimates

Detailed capital and O&M cost estimates have been developed for the Cities of Camden and Gloucester and for the CCMUA. These estimates are premised upon 1) the inclusion of green stormwater infrastructure sufficient to reduce the directly connected impervious areas of Camden and Gloucester by 10%, and 2) that each permittee will be responsible for the future capital and operating costs of CSO controls located within their respective collection systems.

⁵⁻¹ Tables 2-18 through 2-22 for ballasted flocculation facilities and Tables 2-29 through 2-31 for disinfection.

City of Camden

The estimated capital costs (in 2020 dollars) and O&M costs for satellite treatment and for satellite storage at Camden regulators C-22 & C-22A (Cooper River) and C-27 & Thorndyke (Cooper River) are shown on Tables 5-4 and 5-5.

As detailed below, the capital cost estimates for Camden range between \$102 million for the enhanced high rate clarification treatment option and \$130 million for storage tanks. While the estimated capital cost difference of roughly \$28 million or a difference of 27%, it should be noted that the construction cost estimates are Class 5 (Conceptual Screening) as defined by the Association for the Advancement of Cost Engineering and therefore have an expected accuracy range of -50% through +100%.

Table 5-4 – Camden CSO 85% Typical Year Wet Weather Capture Control Cost Estimates* (circa 2019)

Sub-System	Treatment		Storage	
	Capacity in MGD	Cost	Capacity in MG	Cost
Cooper River				
C-22 / C-22A	20 MGD		1.2 MG	
Construction Cost		\$8,316,000		\$10,447,000
Land Acquisition & Remediation		\$605,000		\$605,000
28% Non-Construction		\$2,328,000		\$2,925,000
Total Capital		\$11,249,000		\$13,977,000
50% of Construction for Contingency		\$4,158,000		\$5,223,500
Total With Contingency		\$15,407,000		\$19,200,500
C-27 / Thorndyke	20 MGD		1.2 MG	
Construction Cost		\$8,316,000		\$21,765,000
Land Acquisition & Remediation		\$770,000		\$770,000
28% Non-Construction		\$2,328,000		\$6,094,000
Total Capital		\$11,414,000		\$28,629,000
50% of Construction for Contingency		\$4,158,000		\$10,882,500
Total With Contingency		\$15,572,000		\$39,511,500
Total Cooper River				
Construction Cost		\$16,632,000		\$32,213,000
Land Acquisition & Remediation		\$1,375,000		\$1,375,000
28% Non-Construction		\$4,657,000		\$9,020,000
Total Capital		\$22,664,000		\$42,608,000
50% of Construction for Contingency		\$8,316,000		\$16,106,500
Total With Contingency		\$30,980,000		\$58,714,500

Sub-System	Treatment		Storage	
	Capacity in MGD	Cost	Capacity in MG	Cost
10% DCIA Reduction via GSI				
Construction Cost		\$39,836,000		\$39,836,000
28% Non-Construction		\$11,154,000		\$11,154,000
Total Capital		\$50,990,000		\$50,990,000
50% of Construction for Contingency		\$19,918,000		\$19,918,000
Total With Contingency		\$70,908,000		\$70,908,000
Total Camden Capital Costs				
Construction Cost		\$56,468,000		\$72,048,000
		\$1,375,000		\$1,375,000
28% Non-Construction		\$15,811,000		\$20,174,000
Total Capital		\$73,654,000		\$93,597,000
50% of Construction for Contingency		\$28,234,000		\$36,024,000
Total With Contingency		\$101,888,000		\$129,621,000
* Excludes future costs for system renewal and replacement necessary to maintain design capacities.				

Table 5-5 - City of Camden CSO Controls Estimated Annual O&M and Life Cycle Costs (circa 2019)

Present Worth & Annual Cost Calculations	Treatment & Green	Storage & Green
Annual O&M Cost Estimates		
Non-GSI	\$854,000	\$424,000
GSI Costs	\$329,000	\$329,000
Total Annual	\$1,183,000	\$753,000
Present Worth		
Present Worth of O&M	\$18,016,000	\$11,467,000
Plus Capital Costs (without contingency)	\$73,654,000	\$93,597,000
Total Present Worth	\$91,670,000	\$105,064,000
Estimated Annual Costs		
Debt Service Payments	\$6,188,000	\$7,864,000
Annual O&M	\$1,183,000	\$753,000
	\$7,371,000	\$8,617,000

The control facilities would add between \$7.4 to \$8.6 million to the annual wastewater management costs of the City of Camden. While the capital costs for tanks is higher, the O&M costs are projected to be lower; with a 20 year present worth O&M cost savings of around \$6.6 million. The projected annual costs also include debt service payments of \$6.2 to \$7.9 million, based on the use of the New Jersey Clean Water State Revolving Fund financing program. Total life cycle costs for the two options are \$91.7 million for the EHRC option and \$105.1 million for storage. The present worth calculations include a twenty year operating period and a discount rate for the O&M of 2.75%. Note that the capital costs used in the lifecycle cost calculation (Table 5-5) do not include the 50% construction contingency and are therefore lower than the total capital costs shown in Table 5-4 which do include construction contingencies.

Gloucester City Cost Estimates

The estimated capital costs (in 2019 dollars) and O&M costs for satellite treatment and for satellite storage serving Gloucester are shown on Table 5-6. The estimated capital costs for a treatment based approach to achieving 85% wet weather capture in Gloucester is approximately \$27 million. Estimated capital costs for storage are \$45 million.

Incremental annual costs for Gloucester would range between around \$2.0 million for the treatment option and \$3.0 million for the storage options as shown on Table 5-7. These figures include financing of the capital costs through the N.J. Clean Water SRF as was the case for Camden.

Table 5-6 – Gloucester CSO Control Cost Estimates (circa 2019)

Sub-System	Treatment		Storage	
	Capacity	Cost	Capacity	Cost
Gloucester City - Delaware River				
Satellite Treatment or Storage	6.4 MGD		1.1 MG	
Construction Cost		\$10,943,000		\$20,895,000
Land Acquisition & Remediation		\$550,000		\$550,000
28% Non-Construction		\$3,064,000		\$5,850,000
Total Capital		\$14,557,000		\$27,295,000
50% of Construction for Contingency		\$5,471,000		\$10,447,000
Total With Contingency		\$20,028,000		\$37,742,000
10% DCIA Reduction via GSI				
Construction Cost		\$3,993,000		\$3,993,000
28% Non-Construction		\$1,118,000		\$1,118,000
Total Capital		\$5,111,000		\$5,111,000
50% of Construction for Contingency		\$1,996,500		\$1,996,500
Total With Contingency		\$7,107,500		\$7,107,500
Total Gloucester Capital Costs				
Construction Cost		\$14,935,000		\$24,887,000
Land Acquisition & Remediation		\$550,000		\$550,000
28% Non-Construction		\$4,182,000		\$6,968,000
Total Capital		\$19,667,000		\$32,405,000
50% of Construction for Contingency		\$7,468,000		\$12,444,000
Total With Contingency		\$27,135,000		\$44,849,000

* Excludes future costs for system renewal and replacement necessary to maintain design capacities.

Table 5-7 – Gloucester CSO Control Estimated Annual & Life Cycle Costs (circa 2019)

Present Worth & Annual Cost Calculations	Treatment & Green	Storage & Green
Annual O&M Cost Estimates		
Non-GSI		
	\$394,000	\$118,000
GSI Costs	\$33,000	\$33,000
Total Annual	\$427,000	\$151,000
Present Worth		
Present Worth of O&M	\$6,504,000	\$2,300,000
Plus Capital Costs (without contingency)	\$19,667,000	\$32,406,000
Total Present Worth	\$26,171,000	\$34,706,000
Estimated Annual Costs		
Debt Service Payments	\$1,322,000	\$2,178,000
Annual O&M	\$427,000	\$151,000
Total Annual Costs	\$1,749,000	\$2,329,000

CCMUA Cost Estimates

The estimated capital costs for CSO controls for CCMUA total approximately \$80 million as detailed on Table 5-8. This figure includes \$36.6 million for the expansion of the wet weather capacity at WPCF # 1 from 185 MGD to 220 MGD and \$44.3 to reduce overflows from CCMUA's C-32 regulator sufficiently to achieve 85% capture of wet weather flows during the Typical Year. As noted in Section 2.2, expanding the wet weather treatment capacity to 220 MGD has been determined as neither necessary or cost effective to achieve the 85% system-wide capture goal.

Table 5-8 – CCMUA CSO Control Capital Cost Estimates (circa 2019)

Sub-System	Cost
Delaware Back Channel	
C-32	
Construction Cost	
Regulator Modifications	\$156,300
Flow Restriction Modification	\$39,100
Source Reduction	\$19,379,300
Baldwins Run PS Modification	\$5,000,000
Subtotal Construction	\$24,574,700
Land Acquisition & Remediation	\$550,000
28% Non-Construction	\$6,880,900
Total Capital	\$32,005,600
50% of Construction for Contingency	\$12,287,300
Total With Contingency	\$44,292,900

Sub-System	Cost
Expansion of WPCF # 1 to 220 MGD	
Construction Cost	\$20,000,000
28% Non-Construction	\$5,600,000
50% of Construction for Contingency	\$10,000,000
Total With Contingency	\$35,600,000
Total CCMUA Capital Costs	
Construction Cost	\$44,574,700
Land Acquisition & Remediation	\$550,000
Non-Construction @ 36%	\$12,480,900
Total Capital	\$57,605,600
Add Contingency @ 50% of Construction	\$22,287,300
Total With Contingency	\$79,892,900
* Excludes future general capital improvements and renewals & replacement.	

Projected incremental O&M costs for CCMUA as well as the estimated total lifecycle costs for the CCMUA improvements are shown on Table 5-9.

Table 5-9 – CCMUA CSO Control Incremental O&M and Life Cycle Cost Estimates (circa 2019)

Present Worth & Annual Cost Calculations	
Estimated Incremental Annual O&M Costs	\$500,000
Present Worth	
Present Worth of O&M	\$7,613,600
Plus Capital Costs (without contingency)	\$57,605,500
Total Present Worth	\$65,219,100
Estimated Annual Costs	
Debt Service Payments	\$3,872,000
Annual O&M	\$500,000
Total	\$4,372,000

System-Wide Cost Estimate Roll-Up

The respective cost estimates for Camden, Gloucester and CCMUA are aggregated and summarized on Table 5-10. Aggregated capital costs, including construction contingencies total \$209 million for the EHRC option and \$254 million for the storage option, a difference of about 31%. Combined annual incremental O&M costs are estimated to be \$2.4 million for treatment and \$1.4 million for storage.

As noted above, CCMUA will undertake a comprehensive flow monitoring and model update upon full completion of the remedial sewer and outfall efforts. The results of the modeling update will be used as a basis for re-evaluating technical control alternatives to reflect revised design flow projections as well as emergent technologies, climate change, economic and inflation trends, and other local conditions that have changed since the initial alternatives evaluation (DEAR) in 2019. Revised cost estimates will be developed through this analysis.

5.4 Cost / Performance Considerations

The Cities of Camden and Gloucester and CCMUA have determined that the Presumption Approach⁵⁻² should be used as the basis for their CSO control strategies and have established the control of 85% of wet weather flow volume generated during the Typical Year as the CSO control performance target.


Paragraph G-5(a) of the respective NJPDES permits require that permittees utilizing the Presumption Approach to analyze various levels of CSO controls to determine where the

⁵⁻² Under the USEPA CSO Control Policy (59 FR 18692) a CSO control program that eliminates or captures for treatment no less than 85% of the volume of combined sewage that is collected in the combined sewer system during precipitation events during a Typical Year would be presumed to provide an adequate level of control.

Table 5-10 – System-Wide Roll Up of Cost Estimates (circa 2019)

Permittee	Estimated CSO Control Costs*	
	Treatment	Storage
City of Camden		
Capital Costs		
Before Contingencies	\$73,654,000	\$93,597,000
With Contingencies	\$101,888,000	\$129,621,000
Annual O&M	\$1,183,000	\$753,000
Present Worth		
Present Worth of O&M	\$18,016,000	\$11,467,000
Total Present Worth (w/o Contingencies)	\$91,670,000	\$105,064,000
Gloucester City		
Capital Costs		
Before Contingencies	\$19,667,000	\$32,405,000
With Contingencies	\$27,135,000	\$44,849,000
Annual O&M	\$427,000	\$151,000
Present Worth		
Present Worth of O&M	\$6,504,000	\$2,300,000
Total Present Worth (w/o Contingencies)	\$26,171,000	\$34,706,000
CCMUA		
Capital Costs [excludes Incurred 185 MGD plant costs]		
Before Contingencies	\$57,605,600	57,605,600
With Contingencies	\$79,892,900	79,892,900
Annual O&M	\$500,000	500,000
Present Worth		
Present Worth of O&M	\$7,613,600	7,613,600
Total Present Worth (w/o Contingencies)	\$57,605,500	57,605,500
Rollup: Camden + Gloucester + CCMUA		
Capital Costs		
Before Contingencies	\$150,926,600	\$183,607,600
With Contingencies	\$208,915,900	\$254,362,900
Annual O&M	\$2,110,000	\$1,404,000
Present Worth		
Present Worth of O&M	\$32,133,600	\$21,380,600
Total Present Worth (w/o Contingencies)	\$175,446,500	\$197,375,500
* Excludes future costs for system renewal and replacement necessary to maintain design capacities.		

increment of pollution reduction achieved in the receiving waters diminish compared to the increased costs. Such an evaluation often is referred to as a “knee of the curve” analysis. For this analysis, CCMUA and the Cities initially evaluated the relationship between the frequencies of overflows from the 30 active outfalls during a Typical Year and the volumes of combined sewage discharged from the

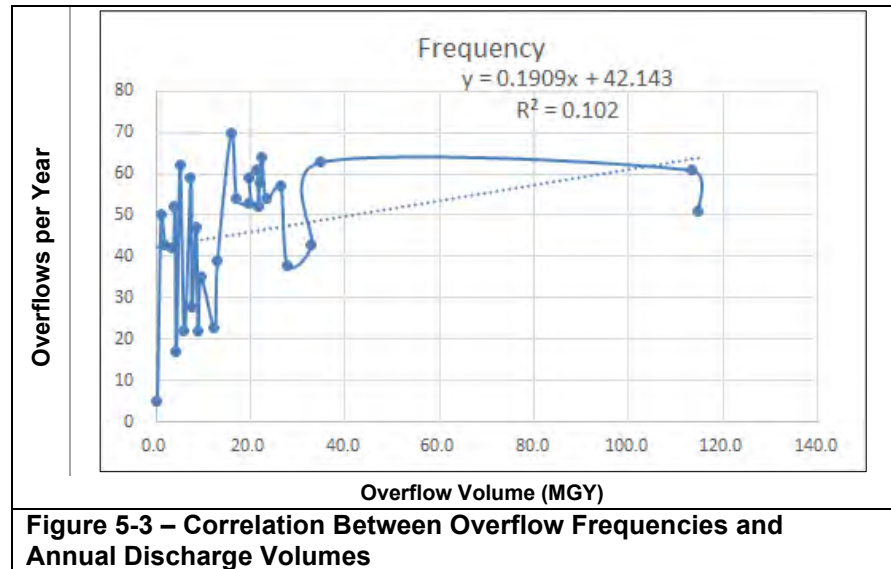


overflows. As is typical for combined sewer systems with diverse sewershed sizes and land use characteristics, there is little correlation between overflow frequencies and annual overflow volumes from individual out falls. This is shown graphically for the Camden / Gloucester / CCMUA combined sewer system on Figure 5-3.

The variability in overflow volumes between outfalls and the weak relationship between frequency and volume supports the selection of the 85% system-wide capture performance standard. The use of an overflow-event number based performance target, if strictly applied across the 30-outfall system, e.g. 4 to 6 overflows per year, could require that controls be in place at every outfall that exceeds the target frequency under baseline conditions. Therefore, decisions as to where to allocate scarce resources would not be driven by the optimization of overflow reduction benefits, as compared to a more flexible volume-based target applied at the system or sub-system level.

The modeling performed for this cost-performance analysis indicates that achieving 85% capture system-wide will reduce annual CSO volumes by roughly 485 million gallons. This level of CSO reduction approximates (and slightly better) that which would be accomplished with control levels between eight and twelve overflows per year.

As shown on Table 5-10, the estimated capital costs for system-wide 85% control is around \$200 million (excluding construction contingencies). This figure is based on the averaging of the system-wide costs using satellite treatment and those using satellite storage and is net of the 50% construction contingency. The \$200 million estimated compares with the approximately \$450 million in estimated capital costs for reducing overflows to eight times per Typical Year. A cost-control level curve showing the CSO removal volumes at CSO frequency controls ranging from twenty overflows per year down to zero is presented in Figure 5-4. Included on this graph are the costs and overflow removal volume under an 85% capture strategy. A corollary cost curve showing the Typical Year remaining annual CSO volumes is shown in Figure 5-5.

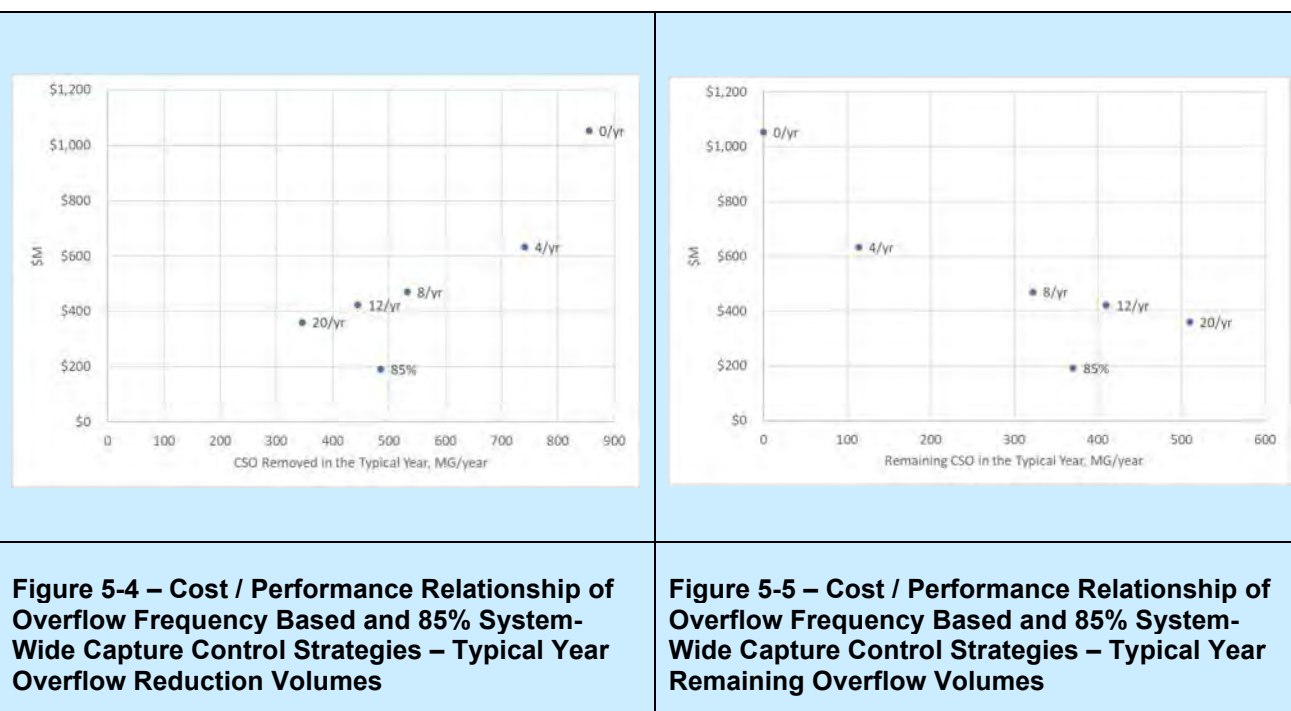

5.5 Site Considerations

The preliminary site requirements for the potential satellite treatment or storage facilities described above are shown on Table 5-11. Approximate site vicinity and current land use maps for these potential satellite facilities are shown on Figures 5-9 through 5-13.

Table 5-11 – Potential Satellite Facilities Vicinity Information

Subsystem		Vicinity of Regulators	Approximate Area Required (acres)	Vicinity Notes
1	Delaware River – Gloucester	G1 or the CCMUA Gloucester City Pump Station	~1.5	A facility would be located either in the vicinity of the G-1 regulator or near the Gloucester City Pump Station. A new pipe would convey wet weather flows from regulators G-4 and G-5 as well as G-1 to this facility. Current brownfield site.
2	Cooper River	C22 – C22A	~1.5	Brownfield (status unknown) private bus yard, Federal Street pump station.
		C27 - Thorndyke	~1.5	Grassed area of Gateway Park
		C17	~1.5	Only required if green control targets can't be met in the Cooper River sub-system.

Gloucester City

The hydraulically optimal location for satellite CSO controls within Gloucester City is in the vicinity of Gloucester regulator structures G-4 and G-5 as shown on Figure 5-6. This however would require placement of a satellite facility within or adjacent to Gloucester's Proprietor's Park.

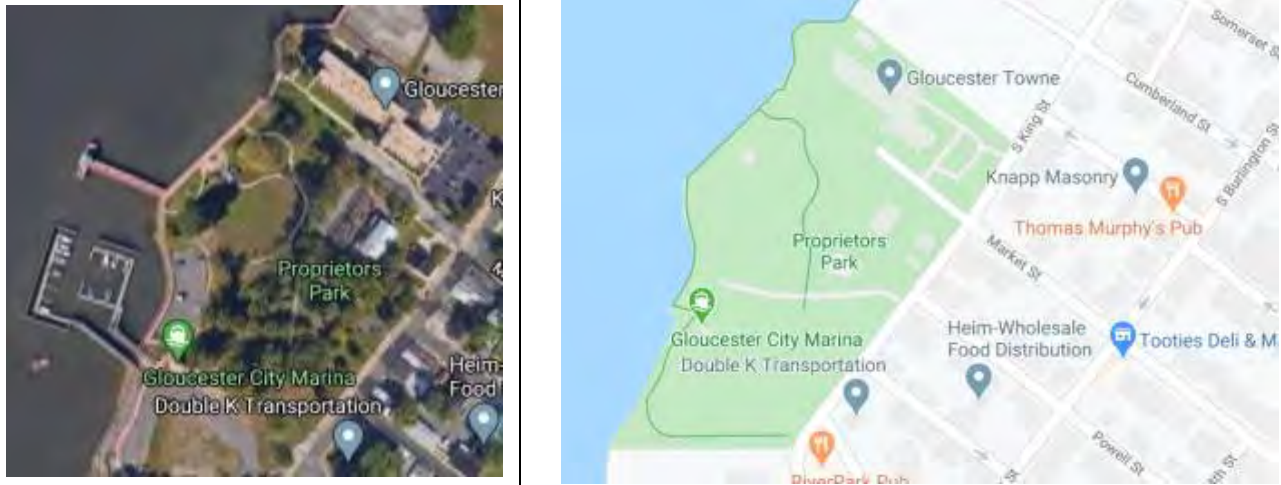


Figure 5-6 – Vicinity of Gloucester City regulators G-4 and G-5 and Adjacent Land Use

To avoid this, an alternative site has been identified in the vicinity of the CCMUA Gloucester City regional pump station and/or around regulator G-1 as shown on Figure 5-7. Consolidation pipes would be needed to convey flow from G-4 and G-5 into the off-site facility.

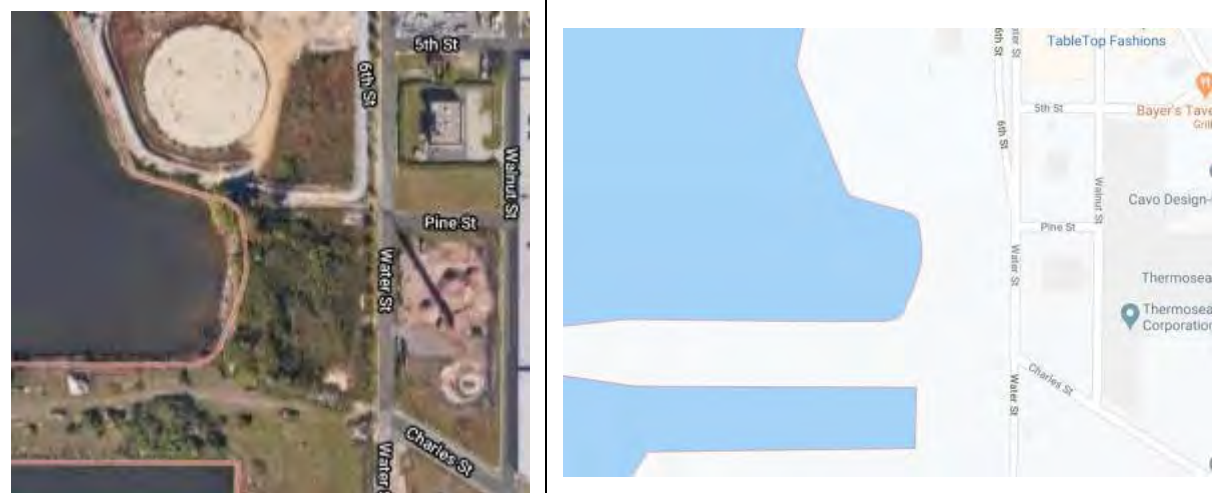


Figure 5-7 – Gloucester City CSO Control Facility Potential Alternative Site Vicinity

Cooper River – Camden C-22 /22A and C-27 / Thorndyke Regulators

These four regulators discharge to the Cooper River. C-22 and C-22A are adjacent to the Federal Street pump station and the Federal Street bridge over the Cooper River as shown on Figure 5-8.



Figure 5-8 – Vicinity of the Camden C-22 / C22-A Outfalls

The outfalls for C-27 and Thorndyke are the most upstream in the Camden combined sewage system that discharge to the Cooper River. The potential location for a satellite facility, adjacent to the existing Thorndyke Street netting facility is shown on Figure 5-9.



Figure 5-9 – Vicinity of the Camden C-27 and Thorndyke St. Outfalls

Cooper River – Camden C-17 Regulator

If the long term goal of reducing runoff from directly connected impervious in the Cooper River sub-system is not met, an additional satellite treatment facility for the C-17 sewershed will be needed to meet the 85% control objective. The C-17 regulator structure is across the Cooper River and slightly upstream from the C-22 regulator as shown on Figure 5-10. Should additional controls for C-17 prove to be necessary in the long term; the cost-effectiveness of upsizing and consolidating either the C-22 or the C-17 satellite facilities and conveying the wet weather flows across the river for treatment or storage could be evaluated.



Figure 5-10 – Vicinity of the Camden C-17

5.6 Conclusions

In the approved Development and Evaluation of Alternatives Report (DEAR) CCMUA and the Cities of Camden and Gloucester presented a suite of control strategies that would result in the system-wide capture and treatment of 85% of wet weather flows to the combined sewer system during a Typical Year. Through the expansion of CCMUA's WPCF # 1 to 185 MGD, the restoration of the hydraulic capacity of Camden collection system and flow reduction through 10% green infrastructure the capture level is projected to reach 81% and additional controls will be necessary in the Cooper River, Delaware River back channel, and the Delaware River Gloucester City sub-systems.

The technical options for achieving the required additional controls that were outlined in the DEAR have been refined in this section and for purposes of long term control planning now focus on satellite storage through tanks or treatment through enhanced high rate clarification and disinfection. This SIAR is not making a recommendation between storage and treatment. Capacity requirements and cost estimates are provided and it is assumed that the ultimate choice between storage and treatment is best left to future municipal decision makers based on then current conditions.

As noted in the introduction to this section, upon completion of the remedial system-wide sewer cleaning efforts by the City of Camden and Gloucester City and subsequent flow monitoring and model update, CCMUA and the Cities will re-evaluate control alternatives as needed which will lead the final selection of additional controls necessary to achieve 85% system-wide typical year wet weather capture.

6

Section 6.0 Financial & Institutional Capability

Assessments Revised September 2023

Note – The financial and institutional capability assessment presented below represents CCMUA's, the City of Camden's and Gloucester City's best understanding of then current conditions and the impacts of implementing the long term control plan as presented in the September 2020 SIAR. This 2020 analysis will be rendered obsolete by the impacts of a number of subsequent developments:

- Potential changes in the use designations and related in-stream water quality standards for Zone 3 of the Delaware River that would result in new treatment plant effluent limits for nutrients (ammonia), currently under development by USEPA and the Delaware River Basin Commission (DRBC);
- The results of the updated CSO control alternatives analyses to be conducted during the forthcoming (2024 – 2028) NJPDES permit cycle upon the completion of system cleaning, flow monitoring, and subsequent revisions to the H&H model;
- USEPA's issuance of revised financial capability guidance in February, 2023;
- Economic changes since 2020 including construction and borrowing cost inflation and an improved potential for federal funding assistance.

CCMUA and the Cities will update the financial and institutional capability assessments as a part of the updated alternatives analyses which is anticipated to occur in the 2027 – 2028 time frame.

6.1 Affordability Assessments

6.1.1 Purpose and Methodology

This section of the SIAR presents a Financial Capability Analysis (FCA) relating to the development of the CSO Long Term Control Plan (LTCP) required under Paragraph G(8)(a) of the Combined Sewer Management section of a permittee's NJPDES discharge permit. The assessment is based upon the EPA document "Combined Sewer Overflows – Guidance for Financial Capability Assessment and Schedule development," (EPA Guidance Document) published February 1997⁶⁻¹, as supplemented by EPA's November 2014 memorandum entitled "Financial Capability Assessment Framework for Municipal Clean Water Act Requirements".⁶⁻²

⁶⁻¹ EPA 832-B-97-004

⁶⁻² November 24, 2014 memorandum from Ken Kopocis, Deputy Assistant Administrator, Office of Water (OW) and Cynthia Giles, Assistant Administrator, Office of Enforcement and Compliance (OECA) to Regional Administrators

This document supports the twofold purposes of the FCA as envisioned in the 1994 CSO Control Policy⁶⁻³ (Policy). First, this FCA is intended to identify the upper limits of what could constitute an affordable future investment strategy as defined by the Policy and related guidance documents under an assumed LTCP implementation schedule; thereby informing the development of CSO, SSO, MS4, TMDL, and other necessary control alternatives. Second, the assessment will support the development of a workable implementation schedule for the LTCP.⁶⁻⁴

The Financial Capability assessment is a two phased process. The residential indicator (RI) is the percentage of a permittee's service area median household income (MHI) expended on wastewater (including stormwater) management. The upper limit of affordability for wastewater services within the Cities and CCMUA will be the point where total wastewater management costs for the typical residential user exceed 2.0% of their respective Median Household Incomes (MHI).

The financial capability indicator is an assessment of the permittee's debt burden, socioeconomic conditions, and financial operations. These two measures are subsequently entered into a *financial capability matrix*, suggested by EPA, to determine the level of financial burden placed on residential customers and the permittee by the existing and projected future expenditures to operate, maintain, and enhance the wastewater management system. The EPA matrix appears in Table 6-12 of this document.

The projected future expenditures driving the RI and imposing demands upon the financial capability of the Cities and CCMUA will include the implementation of CSO controls, stormwater controls, conveyance / collection system rehabilitation, and other operational, maintenance, and capital improvements to the municipal sewer systems. In effect, the future CSO control expenditures will be net of all other expenditures necessary to maintain the appropriate levels of service required to meet public needs, protect public health and the environment and to maintain regulatory compliance under the Clean Water Act, the New Jersey Water Pollution Control Act and the Safe Drinking Water Act.

These analyses are based on information provided by the Cities, CCMUA and external sources such as the on-line fiscal reports available through the New Jersey Department of Community Affairs.⁶⁻⁵

6.1.2 Estimated Current Wastewater Costs per Household ⁶⁻⁶

The Residential Indicator is an approximation of "affordability" which EPA defines as a households' abilities to pay their total wastewater costs and is derived by dividing the total annual wastewater costs for the typical household within the permittees' service areas by the

⁶⁻³ Combined Sewer Overflow Policy Section II-C(8) 59 FR 18694

⁶⁻⁴ "Schedules for implementation of the long-term CSO control plan may be phased based on the relative importance of adverse impacts upon water quality standards and designated uses, and on a permittee's financial capability." (59 FR 18688)

⁶⁻⁵ https://www.nj.gov/dca/divisions/dlgs/resources/fiscal_rpts.shtml

⁶⁻⁶ Estimates are for 2019 based on latest published rate information from the permittees.

median household income within the service areas. The Residential Indicator is compared to EPA-defined criteria to determine whether total annual wastewater costs impose a low, mid-range, or high impact on residential users. Table 6.-1 shows U.S. EPA's Residential Indicator criteria, which define a "low" impact as a cost per household (CPH) less than 1.0% median household income (MHI), a "mid-range" impact between 1.0 and 2.0%, and "high" impact as greater than 2.0% of MHI.

Table 6 - 1 – EPA Residential Indicator

Residential Indicator	Cost per Household
Low Burden	Less than 1.0 percent of MHI
Mid-Range Burden	1.0-2.0 percent of MHI
High Burden	Greater than 2.0 percent of MHI

The estimated typical annual cost for wastewater services for a typical single family residential wastewater user account in 2019 for Camden was \$581 annually. The cost per residential account in Gloucester was \$724 and \$520 in the CCMUA service area. The derivation of these estimates is shown on Table 6.-2.

For these analyses, the annual costs for a single family residential wastewater accounts are used as proxy for households. User charge rate information combined with an estimate of typical potable water consumption provides an empirically based uniform annual cost estimate.

Table 6 - 2 – Calculated Costs per Typical Residential Wastewater Account in 2019

Metric	Permittee		
	Camden	Gloucester	CCMUA
Wastewater Costs per Typical Residential User Account			
Municipal			
Service Charge	\$71.2 ^a	\$372	\$174 ^c
Collection System	<u>\$158^b</u>		
Subtotal Municipal	\$229		
CCMUA	<u>\$219</u>	<u>\$352</u>	<u>\$352</u>
Total	449	\$724	\$526
Median Household Income	\$26,105 ^d	\$51,152 ^d	\$69,283 ^c
Current Residential Indicator	1.7%	1.4%	0.76%

a Camden service charge of \$17.80 per quarter x 4

b Camden collection system charge of \$2.20 per 100 cubic feet of water consumption and an estimated monthly water consumption of 6.02 CCF.

c Average for the 37 CCMUA municipalities weighted by the number of Census households. Municipal costs were calculated based on total costs per household as presented in "Assessing the Affordability of Water and Sewer Utility Costs in New Jersey" by Daniel J. Van Abs (Rutgers University) and Tim Evans (NJ Future) published 2018.

e Source: US Census - American Community Survey (2013 - 2017)

The residential indicator in Camden was at 1.7% of median household income, reflecting the estimated \$449 in annual costs and the median household income of \$26,105. This places the current wastewater cost burden at the upper end of the mid-range category. While the estimated cost per typical residential user in Gloucester was somewhat higher at \$724, Gloucester's median household income of \$51,152 resulted in a residential indicator of 1.45%. This is in the middle of EPA's "medium burden" category.

Calculating the typical cost per residential user throughout the CCMUA service area is a bit less direct. CCMUA has thirty-seven customer municipalities ranging in population from 75,500 (Camden) to 4 (Pine Valley and Tavistock Boroughs), number of households ranging from 26,356 (Camden) to 2 each for Pine Valley and Tavistock, and median household incomes ranging from \$200,000 (Pine Valley and Tavistock) down to \$26,105 (Camden). Annual municipal collection system costs per residential user ranged from \$400 (Chesilhurst Borough) down to zero. It should be noted that the municipalities with "zero" collection system user charges recover their system costs through their property tax bases. A detailed analysis of the collection sewer system related portion of the property tax levies in these municipalities is beyond the scope of this SIAR analysis.

In Camden, 37.4% of the population was living below the poverty line. The total Census households are broken out by income brackets on Table 6.-3 below, along with the respective current Residential Indicators by income bracket. The RI for each bracket was calculated from the mid-point income within the bracket. As may be noted, the current RI for more than 15,000 households exceed 2.0% and around twelve thousand households have wastewater costs exceeding 3.0%.

Table 6-3 – Analysis of the Current Residential Indicator for Camden

Income Bracket	Households		Bracket Average Income	Bracket RI at Typical Cost per Household
	Number	Cumulative		
Less than \$10,000	5,380	5,380	\$5,000	11.64%
\$10,000 to \$14,999	2,538	7,918	\$12,500	4.66%
\$15,000 to \$24,999	4,329	12,247	\$20,000	2.91%
\$25,000 to \$34,999	2,882	15,129	\$30,000	1.94%
\$35,000 to \$49,999	3,368	18,497	\$42,500	1.37%
\$50,000 to \$74,999	3,260	21,757	\$62,500	0.93%
\$75,000 to \$99,999	1,633	23,390	\$87,500	0.67%
\$100,000 to \$149,999	1,217	24,607	\$125,000	0.47%
\$150,000 to \$199,999	380	24,987	\$175,000	0.33%
\$200,000 or more	208	25,195	\$200,000	0.29%
Total	25,195			

In Gloucester, 11.2 percent of the population was living below the poverty line. The total Census households are broken out by income brackets on Table 6.-4 for Gloucester. In Gloucester, around 1,500 households had residential indicators exceeding 2.4% of household income.

Table 6 - 4 – Analysis of the Current Residential Indicator for Gloucester

Income Bracket	Households		Bracket Average Income	Bracket RI at Typical Cost per Household
	Number	Cumulative		
Less than \$10,000	165	165	\$5,000	14.48%
\$10,000 to \$14,999	281	446	\$12,500	5.79%
\$15,000 to \$24,999	470	916	\$20,000	3.62%
\$25,000 to \$34,999	554	1,470	\$30,000	2.41%
\$35,000 to \$49,999	497	1,967	\$42,500	1.70%
\$50,000 to \$74,999	815	2,782	\$62,500	1.16%
\$75,000 to \$99,999	575	3,357	\$87,500	0.83%
\$100,000 to \$149,999	500	3,857	\$125,000	0.58%
\$150,000 to \$199,999	175	4,032	\$175,000	0.41%
\$200,000 or more	43	4,075	\$200,000	0.36%
Total	4,075			

6.1.3 Affordability Impacts of CSO Control Alternatives

The estimated capital, incremental debt service and incremental operation and maintenance (O&M) costs of achieving the 85% control target were developed in Section 5 of this SIAR. CCMUA has developed dynamic financial planning and affordability models Camden, Gloucester and CCMUA. These have been used to project the annual costs per typical single family wastewater user upon full implementation of the CSO controls. The projected impacts are shown on Tables 6-5 through 6-7 for Camden Gloucester and CCMUA respectively.

Included in the tables are the residential indicators for 2042 based on an assumed 20 year implementation schedule. The use of a 20 year implementation schedule is intended only to provide a uniform initial basis for analysis; as will be seen from the model outputs a 20 year implementation schedule would result in unacceptable affordability impacts. Also included is a set of hypothetical residential indicators if the CSO controls could be implemented instantaneously this year. This exercise is intended to remove the impacts of inflation.

Table 6 - 5 – Affordability Impacts of the Evaluated CSO Controls: Camden

Metric	≥ 85% Capture	
	Low	High
Capital Costs (millions in 2019 \$)		
85% Typical Year Wet Weather Capture Program	\$101.9	\$129.6
Incremental Costs to Control Cooper River to Zero Overflows per Year	\$272.1	
Potential Total Capital Costs (85% Capture Program + Cooper River Zero OPY less 85% capture Cooper River satellite facilities)	\$374.0	401.7
Projected Residential Indicator in 2042 (Twenty-Year Implementation with inflation)		
For 85% Capture Program	4.8	5.0

Metric	≥ 85% Capture	
	Low	High
Projected Residential Indicator If CSO Control Costs Were Implemented All at Once This Year (to remove inflation impacts)		
For 85% Capture Program	2.5	2.6
With Cooper River Zero Overflow per Year Controls	4.8	5.0
With Cooper River Zero Overflow per Year Controls (<i>For documentation of financial infeasibility only – Elimination of Lower Cooper River overflows is not included in the proposed long term control program.</i>)	8.4	8.1

As noted in Section 5.3.3 and as demonstrated in Section 5.4.2 the elimination of all overflows to the lower Cooper River is financially not achievable and is not included in the proposed long term control program defined in this SIAR.

Table 6 - 6 – Affordability Impacts of the Evaluated CSO Controls: Gloucester City

Metric	≥ 85% Capture	
	Low	High
Capital Costs (millions in 2019 \$)	\$27.1	\$44.8
Projected Residential Indicator in 2042 (Twenty-Year Implementation with inflation)	4.0%	4.7%
Projected Residential Indicator If CSO Control Costs Were Implemented All at Once This Year (to remove inflation impacts)	3.0%	3.7%

Table 6 - 7 – Affordability Impacts of the Evaluated CSO Controls: CCMUA

Metric	≥ 85% Capture
	Low
Capital Costs (millions in 2019 \$)	\$79.9
Projected Residential Indicator in 2042 (Twenty-Year Implementation with inflation)	0.80%
Projected Residential Indicator If CSO Control Costs Were Implemented All at Once This Year (to remove inflation impacts)	0.75%

Details about the nature and cost breakouts for the control strategies included in these tables are provided in Section 5.3.2 of this document.

Key observations about the data in these table include:

- Owing to its number of outfalls on three receiving streams, the projected least capital cost controls for Camden's CSOs are at \$102 million are roughly four times those estimated for Gloucester and 27% more than CCMUA.
- Camden's least cost controls would push the Camden residential indicator to at least 2.5% even if inflation is excluded.
- Gloucester's controls would likewise result in Gloucester's residential indicator being at least 3.0% with or without inflation.

Due to its size, higher median household income and CSO control obligations being limited to the C-32 outfall and the potential further expansion of its WPCF # 1, the projected RI for the CCMUA service area would appear to remain at the upper limit of what USEPA considers as a low impact. However, due to the income variations between the CCMUA customer municipalities, the use of a regionalized residential indicator is very misleading.

6.1.4 Methodology and Underlying Assumptions

Methodology

CCMUA has developed individual detailed dynamic financial models for each of Camden, Gloucester and CCMUA. These models project current system costs through any reasonable CSO control program implementation period (e.g. 20 through 40 years) based on assumed rates of inflation and any available information as to future system changes or planned capital improvements outside of the CSO controls covered in this SIAR.

Annual revenue requirements for the current municipal systems are calculated by each model based on the projected annual costs along with policy options such as debt service coverage targets, the percentages of capital improvements to be funded by debt or available funds (e.g. from renewal and replacement funds) and the use of retained earnings. The models "start" with the adopted 2019 budgets and 2019 user rates. User rates are adjusted in the model annually based upon changes in revenue requirements. For example, if a hypothetical borough's total wastewater budget is \$10 million in 2020 and typical residential costs are \$300 annually and the projected budget in 2021 is \$11 million, the model would project the cost per residential user to be \$330.

Future annual capital costs for CSO controls along with any other new capital programs that have been identified are overlaid to the existing costs in the models. Based upon the financing policy assumptions used, incremental debt service is added one year after a financed capital expenditure. For model simplification purposes, the models "assume" that debt is issued annually during the course of the implementation phase of the capital program(s). Incremental operation and maintenance (O&M) costs are added as applicable in the years following the completion of capital expenditures.

The models can be run with inflation on or off. Running future scenarios without inflation provides a simpler view of the impacts of varying program scopes and schedules. This approach has the advantage of eliminating the need to estimate future rates of inflation and income growth. However, omitting inflation can understate the affordability impact of long-term programs since income growth has not kept pace with and is not projected to keep pace with water utility capital and O&M cost inflation. For example, for the period of 1999 through

2013, the national costs for typical household wastewater services increased at a rate of 4.8%.⁶⁻⁷ The national Consumer Price Index increased at an annual rate of around 2.4%⁶⁻⁸ for the period, while the US median household income increased from around \$42,000 to \$52,250 at an annual rate of 1.6%.⁶⁻⁹

On the other hand, running the models with inflation turned on provides an arguably more realistic vision of the future albeit based on some conjecture as to future economic variables such as inflation and interest rates. Including assumptions about inflation rates based upon look-backs at historical rates for time periods approximating the CSO control implementation schedule can provide a reasonable approach to estimating future affordability.

Underlying Assumptions

Key assumptions used in the above analysis are summarized on Table 6 - 8. An annotated complete list of all data and assumptions used in the affordability model is provided as Appendix B to this memorandum.

Table 6- 8 – Affordability Model Key Inputs and Assumptions

Item	Value	Notes
Finance		
Bond Term		
Market Interest Rate	6.0%	NJEIT Financing – Smart Growth program offers 75% funding at 0% interest and 25% funding at market rates for 20 years for CSO control projects.
NJDEP	0.0%	
Blended Interest Rate	1.5%	
Target Coverage	125%	
O&M as % of Capital Cost	2.0%	
Economic		
LTCP O&M Inflation	3.9%	Based on national rates of wastewater system O&M costs in 2017 NACWA study.
LTCP Construction Inflation	3.7%	Based on 1984 – 2015 ENR Construction Cost Index for New York City (80%) and Philadelphia (20%).
Estimate Base Year		
MHI Data Year	2015	
Typical Household Monthly Consumption	4,500	Typical urban water consumption.

6.2 Financial Capability Assessment

The second part of the financial capability assessment is intended to evaluate the financial capabilities of the permittees to finance the required CSO controls. The process is similar to that used by the bond rating agencies and includes six items that fall into three general categories of debt, socioeconomic, and financial management indicators. The six items are:

6-7 NACWA 2013 Cost of Clean Water Index

6-8 US Bureau of Labor Statistics

6-9 US Census

1. Bond rating
2. Total net debt as a percentage of full market real estate value
3. Unemployment rate
4. Median household income
5. Property tax revenues as a percentage of full market property value
6. Property tax revenue collection rate

Items 2, 5 and 6 are applicable to municipalities that have taxing authority and that can fund capital expenditures directly by or backed up through property taxation. Municipal authorities such as CCMUA have no taxing authority and these three property tax related metrics are not applicable.

Each item is given a score of three, two, or one, corresponding to ratings of strong, mid-range, or weak, according to EPA-suggested standards. The overall financial capability indicator is then derived by taking a simple average of the ratings. This value is then entered into the financial capability matrix to be compared with the residential indicator for an overall capability assessment). Table 6-9 contains the six criteria and the ratings that categorize the permittee as strong, mid-range, or weak in each category. A discussion of each item follows.

Table 6 - 9 – Permittee Financial Capability Indicator Benchmarks

Indicator	Strong (3)	Mid-Range (2)	Weak (1)
Bond Rating	AAA-A (S&P) or Aaa-A (Moody's)	BBB (S&P) or Baa (Moody's)	BB-D (S&P) or Ba-C (Moody's)
Overall Net Debt as a Percent of Full Market Property Value	Below 2%	2% to 5%	Above 5%
Unemployment Rate	More than 1% below the National Average	+/- 1% of the National Average	More than 1% above the National Average
Median Household Income	More than 25% above National MHI	+/- 25% above National MHI	More than 25% below National MHI
Property Tax as a Percent of Full Market Property Value	Below 2%	2% to 4%	Above 4%
Property Tax Collection Rate	Above 98%	94% to 98%	Below 94%

6.2.1 Bond Rating – Indicator 1

The bond ratings of the three permittees are as follows:

- City of Camden – Standard & Poor's BBB+ which is considered to be mid-range
- Gloucester City – Standard & Poor's AA- which is considered to be strong.
- CCMUA – Moody's Aa2 – which is considered to be strong.

6.2.2 Overall Direct Net Debt as a Percent of Full Market Value – Indicator 2

Debt Burden is measured by overall net debt as a percent of full market property value, which evaluates the ability of local government to issue additional debt. Overall Direct Net Debt is defined as current total liability to be repaid by property taxes divided by the municipality's full market property value. This indicator is relevant as a metric for municipalities issuing general obligation bonds which are substantially repaid through property tax revenues.

Overall direct net debt for Camden for 2019 was \$47.1 million.⁶⁻¹⁰ The percent of total net debt to the three-year average property valuation of \$1.57 billion¹⁰ was 3.03%, which places Camden in the midrange range on this measure.

Overall direct net debt for Gloucester for 2019 was \$13.9 million.⁶⁻¹¹ The percent of total net debt to the three-year average property valuation of \$543 million¹⁰ was 2.75%, which places Camden in the midrange range on this measure.

This metric is not applicable to CCMUA.

6.2.3 Unemployment Rate – Indicator 3

The unemployment rate is used as an assessment of the economic well-being of residential users in the service area. The dataset for the municipal unemployment rates is taken from the US Census American Community Survey 2013-2017 estimates. The American Community Survey gathers data over a 5-year period.⁶⁻¹² The prevailing unemployment rate provided by the ACS for that timeframe more closely represents the actual strength of the economy in a municipality.

The unemployment rate for Camden is 14.0% compared to the national rate of 6.6% for the same time period, resulting in a weak rating. It may be noted that the “weak” rating is triggered in the EPA table when the local unemployment rate is one percent above the national average. Gloucester's unemployment rate was 6.7%, resulting in a mid-range score. The Camden County county-wide unemployment rate of 7.9% can be used as a proxy for CCMUA. This unemployment rate was slightly more than one percent above the national average of 6.6% for the same period, resulting in a weak score.

6.2.4 Median Household Income – Indicator 4

Median Household Income (MHI) divides the relevant incomes of a population into two parts so that half of the incomes are below the median and half of the incomes are above the median. Unlike average income, median income is not skewed by extremely high or extremely low incomes in the dataset. The median household incomes for Camden, Gloucester and the CCMUA service area are shown on Table 6-10.

⁶⁻¹⁰ Source: Camden's 2019 NJDCA User Friendly Budget Sheet USB-10

⁶⁻¹¹ Source: Gloucester's 2019 NJDCA User Friendly Budget Sheet USB-10

Table 6-10 – Median Household Income

Permittee	Median Household Income ⁶⁻¹²	United States	% Difference from US	Categorization
Camden	\$26,105	\$57,650	-55%	Weak
Gloucester	\$51,152		-11%	Mid-Range
CCMUA	\$69,283		+20%	Mid-Range

6.2.5 Tax Revenues as a % of Full Market Value – Indicator 5

The three year average property valuations in Camden was \$1.7 billion.⁶⁻¹³ A tax of \$28.1 million is levied on the assessed valuation. Therefore, the property tax levy is approximately 1.6%. This value is considered strong in the USEPA metrics.

The three year average property valuations in Gloucester was \$543 million.⁶⁻¹⁴ A tax of \$22 million is levied on the assessed valuation. Therefore, the property tax levy is approximately 4.0%. This value is considered weak in the USEPA metrics.

This metric is not applicable to CCMUA

6.2.6 Property Tax Collection Rate

The EPA criterion for a strong rating in this category is a collection rate of more than 98%. Camden's rate is calculated to be 88.4%, which places it in the weak range for real estate tax collections. Gloucester's collection rate is calculated to be 96.7% which is considered mid-range.

This metric is not applicable to CCMUA.

6.2.7 Financial Indicator Score

As shown on Table 6 -11, the overall score for the financial indicators is 2.0, yielding an EPA Qualitative Score of midrange. This calculation is based on the use of all six of the indicators that are applicable to Camden, Gloucester and CCMUA.

Table 6 - 11 – Permittee Financial Capability Indicator Benchmarks

Indicator	Camden		Gloucester		CCMUA	
	Rating	Numeric Score	Rating	Numeric Score	Rating	Numeric Score
Bond Rating	Mid-Range	2	Strong	3	Strong	3
Overall Net Debt as a Percent of Full Market Property Value	Mid-Range	2	Mid-Range	2	NA	
Unemployment Rate	Weak	1	Mid-Range	2	Weak	1

⁶⁻¹² Source: US Census – National Community Survey estimates for 2013 - 2017

⁶⁻¹³ Source: 2019 User Friendly Budget – sheet USB 10

⁶⁻¹⁴ Source: 2019 User Friendly Budget – sheet USB 10

Indicator	Camden		Gloucester		CCMUA	
	Rating	Numeric Score	Rating	Numeric Score	Rating	Numeric Score
Median Household Income	Weak	1	Mid-Range	2	Mid-Range	2
Property Tax as a Percent of Full Market Property Value	Strong	3	Mid-Range	2	NA	
Property Tax Collection Rate	Weak	1	Mid-Range	2	NA	
Total		10		13		
Overall Indicator Score: (numeric score / number of applicable indicators)		1.67		2.17		6.0
EPA Qualitative Score	Mid-Range		Mid-Range		Mid-Range	

6.3 Financial Capability Matrix

In this section the results of the step 1 affordability analysis which goes towards the residential ratepayers' ability to afford CSO controls within the context of other capital investment needs is integrated with the step 2 (Financial Capability) analysis which goes towards the permittee's ability to finance the implementation of the LTCP.

It was established previously that the least present worth cost CSO control options described in this SIAR would result in the following projected residential indicators in 2042 after a twenty-year implementation period:

- Camden – The residential indicator would be 5.4% of MHI for the least cost approach to controlling wet weather overflows from its Delaware River, Cooper River and Newton Creek overflow structures;
- Gloucester - The residential indicator would be 3.3% of MHI for the least cost approach to control its discharges to the Delaware River and Newton Creek; and
- CCMUA – The residential indicator would be 1.0% after implementing controls for its wet weather discharges to the back channel of the Delaware River from its C-32 outfall.

The overall financial capability ratings for Camden, Gloucester and CCMUA are all considered to be midrange under the EPA framework. The intersection of these two ratings on the EPA financial capability matrix places Camden and Gloucester in the category of high financial burden and CCMUA would be in the mid-range, as shown on Tables 6-12 through 6-14 respectively.

Table 6-12 – The Financial Capability Matrix - (Shaded areas Indicate Camden's Ratings)

Permittee Financial Capability Indicators Score	Residential Indicator		
(Socioeconomic, Debt and Financial Indicators)	Low (Below 1.0%)	Mid-Range (Between 1.0 and 2.0%)	High (Above 2.0%)
Weak (Below 1.5)	Medium Burden	High Burden	High Burden
Mid-Range (Between 1.5 and 2.5)	Low Burden	Medium Burden	High Burden
Strong (Above 2.5)	Low Burden	Low Burden	Medium Burden

Table 6-13 – The Financial Capability Matrix - (Shaded areas Indicate Gloucester's Ratings)

Permittee Financial Capability Indicators Score	Residential Indicator		
(Socioeconomic, Debt and Financial Indicators)	Low (Below 1.0%)	Mid-Range (Between 1.0 and 2.0%)	High (Above 2.0%)
Weak (Below 1.5)	Medium Burden	High Burden	High Burden
Mid-Range (Between 1.5 and 2.5)	Low Burden	Medium Burden	High Burden
Strong (Above 2.5)	Low Burden	Low Burden	Medium Burden

Table 6-14 – The Financial Capability Matrix - (Shaded areas Indicate CCMUA's Ratings)

Permittee Financial Capability Indicators Score	Residential Indicator		
(Socioeconomic, Debt and Financial Indicators)	Low (Below 1.0%)	Mid-Range (Between 1.0 and 2.0%)	High (Above 2.0%)
Weak (Below 1.5)	Medium Burden	High Burden	High Burden
Mid-Range (Between 1.5 and 2.5)	Low Burden	Medium Burden	High Burden
Strong (Above 2.5)	Low Burden	Low Burden	Medium Burden

6.4 Additional Economic Factors

Measuring the household burden imposed by wastewater costs as a percentage of the median household income may underestimate the financial burden of the projected wastewater costs per household. As was noted in an analysis of the impacts of CSO controls in the Boston region:

“The greater are the costs of other necessities as a share of MHI, the greater will be the economic burden associated with sewer charges equal to a given percent of MHI.”⁶⁻¹⁵

Therefore, in addition to following EPA guidelines for completion of the financial capability assessment metric, a discussion of socioeconomic conditions in the City of Camden and Gloucester City is essential to the consideration of scheduling and compliance levels with CSO guidelines.

6.4.1 Cost of Living Index

City of Camden

The overall cost of living within the City of Camden has been calculated at 94% of the US national average.⁶⁻¹⁶ Statewide, New Jersey’s cost of living is 123% of the national average. The apparent lower cost of living in Camden is driven by the depressed housing market in the City which results in a housing index of 59% of the national average. Other components in the cost of living index are higher than their respective national averages:

- General goods and services – 105%
- Groceries – 117%
- Health care – 103%
- Transportation – 115%
- Utilities – 108%.

Camden’s cost of living must be considered in the context of its median household income which is only 45% of the national MHI. Allowing for the 4% lower cost of living, the effective MHI in Camden would still only be about 48% of the national median, or conversely the effective cost of living in Camden is more than twice the national average.⁶⁻¹⁷

Gloucester City

The overall cost of living within Gloucester City has been calculated at 100% of the US national average.⁶⁻¹⁵ Statewide, New Jersey’s cost of living is 123% of the national average. The cost of living in Gloucester being at the national average and 23% less than the New Jersey average is also driven by a housing index of 80% of the national average. As is the case for Camden, other components in the cost of living index are higher than their respective national averages:

- General goods and services – 105%
- Groceries – 117%
- Health care – 103%
- Transportation – 115%
- Utilities – 108%.

⁶⁻¹⁵ Assessment of the Economic Impact of Additional Combined Sewer Overflow Controls in the Massachusetts Water Resource Authority Service Area (page 13) prepared by Robert N. Stavins, Genia Long, and Judson Jaffee. Analysis Group Incorporated, August 2004.

⁶⁻¹⁶ Source: Areavibes.com

⁶⁻¹⁷ Calculated as follows: cost of living (100%/94%) X Camden MHI @ 45% = 47.9%; or cost of living index of 100% / 47.9% = 2.08.

Gloucester's cost of living also must be considered in the context of its median household income which is 11% lower than the national MHI. This suggests an effective cost of living in Gloucester that is 12% higher than the national average.

6.4.2 Housing Costs

Based upon a 2017 study⁶⁻¹⁸ by the National Low Income Housing Coalition, the fair market value of a two bedroom apartment in both Camden County and the Philadelphia / Camden/Wilmington MSA was \$1,211 per month or \$14, 532 annually. This works out to 58% of the Camden and 28% of the Gloucester median household incomes.

The same study defines affordable monthly apartment rents at around \$662 per month. This figure represents 30% of the annual wages at the average hourly wages for renters (around \$27,400). At \$662 per month, annual rents equal about 32% of the Camden MHI and around 15% of the MHI in Gloucester.

6.4.3 Local Tax Burdens

City of Camden

The property tax burdens within Camden and Gloucester are substantial. The average residential tax for 2019 in Camden was \$_____. This includes Camden's taxes of \$_____ along with Camden County and school district taxes.⁶⁻¹⁹

Gloucester City

The average residential tax for 2019 in Gloucester was \$4,665 for a property with the average assessed valuation of 108,000. This includes Gloucester's taxes of \$2,397 along with Camden County and school district taxes.²⁰ This compares with a national average local property tax levy of \$3,500 for a similarly priced home.

6.4.4 Poverty Rate⁶⁻²¹

Per the US Census' 2013-2017 American Community Survey the poverty rates in Camden and Gloucester were 37.4 and 11.2 respectively. These compares to the national average poverty rate of 14.6%.

6.4.5 Income Growth Trends

The MHI growth rates between 2000 and 2015 were about 0.69% annually for Camden and 1.95% annually for Gloucester. This growth rate compares with the growth rates for New Jersey (2.20%) and for the U.S. (2.14%).

⁶⁻¹⁸ Out of Reach 2017 – The High Cost of Housing National Low Income Housing Coalition.

⁶⁻¹⁹ Source: 2017 NJDCA User Friendly Budget sheet UFB-1

⁶⁻²⁰ Source: 2017 NJDCA User Friendly Budget sheet UFB-1

⁶⁻²¹ Source: US Census – National Community Survey 2013 - 2017

6.4.6 NJDCA Municipal Revitalization Index (MRI)

The Municipal Distress Index⁶⁻²² measures the social, economic, physical and financial conditions of the 565 municipalities within New Jersey. The MRI is compiled by the NJ Department of Community Affairs and is used in the distribution of needs based funding. Six primary along with four secondary criteria are used:

Primary Criteria

- Children on TANF (Temporary Assistance for Needy Families) per 1,000 persons
- Unemployment Rate
- Poverty Rate
- High school diploma or higher
- Median Household Income
- Percent of households receiving SNAP (food stamps)

Secondary Criteria

- Ten year rate of change in population
- Non-seasonal housing vacancy rate
- Equalized three year effective property tax rate
- Equalized property valuation per capita

The 2017 state-wide MRI rankings for the thirty-seven municipalities within Camden County are shown on Table 6-15. The City of Camden has a ranking of 1 as the most distressed municipality. Gloucester City is ranked 51 state-wide, placing it in the top 10th percentile ranking. A synthesized ranking for all 37 CCMUA municipalities was calculated using the numbers of households per municipality as a weighting factor. The calculated MRI distress score is 40.6 which would give it a ranking of about 79th, or within the top 15th percentile.

Table 6-15 – Municipal Renewal Index for the CCMUA Customer Municipalities

Municipality		2017 Municipal Revitalization Index			Population	Households
		MRI Score	MRI Distress Score	MRI Rank		
1	Camden City	-26.05	100.0	1	75,550	25,195
2	Woodlynne Borough	-14.69	68.4	15	2,950	805
3	Lindenwold Borough	-8.96	52.4	32	17,418	7,096
4	Clemonton Borough	-7.70	49.0	42	4,933	1,898
5	Lawnside Borough	-7.21	47.6	46	2,917	1,148
6	Chesilhurst Borough	-6.64	46.0	49	1,647	584
7	Gloucester City	-6.42	45.4	51	11,333	4,075

⁶⁻²² Measuring Distress in New Jersey: the 2017 Municipal Revitalization Index Office of Policy and Regulatory Affairs, New Jersey Department of Community Affairs.

Municipality		2017 Municipal Revitalization Index			Population	Households
		MRI Score	MRI Distress Score	MRI Rank		
8	Pine Hill Borough	-6.21	44.8	55	10,517	5,232
9	Brooklawn Borough	-6.14	44.6	57	2,006	713
10	Pennsauken Township	-5.11	41.7	71	35,863	12,163
11	Audubon Park Borough	-5.02	41.5	76	1,023	479
12	Bellmawr Borough	-4.54	40.2	83	11,583	4,357
13	Hi-Nella Borough	-4.54	40.1	84	861	366
14	Berlin Township	-4.22	39.3	94	5,453	2,058
15	Mount Ephraim Borough	-3.36	36.9	116	4,641	1,779
16	Magnolia Borough	-3.14	36.3	118	4,310	1,643
17	Somerdale Borough	-3.06	36.0	121	5,417	2,164
18	Runnemede Borough	-3.06	36.0	122	8,391	3,191
19	Merchantville Borough	-2.71	35.1	129	3,769	1,421
20	Waterford Township	-1.69	32.2	165	10,749	3,521
21	Barrington Borough	-1.47	31.6	172	6,811	2,770
22	Laurel Springs Borough	-1.34	31.2	177	1,917	707
23	Stratford Borough	-1.31	31.2	179	7,019	2,576
24	Winslow Township	-0.90	30.0	192	39,317	13,645
25	Oaklyn Borough	-0.88	30.0	193	4,009	1,751
26	Gloucester Township	-0.83	29.8	195	64,034	23,422
27	Berlin Borough	-0.58	29.1	206	7,612	2,750
28	Collingswood Borough	-0.54	29.0	210	13,969	6,023
29	Gibbsboro Borough	0.55	26.0	247	2,183	774
30	Audubon Borough	0.69	25.6	255	8,736	3,500
31	Vorhees Township	1.21	24.2	286	29,386	10,929
32	Cherry Hill Township	2.06	21.8	341	71,204	26,356
33	Haddon Township	2.25	21.3	350	14,612	5,820
34	Haddon Heights Borough	2.65	20.1	373	7,530	2,921
35	Pine Valley Borough	4.51	15.0	472	4	2
36	Haddonfield Borough	5.72	11.6	519	11,428	4,195
37	Tavistock Borough	9.89	0.0	565	4	2
CCMUA Service Area-Wide Weighted by # of Households		(4.71)	40.6	79	511,106	188,031

6.5 Institutional Context

6.5.1 System Ownership, Operation and Maintenance Responsibilities

The Cities of Camden and Gloucester own their respective municipal sewerage consisting of primarily combined collection systems and sanitary collection systems and stormwater collection and conveyance systems in limited areas of each municipality. The combined sewer portions of their collection systems are operated under permits NJ0108812 (Camden) and NJ0108847 (Gloucester). The Camden County Municipal Utilities Authority (CCMUA) provides wastewater conveyance (via the Baldwins Run pump station and force main) and treatment services for Camden and Gloucester along with thirty-five suburban municipalities within Gloucester County. CCMUA's one CSO associated with the C-32 regulator structure upstream of the Baldwin's Run pump station operates under permit number NJ0026182. The two combined sewered municipalities are responsible for the operation and maintenance of their respective systems.

6.5.2 Legal Framework

The Camden and Gloucester combined sewer systems are owned and operated by the cities pursuant to Title 40A of New Jersey Statutes (Municipalities and Counties). New Jersey municipalities are authorized and empowered to:

- "...acquire, construct, improve, extend, enlarge or reconstruct and finance sewerage facilities and to operate, manage and control all or part of these facilities and all properties relating thereto..."
- "To issue bonds of the local unit or units to pay all or part of the costs of the purchase, construction, improvement, extension, enlargement or reconstruction of sewerage facilities";
- "To make and enter into all contracts and agreements necessary or incidental to the performance...";
- "To fix and collect rates, fees, rents and other charges..."
- "To prevent toxic pollutants from entering the sewerage system.";
- "To exercise any other powers necessary or incidental to the effectuation of the general purpose of N.J.S.40A:26A-1 et seq."⁶⁻²³

The financial management of the cities' combined sewer systems are regulated under Chapter 4 of Title 40A. Municipalities are required to establish public utility funds to isolate sewer system costs and revenues from the municipal general funds:

"All moneys derived from the operation of publicly owned or operated utility or enterprise and any other moneys applicable to its support, shall be segregated by the local unit and kept in a separate fund which shall be known as "utility fund" and shall bear a further designation identifying the utility or enterprise and, except as provided

⁶⁻²³ N.J.S.40A:26A-1 et seq. Municipal and County Sewerage Act.

in section 40A:4-35, shall be applied only to the payment of the operating and upkeep costs, and the interest and debt redemption charges upon the indebtedness incurred for the creation of such utility or enterprise.”⁶⁻²⁴

The annual budgets for municipal sewerage systems are controlled through the Local Budget Law, codified at N.J.A.40A:4-1 et seq. Annual operating, debt service, revenue and five-year capital improvement budgets are developed using forms and excel templates specified by the New Jersey Department of Community Affairs. The draft budgets are reviewed and approved by the Department prior to final adaption of the budget by the municipalities prior to the start of the fiscal year.

CCMUA owns and operates its regional conveyance interceptor system and the Water Pollution Control Facility # 1 under the New Jersey Municipal and County Utilities Authorities Law.⁶⁻²⁵ Municipal Utility Authorities are empowered to provide water, wastewater, solid waste and hydroelectric power generation and distribution services in a defined service area (district). These services may be provided directly to end-user properties (retail services) or indirectly through service contracts with the municipalities.

CCMUA provides wholesale wastewater conveyance and treatment to Camden, Gloucester and the other municipalities within its service area under the terms of the Service Agreement of December 1986 with its participant municipalities. Under the terms of the Service Agreement the participant municipalities are individually responsible for the operation, maintenance, expansion and replacement of their local collection systems.⁶⁻²⁶ However, CCMUA has the option at its sole discretion but not the obligation to address inflow and infiltration on a regional basis where cost-effective.⁶⁻²⁷ Taken together, these provisions appear to preclude CCMUA from assuming the costs of combined sewer control in Camden or Gloucester beyond those relating to facilities that may provide incidental or equivalent reductions in inflow and infiltration.

Municipal utility authorities have broad powers to acquire, build, own, be the lessor or lessee, operate and maintain wastewater and other public works systems.⁸⁻²⁸ They can finance capital improvements through revenue bonds. With the exception of retail services provided outside of their geographic districts, municipal authorities can set wholesale and retail rates (as applicable) without review by the New Jersey Board of Public Utility Commissioners. The annual budget process for municipal utility authorities is proscribed in the Local Authorities Fiscal Control Law⁶⁻²⁹ and closely parallels that used by municipal governments under the Local Budget Law.

⁶⁻²⁴ N.J.S.40A:4-62

⁶⁻²⁵ N.J.S.40:14B-1 et seq.

⁶⁻²⁶ Section 502 – Operation and Maintenance of the Local Sewerage System

⁶⁻²⁷ Section 503 – Authority’s Option to Correct Infiltration and Inflow.

⁶⁻²⁸ N.J.S.40:14B-20 (Powers)

⁶⁻²⁹ N.J.S.40A:5A-1 et seq.

6.6 Potential Impacts of the COVID-19 Pandemic on Affordability

The projections and conclusions concerning the affordability of the CSO control program proposed in this SIAR by CCMUA, the City of Camden and Gloucester City and their respective financial capabilities to finance the CSO control program are premised on the baseline financial conditions of the three permittees as well as the economic conditions in New Jersey and the United States generally at the time that work on this SIAR commenced. While the impacts of the COVID-19 pandemic on the long-term affordability of the CSO LTCP are obviously still unknown, it is reasonable to expect that there will be potentially significant impacts. There are several dimensions to these potential impacts, including reduced utility revenues and household incomes.

6.6.1 Potential Wastewater Utility Revenue Impacts

This Financial Capability Assessment cannot reflect the currently unknowable impacts on wastewater utility revenues stemming from the national economic upheaval resulting from the COVID-19 pandemic. It is however extremely likely that CCMUA, the two Cities and municipal wastewater utilities in general across the United States will face significant and potentially permanent declines in revenues from households unable to pay their water and sewer bills and the sudden decline in industrial and commercial demands for potable water and wastewater treatment.

On March 20, 2020 the National Association of Clean Water Agencies (NACWA) issued a press release stating that:

“NACWA conservatively estimates the impact to clean water utilities nationwide of lost revenues due to coronavirus at \$12.5 Billion. This is a low-end estimate, assuming an average loss of revenue of 20% which is well within the range of what individual utilities are already projecting. Some utilities are anticipating closer to a 30% or 40% loss in revenue. This estimate is based on the substantial historical utility financial data NACWA has on file through its Financial Survey and recent reports from NACWA members on the decrease in usage they are observing in their systems over the last few weeks.”⁶⁻³⁰

The impact of a 20% to 40% revenue loss, along with increased costs that have been and will continue to be experienced by water and wastewater utilities such as overtime and the writing off of customer accounts receivable could have a profound impact on the affordability of the proposed CSO controls and the ability to finance them.

Most of the costs of a municipal wastewater system are relatively fixed within broad operating ranges. Debt service and other capital costs are fixed once incurred. Some operating costs are somewhat variable with wastewater flows, e.g. chemical and electrical power usage but this variability is lessened by the reality that inflow, infiltration and stormwater flow in a combined system are not affected by billed water consumption. Labor costs are not directly variable, e.g. a twenty percent reduction in billed flow would not result

⁶⁻³⁰ NACWA press release: [Coronavirus Impacting Clean Water Agencies; Local Utilities and Ratepayers Need Assistance](#) March 20, 2020

in a need for twenty percent less labor. Maintenance costs might go down somewhat as equipment operating times may be reduced.

As costs do not decline proportionately to billed flow, it can be expected that user charge rates must be raised to generate sufficient revenue to sustain current operations. The relationship between changes in costs and revenues and the resultant changes in user charge rates is complex and has not yet been fully analyzed. At this point it can be assumed that user rate increases may be necessary to simply maintain current operations, and these rate increases will potentially erode the financial capabilities to fund the CSO LTCP.

6.6.2 Potential Median Household Income Impacts

The impacts of the pandemic on median household incomes in Camden, Gloucester and the entire CCMUA service area cannot be determined at this point. Historical analogies may provide some useful, albeit disturbing, context but are not presented as predictive:

- U.S. median household income fell by 6.2% from \$53,000 in 2007 to \$49,000 in 2010. In New Jersey, the MHI decreased by around 4.0% for the same period.³¹
- The U.S. unemployment rates rose from 5.0% in December of 2007 to 9.9% in December of 2009.³²
- Data on impacts of the Great Depression on median household income are not available. As a proxy, the personal income per capita data are available. For 1929 this was \$700. By 1933 this figure bottomed out at \$376, a decline of 46%. Unemployment for the same period rose from around 3.0% to 25%.³³

While a quantifiable assessment of the impact of the pandemic on median household income is not feasible at this time, reduction in base year MHI can be expected. This will further exacerbate the impacts of the revenue reductions described above on LTCP affordability, as higher base user charge rates will absorb an increased portion of lower MHI.

6.2.3 Implications for the Long Term CSO Control Program

CCMUA, Camden and Gloucester anticipate that the financial implications of the COVID-19 pandemic will be discussed with NJDEP during the review of the SIAR and as the 2021 – 2025 NJPDES permit is developed.

Given the current and likely continuing uncertainties as to the New Jersey and national economic conditions, Permittees will be reticent to commit to long term capital expenditures for CSO controls without the incorporation of adaptive management provisions, including provisions to revise and reschedule the long term CSO controls proposed in this SIAR based on emergent economic conditions beyond the permittees' control. As detailed in Section 8 of this SIAR, these provisions could include scheduling the implementation of specific CSO control measures to occur during the five year NJPDES permit cycles. A revised affordability

³¹ Source: [Fact Sheet: Income and Poverty Across the States, 2010](#) Joint Economic Committee, United States Congress, Senator Robert P. Casey, Jr. Chairman.

³² Source: Bureau of Labor Statistics data series LNS1400000

³³ Source: Federal Reserve Economic Data (FRED) data series: A792RCOA052NBEA

assessment should be performed during review of the next NJPDES permit to identify controls that are financially feasible during that next permit period.

6.7 USEPA Proposed Revisions to the Financial Capability Assessment Process

CCMUA, Camden and Gloucester are aware of these pending changes to EPA's guidance on Financial Capability Assessment (FCA) announced on September 15, 2020. This new guidance is still under review and not yet final, but it is recognized that it may impact the FCA and in turn the LTCP implementation schedule presented in this report. If the final guidance prompts changes to the FCA and the implementation schedule, these elements of this LTCP may be modified and resubmitted to NJDEP for review and approval.

7

Selected Long Term Control Program

7.1 Selected Long Term Control Program Overview

The selected long term control program consists of six program elements that will have phased and overlapping implementation schedules (detailed in Section 8). These six elements are:

1. ***Completion of Projects to Optimize Current Assets*** - Since the submittal of the SIAR in September of 2020 CCMUA completed the capacity expansion of its Delaware Water Pollution Control Facility (WPCF) # 1 to 185 MGD in 2020. The City of Camden has completed the rehabilitation of 28 regulator structures and the upgrading of the Arch Street pump station and is working towards the restoration of the hydraulic capacity of Camden's combined collection sewer system through a comprehensive sewer and outfall cleaning and rehabilitation program. Gloucester City has also been progressing with system-wide collection system and outfall cleaning and as-needed spot repairs.

Additional details as to the status of LTCP related projects identified in the 2020 SIAR are described in the previous sections of this revised SIAR as well as in the joint CCMUA / City of Camden / Gloucester City response to NJDEP's request for information letter of June 12, 2023 provided as Appendix C.

2. ***Efficacy Evaluation*** - The evaluation of the efficacy of these current improvements through comprehensive flow monitoring which will inform the refinement and recalibration of the existing hydrologic / hydraulic model to then current conditions. This will establish a new baseline of overflow statistics informed by the wet weather operating history with these capacity improvements in place. The proposed scheduling for the flow monitoring and model recalibration is provided in Section 8 of this document. Similar evaluations may occur after other improvement project milestones such as the implementation of the formalized green stormwater infrastructure and the street flooding mitigation program elements.
3. ***Formalized Green Stormwater Infrastructure Program*** - Accelerating green stormwater infrastructure through a coordinated, formalized and expanded GSI Implementation Program with the goal of achieving a ten percent reduction in the directly connected impervious areas contributing stormwater runoff to the combined sewer system. GSI efforts since September 2020 are listed in Section 3.5 of this revised SIAR and in Attachment 1 to Appendix C.
4. ***Street Flooding Mitigation Program*** - The development and rapid implementation of a comprehensive Street Flooding Mitigation Program will be developed within the City of Camden to provide an empirical understanding of the frequency, location and extent of street flooding remaining after the Camden sewer system is cleaned. This will serve as the basis for short and long term operational and capital improvements. Subsequent to the submittal of the SIAR, CCMUA and the City of Camden have been

working with the Drexel University School of Engineering on flood sensors and reporting technologies in East Camden areas currently prone to street flooding. Moreover, through the paralleling efforts of sewer and outfall cleaning and the expansion of treatment capacity at CCMUA's WPCF #1, reductions in incidences of street flooding have been noted along the Delaware River. Street flooding mitigation efforts since September 2020 are listed in Section 4.4 of this revised SIAR and in Attachment 1 to Appendix C.

5. **Cooper River Water Quality Optimization Program** – The Cooper River is an important environmental, recreational and economic asset for the City of Camden's economic redevelopment. Eliminating Camden's CSOs from the Cooper River is not financially feasible and would not result in water quality compliance. CCMUA and the City of Camden are committing to work with the other Cooper River municipalities, stakeholders and NJDEP to develop a **Cooper River Water Quality Optimization Strategy** during the first NJPDES permit cycle after this SIAR is approved. As detailed in Section 7.6, the CCMUA has developed an initial sampling program for the summer of 2023 to evaluate sampling access sites and to start developing contemporary data. Results for Cooper River sampling conducted during the summer of 2023 are provided in Section 7.6.
6. **Additional Structural Controls** – Within the limitations imposed by affordability constraints, structural controls in each of the five sub-systems that will raise the level of CSO capture in each sub-system and system-wide to no less than 85% of wet weather flows during the Typical Year.

Due to the extremely limited affordability and financial capabilities of the Cities of Camden and Gloucester, as demonstrated in Section 6, these controls will require significant external funding and will likely need to be implemented over the course of several NJPDES permit cycles.

Each of these program elements are described in further detail in Sub-section 7.2 – 7.7. The anticipated cumulative CSO control performance as the program is implemented is shown on Table 7-1.

Table 7-1 – Project Cumulative CSO Control Levels as the Program is Implemented

Program Element		System Wide	Delaware River - Camden	Delaware River- Gloucester	Delaware River – Back Channel	Cooper River	Newton Creek
Baseline	Baseline Conditions						
	Percent Capture	69%	71%	69%	69%	69%	79%
	Overflow Volume (MGY)	822.9	404.7	75.8	140.2	170.5	31.7
	Modeled Street Flooding (MGY)	79.7	52.3	6.5	1.9	8.7	10.4

Program Element		System Wide	Delaware River - Camden	Delaware River- Gloucester	Delaware River – Back Channel	Cooper River	Newton Creek
Program Element 1	System Optimization - Completion of Current Projects						
	Percent Capture	78%	89%	69%	69%	70%	85%
	Overflow Volume (MGY)	579.9	167.3	75.3	142.0	170.4	24.8
	Modeled Street Flooding	33.0	13.8	6.4	0.6	6.9	5.2
Program Element 2	Efficacy Evaluation	This program element will evaluate the levels of control achieved after the completion program elements 1 and may also be conducted as needed after program elements 3 and 5.					
Program Element 3	Formalized Green Stormwater Infrastructure Program (results of 10% DCIA reduction)						
	Percent Capture	81%	91%	74%	72%	75%	87%
	Overflow Volume (MGY)	487.0	135.3	63.9	125.3	141.5	20.9
	Modeled Street Flooding	24.4	10.3	4.7	0.3	4.9	4.2
Program Element 4	Street Flooding Mitigation Program	The CSO control impacts of the street flooding mitigation cannot be quantified prior to its development and implementation.					
Program Element 5	Cooper River Regional Water Quality Optimization Strategy	This program element will not directly impact CSO overflow levels. It will identify steps that CCMUA, Camden, NJDEP and the other Cooper River municipalities can take to improve water quality and enhance safe recreational use of the Cooper River.					
Program Element 6	Additional Structural Controls (statistics are for satellite storage for Del-GL and Cooper)						
	Percent Capture	86%	91%	85%	85%	85%	87%
	Overflow Volume (MGY)	341.5	135.3	35.2	68.0	82.2	20.9
	Modeled Street Flooding	<24.4	<10.3	<4.7	<0.3	<4.9	<4.2

7.2 Program Element 1 – Completion of Current Projects

7.2.1 Treatment Plant Capacity Expansion

In 2016 CCMUA proactively undertook the expansion of treatment capacity at its Delaware Water Pollution Control Facility No. 1 from 150 MGD to 185 MGD and completed the project in 2020. Improvements included:

- ***Influent Pump Upgrades*** – CCMUA has completed a major capacity expansion of its influent pumping capacities including upgrading two of the four pumps from 45 MGD to 60 MGD, resulting in a firm pumping capacity of 180 MGD with one pump out of service and a total pumping capacity of 240 MGD. Improvements also include new high efficiency variable frequency drive motors and related upgrades to the power distribution equipment.
- ***Process Train Hydraulic Improvements*** – CCMUA has reduced hydraulic bottlenecks in the primary sedimentation tankage piping and channels to enable full treatment of up to 185 MGD.

Statistics documenting the benefits of these plant capacity improvements on peak flow rates into the plant are detailed in Section 2.4 of this revised SIAR.

7.2.2 Hydraulic Capacity Restoration

City of Camden

The City of Camden is currently undertaking a number of projects intended to restore and optimize the use of the design hydraulic capacities of its collection system:

- ***Collection System Cleaning and Spot Repairs*** – Through its collection system contract operator, American Water Operations & Maintenance LLC, Camden has embarked on a multi-year project to address deferred cleaning and to make spot repairs within its collection system. It is anticipated that this remedial system-wide cleaning will be completed in 2024. Statistics related to Camden’s cleaning activities are provided in Appendix C of this revised SIAR. Maps showing areas cleaned are provided in Appendix D.
- ***Regulator Rehabilitation*** – The City of Camden undertook a comprehensive system-wide inspection of its regulator structures which determined that the regulator mechanisms required extensive repairs. Repairs have been prioritized for the regulator mechanisms for Camden regulators C-1 through C-9, thereby enabling the control of flows into the Camden interceptors. Flows from the other Camden regulators can be controlled through the Arch Street, Pine Street and Baldwin’s Run pump stations and through a control gate immediately upstream of the treatment plant, eliminating the need for the regulator controls. To maintain maximum flexibility should the need arise in the future to re-use these regulators as a part of flood prevention, the deteriorated mechanisms will be removed, and their anchor systems replaced with stainless steel plates. Camden completed the rehabilitation of its 28 regulators in 2022.
- ***Overflow Outfall Cleaning*** - Concurrent with its regulator rehabilitation project, Camden is addressing blockages that it has identified at some of the CSO outfalls. Dredging is required to remove and clear these blockages. The City of Camden has been working closely with CCMUA and NJDEP to complete this program as expeditiously as possible. Two projects were developed with CCMUA currently working on the most critical nine of these outfalls and a second project by the City to

clear the remainder of the outfalls. As of September, 2023 the outfall cleaning was estimated to be approximately 90% complete with completion anticipated in 2023.

- ***Arch Street Lift Station Upgrades*** – Camden and CCMUA have upgraded the capacity of the Arch Street Lift Station by replacing the three existing 75 horsepower motors with new 100 horsepower motors and replacing the three existing 22.25" impellers with 24.25" impellers.
- ***Institutionalization of Green Stormwater Practices for Redevelopment*** – the stormwater control ordinance Article III (725-12 through 725-22) is applicable to any site plan or subdivision that requires preliminary or final site plan approval. Section 725-14 of Camden's stormwater control ordinance requires that "to the maximum extent practicable, the (stormwater quantity and quality) standards ... shall be met by incorporating nonstructural stormwater management strategies...into the design of the project" (725-14.E).

Gloucester City

Approximately 18 miles of sewer were cleaned and jetted between 2021 and May of 2023 out of a total of 39 miles of sewers. Gloucester City anticipates that the system-wide cleaning will be completed within 2023. A map showing the extent of the system cleaning is provided as Attachment D to Appendix D of this revised SIAR. As a result of regular inspections of Gloucester's seven regulator structures the need for remedial cleaning of regulator G-1 was identified and completed in May of 2023, resulting in a significant reduction in street flooding. In August of 2023 CCMUA conducted an inspection of the Gloucester regulator and outfall structures and identified outfall structures with obstructions. These are expected to be cleaned in 2025 and into 2026 based on planning, design and permitting work to be completed in 2024. A copy of the 2023 outfall and regulator inspection report is provided as Attachment E to Appendix D.

As shown in Table 7-1, with the expansion of CCMUA's treatment capacity to 185 MGD and the restoration of the Camden and Gloucester collection systems' hydraulic capacity, the annual overflow volumes are projected to decrease from 823 to 582 MGY and the system-wide capture rate increase from 69% to 78%. In addition, the volume of modeled surface flooding would be reduced by roughly 50% from 80 million gallons to 33 million gallons in the Typical Year. The projected capital costs for these current wet weather control related projects total roughly \$47 million as shown on Table 7-2. These figures do not include the investments by the Cities and CCMUA for green infrastructure to date.

Table 7-2 – Ongoing Wet Weather Control Capital Investments (as of the 2020 SIAR)n

Current Control Project	Capital Costs (\$ millions)
CCMUA – Expansion of WPCF # 1 to 185 MGD	
Influent Pump Upgrades	\$10.1
Wet Weather Improvements	\$3.8

Current Control Project	Capital Costs (\$ millions)
Influent Junction Separation	\$8.0
Subtotal CCMUA	\$21.9
City of Camden	
Collection System Cleaning (estimated, ongoing)	\$12.0
Regulator Improvements	\$5.4
Outfall Dredging	\$5.2
Arch Street Lift Station Upgrade	\$2.1
Subtotal Camden	\$24.7
Grand Total	\$46.6

7.3 Program Element 2 – Iterative Efficacy Evaluation

The second element of the long term control program will be iterative flow monitoring and recalibration of the hydrologic / hydraulic model to reflect changing conditions. The first round of flow monitoring will occur after the completion of the initial cleaning of the Camden and Gloucester collection system and outfalls. This flow monitoring will occur in 2025 and as needed into 2026. By that time, CCMUA will have accumulated operating experience with the WPCF capacity at 185 MGD which will enable the model to be updated in 2026 to reflect CCMUA's system control rules and understanding of the wet weather behavior of the three trunk lines going into the plant. It is anticipated that an efficacy evaluation will be repeated after other milestones such as the formalized GSI, and the street flooding mitigation efforts once these programs have been implemented for a period sufficient to determine how much GSI is likely to be accomplished over a reasonable planning horizon.

7.4 Program Element 3 – Formalized Green Stormwater Infrastructure Program

As detailed in Section 3, CCMUA and the Cities of Camden and Gloucester are targeting a 10% or around a 145 acre reduction in impervious areas that are directly connected to the combined sewer system (DCIA) through the installation of GSI. CCMUA and the Cities are proposing the establishment of a framework for the implementation of GSI that would formalize, expand upon and support the current efforts of groups such as the Camden SMART initiative. The framework is targeted for completion during the first permit cycle, with work to commence upon NJDEP approval of this SIAR. The framework will include specific performance targets for GSI implementation, e.g., 30 acres per five year NJPDES permit cycles.

Since 2017, projects capturing stormwater flows from approximately 29 acres have been constructed or are in planning or design phases. The project locations and sizes are described in Section 3.5 and in Attachment 1 to Appendix C of this revised SIAR.

7.5 Program Element 4 – Street Flooding Mitigation Program

The fourth Long Term Control Program element will be the implementation of a Comprehensive Street Flooding Mitigation Program as detailed in Section 4 of this document. The objective is to establish a framework for a comprehensive program to understand, reduce the occurrences of, and mitigate the impacts of street flooding. The program will establish the empirical basis for street flooding mitigation and assign responsibilities for the prevention of and response to street flooding events. It is anticipated that a detailed program plan will be completed early in the initial (2021 – 2026) NJPDES permit cycle following the approval of this SIAR. Steps taken to mitigate street flooding since the September 2020 submission of the SIAR to NJDEP were described in Section 4.4 of this revised SIAR.

7.6 Program Element 5 – Cooper River Regional Water Quality Optimization Strategy

The fifth Long Term Control element will be the development of a regional strategy to optimize water quality in the Cooper River. This strategy will take a watershed-based approach to reducing the discharge of pathogens and other pollutants into the Cooper River that degrade it's recreational and economic redevelopment usage as well as its aquatic habitat. Pending refinement by stakeholders, two preliminary goals are identified:

- Achieving water quality standards for pathogens during dry weather; and
- Reducing wet weather impacts, including recovery time.

The intent of the strategy is to identify *what, how, and who* – is needed to achieve these goals. It will be developed during the first NJPDE permit cycle following the approval of this SIAR (2024-2028). A stakeholders' working group (may be derived from existing groups and interested parties). Anticipated initial activities could include:

1. Compilation and review of existing data and planning efforts such as the Tri-County Water Quality Management Plan, the circa 2003 TMDL for fecal coliform in Watershed Management Area 18, the most recent NJDEP Section 303 Integrated WQ Report, current NJPDES MS4 stormwater permits, development and land use plans for the 40 square mile Cooper River watershed.
2. Development of Cooper River recreational usage policies and best practices e.g.:
 - o Determine the need for and implementation as warranted a post-wet weather sampling program to determine when pathogen levels in the river meet state standards for recreational secondary (e.g., boating) or primary (e.g., swimming) contact.
 - o Develop and implement a public notification program using the internet, call-in and/or visual notification (e.g., orange "CSO" flags flown at marina's in Pittsburgh during and after CSO events).

3. Identify opportunities to support and expand recreational usage of the Cooper River and stewardship of its aquatic habitat as a critical local environmental resource and as a catalyst for economic growth and community revitalization.
4. Identify and support opportunities for funding and cooperation with other groups and agencies for riparian improvements, e.g., multi-purpose stream bank stabilization with recreational trails, invasive species control and habitat enhancement and restoration, etc.
5. Identify and support feasible and implementable green stormwater management, other source reduction and modifications as appropriate of municipal and county land use and redevelopment regulations and policies that enhance compliance with MS-4 requirements and reduce the impacts of non-point source runoff.

As a proactive step in developing a Cooper River water quality optimization strategy CCMUA developed an initial sampling program for the summer of 2023 to evaluate sampling access sites and to start developing contemporary data. Six sampling locations were selected for 2023 with five along Cooper River and one on the back channel of the Delaware River:

- USGS 01467190 (Rt 130 bridge) – just upstream of tidal boundary
- USGS 01467150 (Kings Highway, Haddonfield) – HUC boundary of South Branch
- NJDEP_BFBM-ANO188 (Park Blvd, Cherry Hill) – HUC boundary of North Branch
- 31DELRBC_WQX-CooperRiver at Cuthbert Blvd (Cherry Hill) – nontidal, upstream of Rt 130
- 31DELRBC_WQX-CooperRiver near mouth (State St, Camden) – CSO area
- DRBC-DRLE-9904 - back channel

The approximate locations of the sampling sites are shown on Figure 7-1.

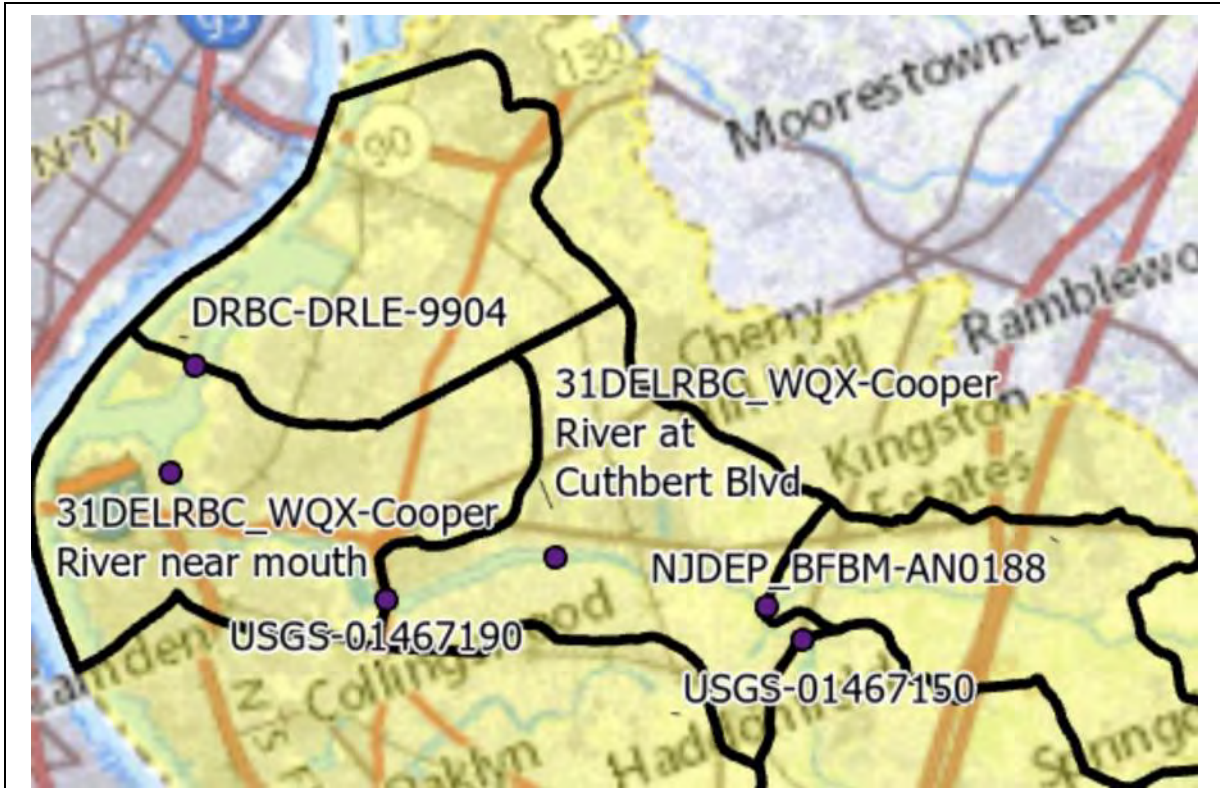


Figure 7-1 – 2023 Cooper River Water Quality Sampling Locations

The sample location in the back channel of the Delaware River proved inaccessible and not sampled in 2023. Of the five Cooper River sampling locations, one is subject to influence from combined sewer overflows. The remaining sites are located upstream of the CSO outfalls and isolated from CSO discharge by the dam just upstream of Kaighn Avenue forming Cooper River Lake. An example of the data for E. coli from early summer of 2023 is provided on Table 7-3.

Table 7-3 – Initial 2023 Cooper River Sampling Data

Sampling Location	CSO Influence ?	E Coli WQS Violated?			Sampling Dates							
		Single Sample > 235 colonies / 100 ml	Geometric Means		5/3/23	5/18/23	5/25/23	6/1/23	6/7/23	6/15/23	6/20/23	6/29/23
			Value	Exceed 126 col./ml?								
State Street Bridge	Yes	5	513	yes		162	214	115	2,420	866	387	613
Route 130 Bridge	No	4	210	yes		125	236	20	167	345	133	345
Cuthbert Blvd. Bridge	No	8	1,742	yes		1,050	2,420	1,550	980	1,550	2,420	2,420
Park Blvd.	No	4	314	yes		199	308	153	326	613	1,410	173
King's Highway	No	8	1,076	yes	517	517	2,420		727	1,120	816	1,300

As shown on Table 7-3, the E.-coli water quality standard of 235 CFU/ 100 ml for single samples and of 126 CFU/100 ml for the geometric means were exceeded in all of the locations

upstream of CSO influence during dry weather sampling events. More detailed data analysis will be performed and documented in later reports as more data is collected during future permit cycles.

7.7 Program Element 6 – Sub-System Additional Structural Controls to Achieve 85% Capture

Based on the results of the post-cleaning flow monitoring and modeling, CCMUA and the Cities will update the structural controls alternatives analysis to determine additional controls needed to achieve 85% typical year wet weather capture. This is anticipated to occur in the 2027 – 2028 time frame. The updated alternatives analysis will also provide a more accurate projection of long term implementation scheduling. CCMUA's and the Cities' best projections and commitments based on understandings as of 2023 are detailed in Section 8.

Subject to changing conditions and understanding, e.g., as a result of flow monitoring and model updates under program element 2, as of September 2020 CCMUA and the Cities of Camden and Gloucester propose the following suite of structural controls that along with the 10% GSI will achieve the 85% wet weather capture during the Typical Year control performance goal.

- **Delaware River – Camden:** CCMUA will undertake modifications to the C-3 regulator structure and implement revised wet weather operating procedures. These, coupled with the completion of the capacity expansion at WPCF # 1 to 185 MGD will enable 85% capture from the Delaware River – Camden sub-system.
- **Delaware River – Gloucester:** A satellite control facility will be installed to capture overflows from the G-4, G-5, and G-1 regulators. This could be either a 1.1 million gallon storage tank or a 6.4 MGD high rate wet weather treatment facility that would provide at least the equivalent of primary treatment as well as for disinfection and dechlorination (as necessary depending on the disinfection approach selected).
- **Cooper River:** Satellite control facilities will be installed in two locations. One facility will capture flows from Camden regulators C-22 and C-22A and have either a storage capacity of 1.3 million gallons or a 20 MGD treatment capacity. It is anticipated that the location will be adjacent to or in the vicinity of Camden's Federal Street pump station. The second facility will capture flows from Camden's C-27 regulator and from the Thorndyke Street outfall, which receives flows from several upstream regulators. This facility would have a storage capacity of 3.0 million gallons or a treatment capacity of 20.4 MGD located near the Thorndyke outfall.
- **Delaware River Back Channel:** The 85% control target will be achieved in the Delaware River Back Channel through two projects. First, the combined sewer flows that are currently discharged from the Pennsauken Township sewer system into the Camden combined system will be re-routed for discharge to the Delaware River back channel after treatment and disinfection. The second component of the Delaware Back Channel controls will be the modification and reconfigurations of regulator structures and power supplies associated with the Baldwins Run pump station to enable full utilization of its 25 MGD capacity.

Design work for the separation of combined sewer areas of Pennsauken Township is complete and pending construction permit approval. CCMUA is currently evaluating options for the conveyance of the separated Pennsauken stormwater for discharge to Delaware River back channel through or adjacent to CCMUA's C-32 outfall structure. This conveyance strategy may involve targeted sewer separation in Camden neighborhoods adjacent to Pennsauken or a dedicated stormwater line for the removed Pennsauken stormwater. In either case, CCMUA is studying the optimization of stormwater inlet placement and configuration to mitigate street flooding in East Camden.

- Potential Further Expansion of CCMUA's WPCF #1 Wet Weather Treatment Capacity:** As detailed in Section 2 of this SIAR; CCMUA has evaluated the potential to expand the wet weather treatment capacity of its WPCF up to 220 MGD as determined necessary in the future. Expansion of the plant wet weather capacity to 220 MGD was determined to be not necessary or cost effective to meet the 85% system-wide typical year capture target however in the 2020 SIAR. If warranted, this option could be re-examined during the updating of the structural controls analysis anticipated in the 2027-2028 timeframe.

CCMUA and the Cities recommend against the selection between satellite storage and treatment at this time. As will be detailed in Section 8 (Implementation), the proposed structural controls outlined above are proposed not to occur until after the results of program elements one through four are mostly implemented and their impacts on CSO evaluated through flow monitoring and modeling. Moreover, additional advancements in wet weather treatment and storage technologies are likely to occur. In addition, water quality standards or other regulatory requirements may change, e.g., as a result of DRBC's current water quality monitoring efforts.

Another reason to defer a decision on the satellite control technology is uncertainty as to the feasibility of reaching the 10% DCIA reduction target. The targeted 10% reduction in DCIA is aggressive and unlike structural controls such as satellite storage or treatment, the implementation of green infrastructure, the timing and scope of green stormwater projects are not completely under the control of the Cities.

Should the 10% DCIA goal prove to be unachievable in a regulatorily acceptable time-frame, the capacities of the satellite treatment facilities described in Section 5 that are anticipated to be necessary to achieve 85% system-wide wet weather capture would be upsized. The estimated revised facility sizes required with a zero percent reduction in DCIA are shown on Table 7-4 to bracket the sizes needed.

Table 7-4 – Control Facility Sizing Implications of Zero DCIA Reduction

Sub-System	Locations	Required Capacities			
		Storage (MGY)		Treatment (MGD)	
		0% DCIA Reduction	10% DCIA Reduction	0% DCIA Reduction	10% DCIA Reduction
Delaware River – Gloucester	G-4 / G-5	0.6	1.2	4.1	6.8
	G-1	0.5	0.7	2.3	4.4
Cooper River	C-22 / C-22A	1.3	2.6	20	21

Sub-System	Locations	Required Capacities			
		Storage (MGY)		Treatment (MGD)	
		0% DCIA Reduction	10% DCIA Reduction	0% DCIA Reduction	10% DCIA Reduction
Newton Creek	C-27 / Thorndyke	3	3.5	20.4	38.5
	C-17	NA	0.4	NA	4.8

The final size requirements of satellite facilities will be finalized after the GSI Implementation Program has been implemented long enough to determine the level of GSI that is achievable and the system performance with the green and other improvements has been quantified through future flow monitoring and modeling.

7.8 Implications of the Financial Capability Assessment

7.8.1 Problem Statement

NOTE: CCMUA and the Cities will update the financial and institutional capability assessments detailed in Section 6 of this SIAR Update as a part of the updated alternatives analyses.

The long term CSO control planning process set forth in the NJPDES permits is based on the logical progression from system characterization to a broad evaluation of control alternatives to the selection of the optimal control strategy for a given permittee. Included in this process is a consideration of the impacts of the long term controls on ratepayer affordability and on the permittee's financial capability to finance the controls. Per the USEPA CSO Control Policy, these financial factors serve to inform the setting of the implementation schedule for the long term controls.

The logic of the long term control planning process is challenged when as documented in Section 6, the affordability of CSO controls for Camden and Gloucester is extremely limited. As shown on Table 7-5, there is a huge gap between the estimated costs of the selected long term control program and the economic and financial resources of the residents and municipal governments of Camden and Gloucester.

Table 7- 5 – Financial Capability and Control Program Capital Costs

Item	Permittee	
	Camden	Gloucester
<i>Future Capital Costs Triggering a 2.0% Residential Indicator in 2042 (\$ millions)</i>		
With Inflation	\$0.0	\$1.7
Without Inflation	\$30.0	\$12.5
<i>Estimated Total Capital Costs of 85% Capture Long Term Program by Permittee (in 2019 dollars)</i>		
Least Cost	\$101.9	\$27.1
Most Cost	\$129.6	\$44.8

Item	Permittee	
	Camden	Gloucester
Projected Residential Indicator After Full Implementation in 2042^a		
	With Inflation	
Least Cost	4.8%	4.0%
Most Cost	5.0%	4.7%
	Without Inflation	
Least Cost	2.5%	3.0%
Most Cost	2.6%	3.7%

^a 2042 is used for example only. It is based on the approval of the SIAR in 2021 and implementation of the long term control program through 2041. These dates may not be appropriate for Camden and Gloucester.

As shown on Table 7-5 the least capital cost option for Camden is \$101.9 million while the amount of future capital costs causing the residential indicator to exceed the USEPA 2.0% high burden trigger is \$30 million assuming no inflation while the figures for Gloucester are \$12.5 million in current dollars.

7.8.2 Impacts of Inflation

The 1997 USEPA guidance document on affordability and financial capability assessment does not account for inflation beyond bringing older cost or income data to the current year. This simplification eliminates the need to project economic trends such as household income or construction costs. However, if the potential effects of inflation are not considered, the affordability of long term CSO controls can be overstated. Nationally, the growth in the cost of wastewater services have outpaced the growth in household incomes. A comparison of national cost trends and the growth in household incomes for Camden and Gloucester for the period of 1999 through 2013 is shown on Figure 7-2.

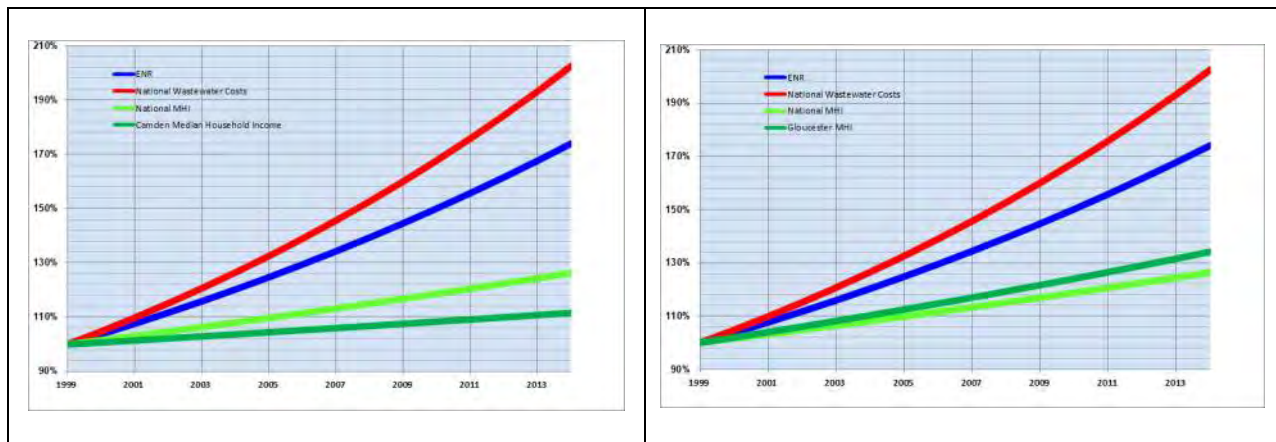


Figure 7-42– Comparison of Rates of Growth of Wastewater System Costs Nationally with Growth in Camden's (left) and Gloucester's (right) Median Household Income. [sources: NACWA, US Census]

The graphs demonstrate the potential erosion in affordability if the growth of costs is greater than the growth in household incomes. If inflation is considered in projecting affordability, the \$30 million new capital expenditure figure that causes Camden's residential indicator to

cross the 2.0% high burden threshold disappears. Based on the historically based inflation rates used in the affordability model, Camden’s residential indicator is projected to rise to 3.55% with no new capital expenditures through 2041. Projected inflation erodes the \$12 million new capital trigger for Gloucester down to \$1.7 million.

Obviously, the future rates of inflation cannot be known. Therefore, the scope and schedule for implementing the long term control program outlined above will need to be based on iterative re-evaluations of affordability and financial capability under the adaptive management process detailed in Section 8 of this document. This adaptive management strategy will include empirical triggers for reconsidering the type, scale and scheduling of control elements within the context of interim targets to be established in future NJPDES permits.

7.8.3 Alternative Implementation Schedules

The base case affordability / financial capability assessment assumes a 22 year implementation schedule based on the durations for facilities planning, design and construction shown in Table 7-6.

Table 7-6 – Base Case Implementation Schedule for Affordability and Financial Capability

Start Date	2021
Facilities Planning	1
Design & Permitting	3
Construction	<u>17</u>
Total Years to Implement LTCP (inclusive)	21

The assumed start date is based on the submittal and approval of the SIAR in 2020 and coincides with the effective date of the next NJPDES permit. The impacts of extending this implementation period has been evaluated. The impacts of extending the implementation schedule on the residential indicators depend on whether or not inflation is considered as shown in Table 7-7.

Table 7-7 – Impacts of Implementation Scheduling on the Residential Indicators

Implementation Duration in Years	Camden Residential Indicator		Gloucester Residential Indicator	
	With Inflation	Without Inflation	With Inflation	Without Inflation
22	4.8%	2.5%	4.0%	3.0%
32	6.0%	2.7%	4.2%	2.2%
42	7.2%	2.2%	4.1%	2.1%

If as is assumed in the base-case affordability model that costs will continue to outpace income growth, affordability decreases as the implementation period is extended. If inflation is not included in the analysis, extending the implementation period does improve affordability, however even with an implementation period extending more than forty years, the residential indicators for both Camden and Gloucester are projected to remain well over the 2.0% high burden threshold.

7.8.4 Annual Pay-as-You-Go Funding

The amounts that each city could spend on an annual basis without causing their respective residential indicators to exceed 2.0% have also been calculated and are shown on Table 7-8.

Table 7-8 – Maximum Annual Expenditures Without Trigger a 2.0% Residential Indicator

Implementation Duration in Years	Camden		Gloucester Residential Indicator	
	With Inflation	Without Inflation	With Inflation	Without Inflation
22	None	~\$1.0 million	\$80,000	\$530,000
32	None		None	
42	None		None	

7.8.5 External Funding Needs

As documented above, the least capital cost of 85% wet weather flow capture control options would result in residential indicators of well over the 2.0% high burden threshold with or without factoring in inflation. Conversely, put on an annual expenditure basis, Camden and Gloucester could only afford around \$1.0 million and \$530,000 respectively before triggering the high burden. Moreover, increasing the implementation schedule out past 2060 would not resolve the affordability problem even at zero inflation. In addition, the amounts of capital expenditures that could be incurred by the two cities include necessary renewal, replacement and other non-CSO control project costs.

A meaningful CSO control program is not feasible for Camden or for Gloucester without either a significant reduction in capital costs through the reduction in the targeted level of controls or through external funding that would effectively reduce the capital expenditures by the two cities. It has been demonstrated in Section 5.4 (cost and performance considerations) that a Presumption based control strategy targeting 85% control of Typical Year wet weather is the lest-cost path towards compliance with the performance metrics in the CSO Policy and in the NJPDES permits. Therefore, the path forward must include significant external funding through the State of New Jersey or through a yet to be promulgated federal funding program. Shown on Table 7-9 are the impacts of various levels of external capital funding and/or capital cost reduction on the residential indicators over a twenty-two and thirty-two year implementation schedule.

Table 7-9 – External Funding and/or Capital Cost Reduction Impacts on Residential Indicators

Grant / Capital Cost Reduction	Camden Residential Indicator				Gloucester Residential Indicator			
	With Inflation		Without Inflation		With Inflation		Without Inflation	
	22 Years	32 Years	22 Years	32 Years	22 Years	32 Years	22 Years	32 Years
0%	4.9	6.0	2.5	2.3	4.0	4.2	3.0	2.2
25%	3.8	5.8	2.3	2.2	3.6	3.9	2.5	2.0
50%	4.2	5.4	2.2	2.0	3.2	3.6	2.2	1.8
75%	3.8	5.1	2.0	1.9	2.8	3.3	1.8	1.7
100%	3.6	4.9	1.9	1.9	2.4	3.0	1.6	1.6

The combinations of implementation schedule and external funding or cost reductions that would result in a projected residential indicator of 2.0% or less are highlighted in green.

No combinations of schedule and funding work if inflation is included. Camden's program could be workable from an affordability standpoint with either a 22 year or 32 year implementation schedule and funding of 75% or more of the capital costs. For Gloucester's program to be considered as affordable over a 22 year schedule, funding of around 60% would be required. If the Gloucester implementation period were extended to 32 years, 25% or greater funding would result in the residential indicator not exceeding 2.0%

The examples shown in this section and in the entire SIAR are the results of the myriad assumptions and estimations used in the development of control program costs and future economic conditions. These will change and be refined as the long term control program moves into implementation; but as presented are sufficiently accurate to form the basis for the development of a regulatory compliance strategy moving forward.

7.9 Construction and Financing Schedule

Paragraph G-8(a) of the NJPDES permits requires the submittal of a Construction and Financing Schedule as an early long term control program deliverable to NJDEP. Due to the financial constraints facing Camden and Gloucester the scope of this document will need to be broadened into a comprehensive program financing and funding strategy that addresses from a financial perspective *what is doable and when?* While Section 8 of this revised SIAR includes a general design and construction schedule for structural controls, **CCMUA and the Cities will prepare a detailed construction and design schedule as a part of the updated evaluation of structural alternatives for submission to NJDEP no later than six months before the end of the forthcoming five year (2024 – 2028) NJPDES permit cycle.**

Developing a workable funding strategy will require a partnership between the two Cities, CCMUA, NJDEP and likely other state and regional agencies such as the New Jersey Department of Community Affairs and Department of Transportations. Allied and related agencies such as Camden County will likely also play a role; the former in leveraging County road and highway projects to support green stormwater infrastructure or sewer line renewal and replacement coincident with road work.

State Programs beyond the New Jersey Clean Water Revolving Loan Program that target low income areas, transportation or economic redevelopment potentially could be leveraged with specific CSO projects, e.g., coordinating local sewer separation with the water and sewerage needs of a redevelopment or roadwork project. In addition, new state legislation and appropriations actions may be required by the State Legislature. These could be pursued with and through NJDEP and the other New Jersey combined sewered municipalities and authorities.

Current federal funding for public water and wastewater systems is limited pending new Congressional action on infrastructure programs. Existing programs such as the Water Infrastructure Finance and Innovations Act (WIFIA) – which provides loans from the US Treasury Department (Administered by USEPA) are likely of limited applicability to Camden and Gloucester. In the past Congressional appropriations to the US Army Corps of Engineers Civil Works funding through Sections 219 and 206 of the Water Resources Development Act have been used successfully in other regions

towards CSO control funding.

While current federal funding is not robust, long term consideration could be given towards crafting new pushes for federal assistances if conditions appear to be propitious. Previous successful examples include Rouge River Program in the Detroit area and the 3 Rivers Wet Weather Program (Pittsburgh) which together channeled more than \$300 million in federal funding towards municipal wet weather and CSO control projects.

The Construction and Financing Schedule and all aspects of the long term control program implementation will incorporate adaptive management as described more fully in Section 8 of this document. As detailed in Section 8, CCMUA and the Cities propose that the implementation schedule for the CSO control program be synchronized with the five year NJPDES permit cycles. Specific enforceable CSO control program targets will be negotiated during the NJPDES renewal process. These targets will be subject to revision due to forces beyond the control of CCMUA and the Cities including but not limited to natural disasters (e.g., hurricane), pandemics or other disasters along with resultant severe economic downturns which disrupt the revenues available to the three permittees or the abilities of the rate payers to pay their sewer bills. It is proposed that the Construction and Financing Schedule include specific metrics defining triggering events.

A key component of adaptive management will be the inclusion of an affordability and financial capability trigger in the Construction and Financing Schedule. The projects and activities to be included in each five-year permit cycle would be selected and scheduled such that the residential indicator in either City and in the CCMUA service area not exceed the 2.0% of median household income triggering the USEPA high burden definition. Should economic or other conditions occur such that the residential indicators exceed 2.0% during a permit cycle or lead to reasonable expectations that the 2.0% value be exceeded in subsequent permit cycles the projects and activities in subsequent permit cycles will be modified in cooperation with NJDEP.

8

Section 8 Implementation Schedule & Adaptive Management Revised September 2023

8.1 Implementation Scheduling Context

The implementation of CSO controls by CCMUA, the City of Camden and Gloucester City will require a long term commitment of scarce financial resources. The reduction of CSOs also presents an intergenerational opportunity to serve as a catalyst for sustainable redevelopment and growth in Camden and Gloucester.

The implementation scheduling strategy proposed in this SIAR has been informed by the following:

- CCMUA and the Cities already completed key projects focusing on projects that will provide significant near-term overflow and street flooding benefits such as the expansion of the WPCF # 1, upgrading the capacity of the Arch Street pump station and regulator rehabilitation by the City of Camden and substantial progress towards the cleaning of the Camden and Gloucester City collection systems and outfalls.
- Upon the completion of remedial system cleaning by the City of Camden and Gloucester City; CCMUA will undertake a comprehensive flow monitoring program and recalibration of the hydrologic / hydraulic model to establish a contemporary baseline of system performance (2025 – 2026).
- During the 2024 – 2028 NJPDES cycle, the recalibrated model will then be used for an updated evaluation of alternatives to define the types, locations, and design standards for additional CSO controls needed to achieve 85% system-wide capture for the Typical Year. This evaluation will include an updated financial capability assessment and the proposed Construction and Financing Schedule for NJDEP approval and implementation in subsequent five-year permit cycles.
- The projected costs to fully implement the CSO control strategy are far greater than the financial resources currently available to the Cities of Camden and Gloucester ; and
- The complete implementation of the CSO control strategy presented in this SIAR will span multiple five-year NPDES permit cycles; and will be implemented in the midst of climate and other changes and uncertainties. Therefore, ongoing performance monitoring and adaptive management will be required to adjust the control program to match changing conditions.

8.2 Proposed Implementation Schedule

The implementation schedule will synchronize projects, milestones and activities to coincide with the five year NJPDES permit cycles. In brief it includes:

First Five Year Permit Cycle (2024 – 2028)

1. Gloucester sewer cleaning completion by 12/31/23
2. Camden sewer cleaning completion in 2024

3. Gloucester outfall cleaning completion in 2025 or early 2026 (dependent on aquatic species protection requirements)
4. Flow monitoring of entire CCMUA, Camden Gloucester system (dependent on cleaning and weather conditions, anticipate spring and fall of 2025 or spring of 2026 as needed for adequate data).
5. Formalize Green Stormwater Infrastructure Program by 12/31/25 – implementation ongoing thereafter.
6. Formalize Street Flooding Mitigation Program by 12/31/25 – implementation ongoing thereafter.
7. Continue Cooper River water quality monitoring and develop a Cooper River Water Quality Strategy - through June 2028.
8. Update the hydrologic/hydraulic model – 2026.
9. Updated evaluation of structural control alternatives along with the proposed Construction and Financial Schedule and the updated FCA to be completed and submitted to NJDEP no later than June 30, 2028.

Second and Third Permit Cycles (2029 – 2033 and 2034 – 2038)

10. Planning, design, permitting, land acquisition, etc. – (NJPDES Cycle 2: 2029 – 2033)
11. Construction of additional structural controls – (NJPDES Cycle 3: 2034 – 2038)
12. Ongoing implementation of GSI and flood mitigation programs as well as periodic system performance and efficacy evaluation through flow monitoring and modeling.

The proposed implementation schedule synchronized with NJPDES permit cycles is shown by category of activity in Gantt chart form (Figure 8-1) on the following page. It should be noted that the dates specified above are contingent on reasonable and timely regulatory approvals and other variables beyond the control of CCMUA and the Cities.

8.3 Adaptive Management

The implementation schedule outlined in Table 8-1 above includes an evaluation at the completion of each five year NJPDES permit cycle. Based on these evaluations, CCMUA and the Cities will revise the LTCP as necessary with NJDEP's coordination and approval. This process exemplifies the concept of adaptive management.

Adaptive Management, as defined by the EPA, is “the process by which new information about the health of a watershed is incorporated into the watershed management plan.”⁸⁻¹ In the context of the SIAR adaptive management assumes that while the CSO control goals will remain constant, the tactical approaches to achieving the goals must be adjustable.

CCMUA and the Cities will also be subject to a variety of future conditions beyond their controls which may materially affect the benefits, feasibility and scheduling of the CSO controls described in this SIAR, thereby triggering a need to revise the LTCP. Examples of such triggering conditions include:

⁸⁻¹ Watershed Analysis and Management Guide for Tribes (2000) EPA Watershed Analysis and Management Project. Step 5 page 1.

- External changes requiring modifications to the fundamental planning and design bases used in the development of the LTCP or in subsequent design due to changing demographics, municipal collection system conditions, climate change and other external changes, etc.;
- Emergent regulatory requirements specific to the receiving streams (e.g. TMDLs) or in general (e.g. the promulgation of a National SSO Policy);
- Emergent economic and other developments and trends that could materially affect the affordability and CCMUA's and the Cities' abilities to finance the CSO controls that would be expected to cause the residential indicator for any of the permittees to exceed 2.0% of median household income.
- Changes to water quality standards and guidance that could affect the types and levels of wet weather controls necessary to meet the program objectives;
- Innovative and alternative technologies that could enhance water quality and/or reduce costs thereby enabling expanded control efforts.
- The unavailability of supplies, materials, contractors or labor necessary to implement the LTCP as scheduled in the LTCP due to conditions beyond CCMUA's and the Cities control such as a natural disaster or other emergency; and
- Local, state or federal legal impediments to the timely or orderly implementation of the LTCP e.g. lengthy litigation over land acquisition or inability to obtain required permits.

CCMUA and the Cities will inform NJDEP upon becoming aware of circumstances such as those listed above as to:

- An analysis of the issues and implications posed by the condition;
- An analysis of the impacts on the implementation of the LTCP or the efficacy of the controls; and
- A proposed plan of action to address the adverse conditions that will preserve CCMUA's and the Cities' compliance with their NJPDES permits and the requirements of the CSO Control Policy.

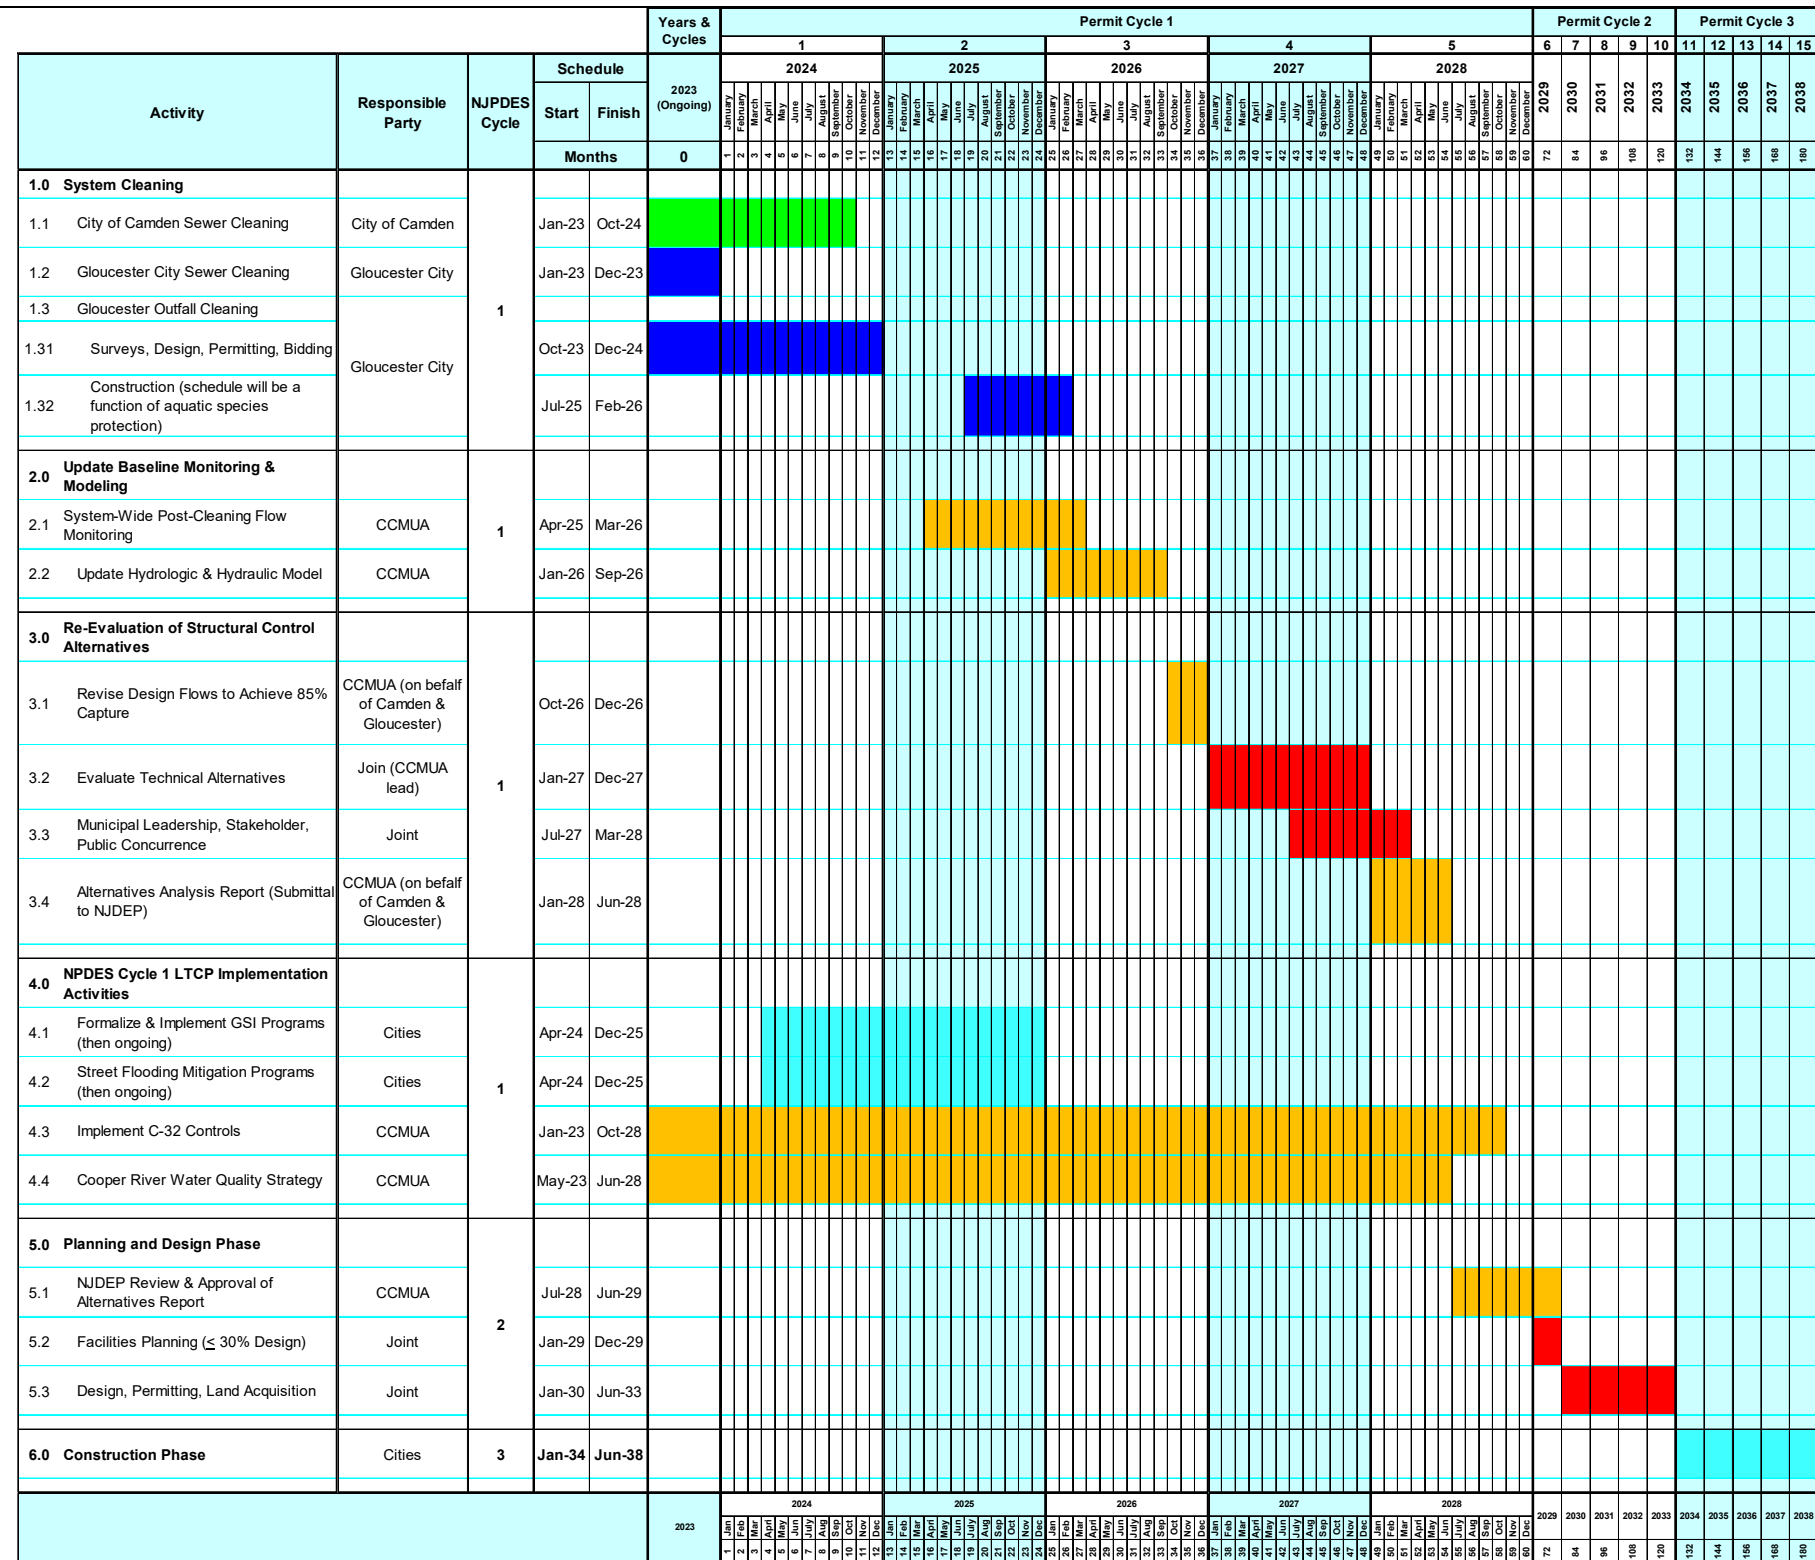


Figure 8-1 – Proposed LTCP Implementation Schedule

Appendices to Revised SIAR

A. Stakeholder Participation	1
B. NJDEP May 2021 Comments & Responses	107
C. NJDEP Comments of June & July 2023 & Responses	251
D. NJDEP Comments of August & Responses	277

pg.

SELECTION AND IMPLEMENTATION OF ALTERNATIVES REPORT

Camden County Municipal Utilities Authority
City of Camden
Gloucester City



NJPDES Permit Nos.

NJ0026182

NJ0108812

NJ0108847

September 2020

Revised September
2023



APPENDIX - A

Camden SMART Green Infrastructure Sites

Project Name - Features	GI #	Street Address	Neighborhood	Completion Date	Gallons of Stormwater Captured per Year
Michael Doyle Fishing Pier	1	200 Jackson Street	Waterfront South	4/1/2003	-
20th St Community Garden, Rain Garden	2	N 20th at River Ave	Cramer Hill	6/1/2010	63,000
Sumner Elementary School, Rain Garden	3	1600 S 8th St	Centerville	6/1/2010	110,000
Ferry Avenue Rain Garden	4	1656 Ferry Avenue	Waterfront South	3/1/2011	75,000
Waterfront South, Rain Gardens, Wildflower Meadow	5	S Broadway @ Chelton Ave	Waterfront South	7/1/2011	470,000
Ferry Avenue Library, Rain Garden	6	852 Ferry Avenue	Centerville	4/1/2012	62,500
Brimm School, Rain Garden	7	1626 Copewood Street	Whitman Park	5/1/2012	81,000
PRUP, Rain Garden and Rainwater Harvesting	8	818 S. Broadway	Bergen Square	6/1/2012	31,250
RT Cream School Rain Garden	9	1875 Leon Huff Street	Centerville	6/1/2012	25,000
29th St., Rain Gardens	10	29th St @ Pierce St & Tyler St	Cramer Hill	7/1/2012	296,000
Woodrow Wilson High School, Rain Garden	11	3100 Federal Street	Stockton	7/1/2012	30,000
Waterfront South Native Plant Nursery	12	1645 Ferry Avenue	Waterfront South	7/11/2012	-
Park Blvd, Rain Garden #1	13	Park Blvd @ Magnolia Ave	Parkside	8/1/2012	60,000
Park Blvd, Rain Garden #2	14	Park Blvd @ Vesper Blvd	Parkside	8/1/2012	40,000
304 State St., Rainwater Harvesting	15	304 State Street	North Camden	9/1/2012	3,000
Neighborhood Center	16	278 Kaighns Ave	Central Waterfront	9/1/2012	119,000
Rain Garden, Rainwater Harvesting	17	N Front St at Penn Street	Cooper Grant	3/1/2013	5,000
Front St. Community Garden, Rainwater Harvesting	18	N 7th Street @ Erie Street	North Camden	4/1/2013	47,700
Pyne Poynt School, Rain Garden	19	27 N 36th Street	Rosedale	5/1/2013	22,500
Urban Promise Academy, Rain Garden	20	1251 Collings Ave	Fairview	5/1/2013	22,500
Yorkship Elementary School, Rain Garden	21	29th St @ River Ave	Cramer Hill	7/1/2013	175,000
St. Anthony's, Rain Garden	22	Jasper Street	Waterfront South	10/15/2013	117,000
Liney Ditch Park, Shelterbelt Tree Planting	23	Baird Blvd & Cooper River	Marlton	6/1/2014	122,000
Baird Blvd, Rain Garden	24	Route 30 & Thorndyke	Marlton	6/1/2014	221,000
Gateway Park, Rain Garden	25	200 Jackson Street	Waterfront South	6/1/2014	258,000
Jackson St, Rain Garden	26	Trenton & Newton Ave	Cooper Grant	6/1/2014	32,000
Trenton Ave, Rain Garden	27	1219 Haddon Ave	Parkside	10/1/2014	12,000
Parkside Learning Garden, Cistern	28	295 Chestnut Street	Central Waterfront	11/1/2014	51,541
Mt. Zion Highway of Holiness, Porous Pavement	29	278 Kaighns Ave	Central Waterfront	11/1/2014	17,306
Neighborhood Center, Porous Pavement	30	227 Jefferson St	Waterfront South	8/1/2015	5,000,000
Phoenix Park Phase #1, Wildflower Meadow, Depaving, Porous Pavement, Trees	31	311 Grand Ave	Marlton	9/15/2015	29,687
Acelero Learning Center, Downspout Planters					

Camden SMART Green Infrastructure Sites

Adventure Aquarium, Rain Gardens	32	1 Riverside Drive	Central Waterfront	9/15/2015	158,854
Brimm School, Porous Pavement, Stormwater Planter	33	1626 Copewood Street	Whitman Park	9/15/2015	121,774
Cooper Sprouts Community Garden Rain Garden, Rainwater Harvesting, Porous Sidewalk, Trees	34	7th & Newton Avenue	Cooper Grant	9/15/2015	221,415
Dudley Grange Park, Rain Garden, Trees	35	3100 Federal Street	Dudley	9/15/2015	27,488
Ferry Avenue Library Rain Garden, Stormwater Planter, Downspout Planter, Tree	36	852 Ferry Avenue	Centerville	9/15/2015	282,508
Henry H Davis School, Downspout Planters	37	3425 Cramer St	Rosedale	9/15/2015	79,716
Octavius V. Catto School, Rain Garden, Trees	38	3100 Westfield Ave	Dudley	9/15/2015	207,031
Respond Day Care, Rainwater Harvesting, Trees	39	309 Vine St	North Camden	9/15/2015	35,735
St. Bartholomew's Church, Rain Garden, Rainwater Harvesting	40	749-751 Kaighns Ave	Bergen Square	9/15/2015	7,500
St. Joan of Arc Church, Rainwater Harvesting	41	3107 Alabama Rd	Fairview	9/15/2015	2,500
US Wiggins Elementary School, Porous Pavement, Tree Pit	42	400 Mt. Vernon St	Bergen Square	9/15/2015	79,716
Vietnamese Community Garden Rain Garden, Rainwater Harvesting, Porous Sidewalk	43	29th & Cramer St	Dudley	9/15/2015	114,279
Yorkship Elementary School Porous Pavement, Landscape Planters, Trees	44	1251 Collings Rd	Fairview	9/15/2015	145,414
Union Field/ Malandra Hall, Rain Garden	45	1244 S Merrimac Rd	Fairview	9/15/2015	340,000
Von Nieda Park/ Baldwin's Run	46	29th & Harrison St	Cramer Hill	10/1/2015	50,000,000
Von Nieda Park, Rain Garden	47	29th & Harrison St	Cramer Hill	4/1/2017	10,614
4th & Washington, Stormwater Planters	48	4th & Berkley St	Lanning Square	5/1/2017	192,800
Admin Parking Lot, Porous Pavement, Rain Garden	49	1645 Ferry Avenue	Waterfront South	5/1/2017	738,400
Bonsall School, Stormwater Planters, Porous Pavement	50	1575 Mt. Ephraim Ave	Liberty Park	5/1/2017	736,300
Broadway Triangle, Rain Garden	51	Walnut St & Broadway	Bergen Square	5/1/2017	104,300
Coopers Poynt School, Porous Pavement	52	3rd & York Sts,	North Camden	5/1/2017	495,200
Cramer School, Tree Pits	53	2800 Mickle Street	Stockton	5/1/2017	960,360
Elijah Perry Park, Porous Pavment	54	Ferry Ave & Phillips St	Centerville	5/1/2017	294,400
Westfield Ave, Porous Pavement	55	3706 Westfield Ave	Rosedale	5/1/2017	176,700

Camden SMART Green Infrastructure Sites

Phoenix Park Phase #2, Wildflower Meadow, Depaving, Porous Pavement, Trees	56	227 Jefferson St	Waterfront South	11/1/2017	1,000,000
Cramer Hill Nature Preserve, Nature Trail	57	32nd & Farragut Ave	Cramer Hill	12/1/2017	-
9th and Woodland Ave, Infiltration Trench, Trees	58	9th & Woodland Ave	Morgan Village	12/1/2018	35,298
Dudley School, Rain Garden	59	2250 Berwick St	Marlton	12/1/2018	108,807
Early Childhood Development Center, Planter Boxes	60	1602 Pine St	Parkside	12/1/2018	107,301
Princess Ave, Infiltration Trench, Porous Pavement, Trees	61	Princess & Walnut St	Parkside	12/1/2018	191,301
Coopers Poynt School	62	3rd & York St	North Camden	In Progress	-
Domenic Andjuar Park	63	Erie & Point St	North Camden	In Progress	-
Molina School	64	7th & Elm St	North Camden	In Progress	-
Gateway Park Bioswale	65	Route 30 & Thorndyke	Marlton	In Progress	-
Historical Society Rain Garden	66	1900 Park Blvd.	Parkside	In Progress	37,100
				TOTAL:	64,611,795



Appendix A-2

Imagine A Day Without Water 2017

October 12, 2017

1 of 21



The SMART Team



Appendix A-2



Types of Water

- Drinking water
- Sewage
- Stormwater Runoff

Appendix A-2





Where do we get our Drinking Water?



Camden's water history:

1845: Camden Water Works

Takes water directly from Delaware River (Cooper St)
(1854: Pavonia station)


1898: Morris-Delair System

Water pumped to surface from PRM Aquifer

1909: Phila Water Dept

Pumps from PRM Aquifer



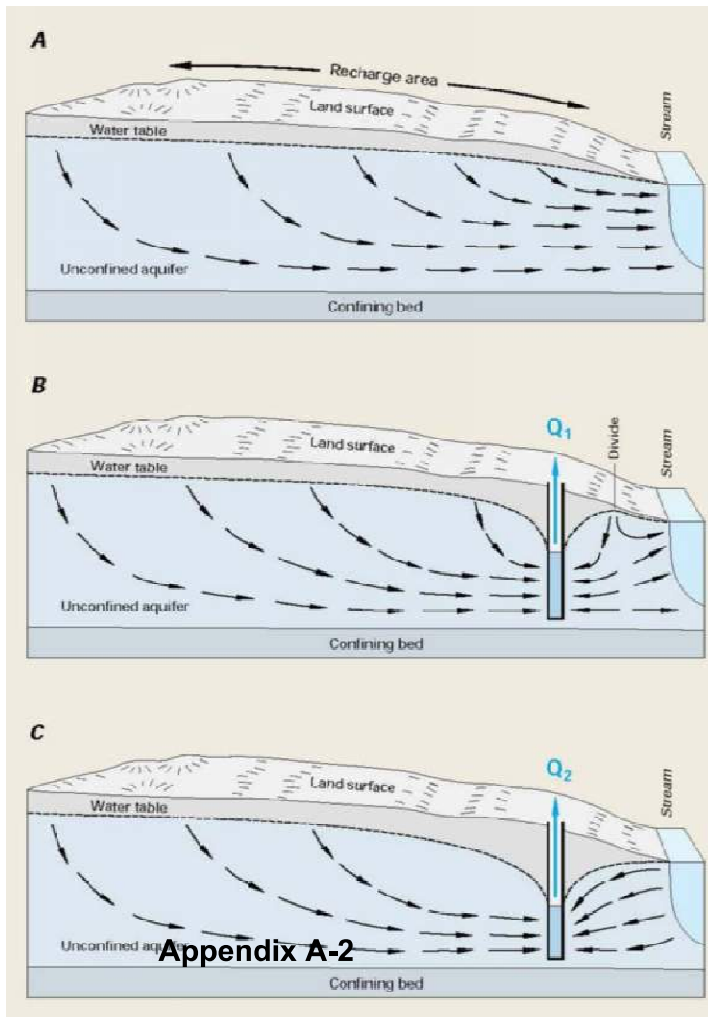

Appendix A-2

What is an aquifer?


A geological formation that is pumped for water supply.

In Camden city, the Potomac-Raritan-Magothy (PRM) Aquifer is our most important source of drinking water.

*...The PRM Aquifer sits directly below us...
...and, it is vulnerable to pollution*





Where do we get our Drinking Water in Camden?

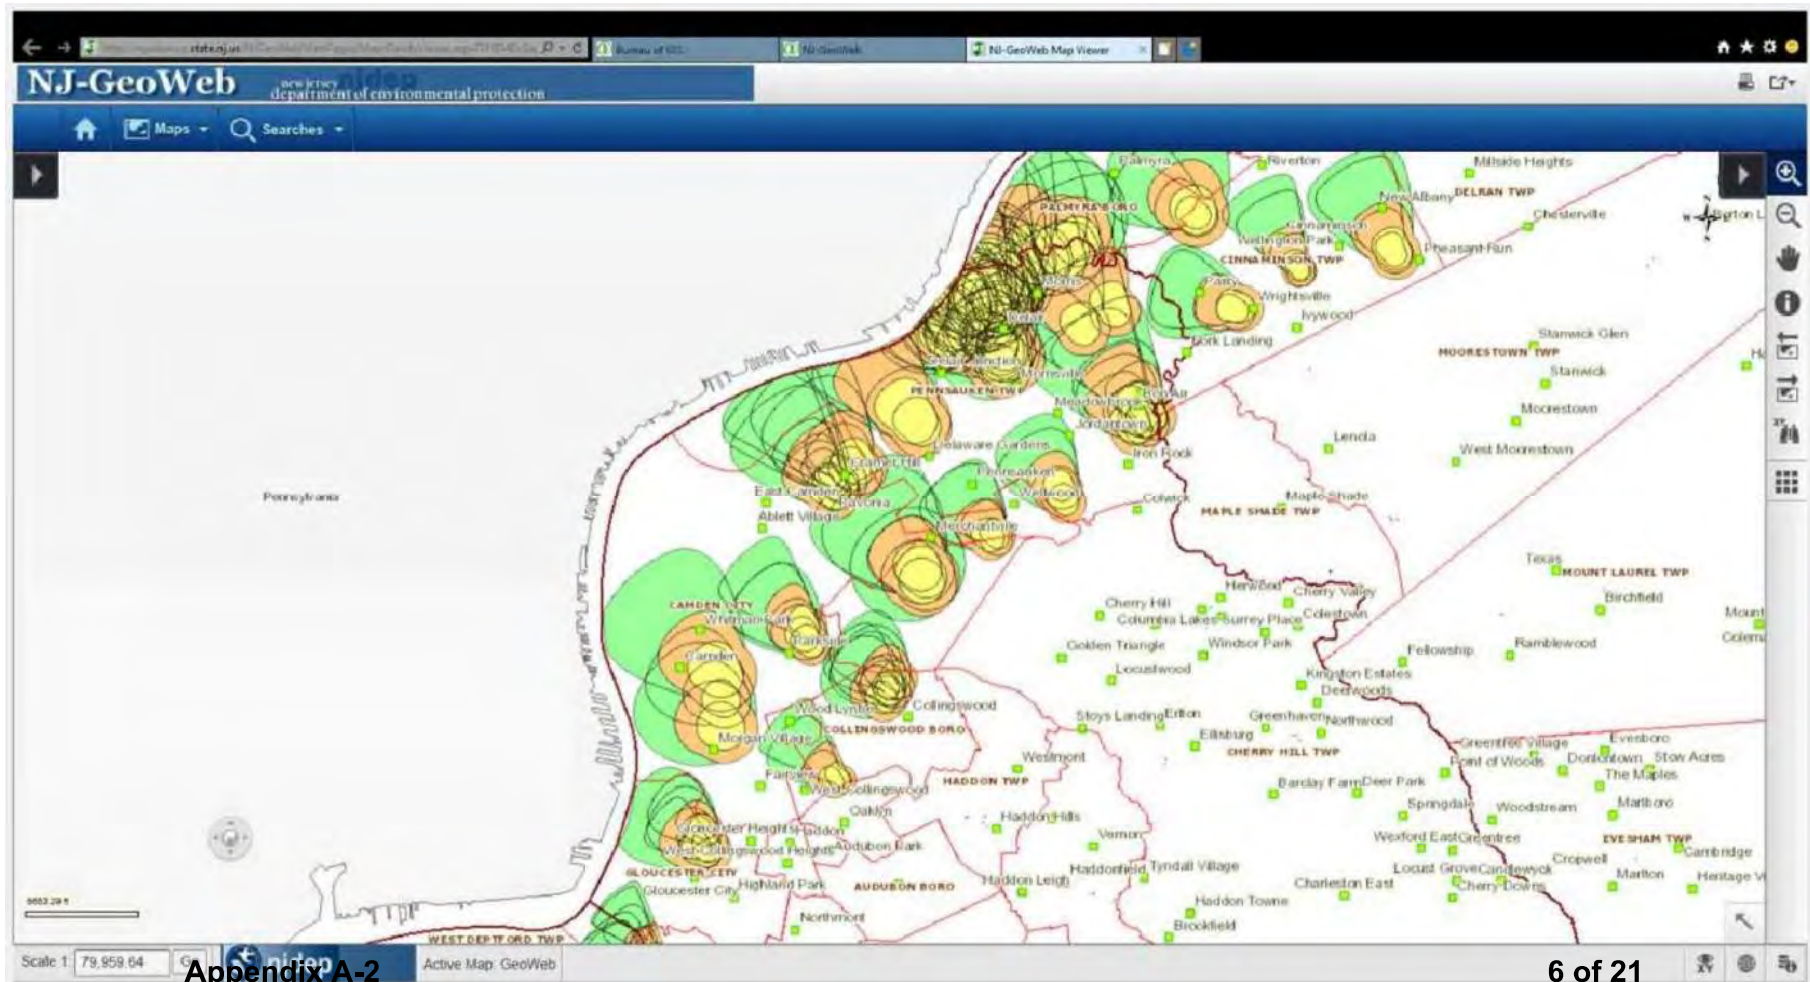

NJDEP Wellhead protection area maps for Camden area water supply wells




Where do we get our Drinking Water?

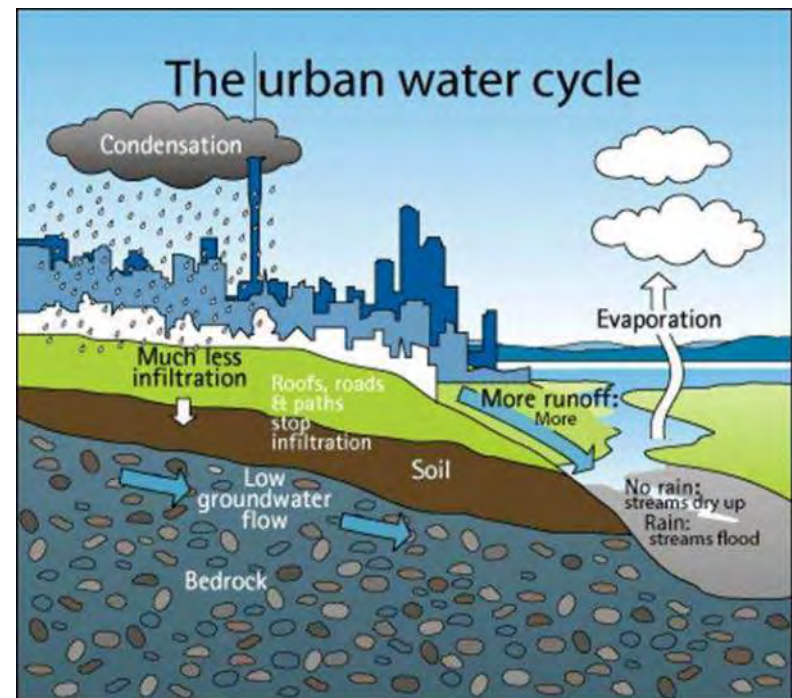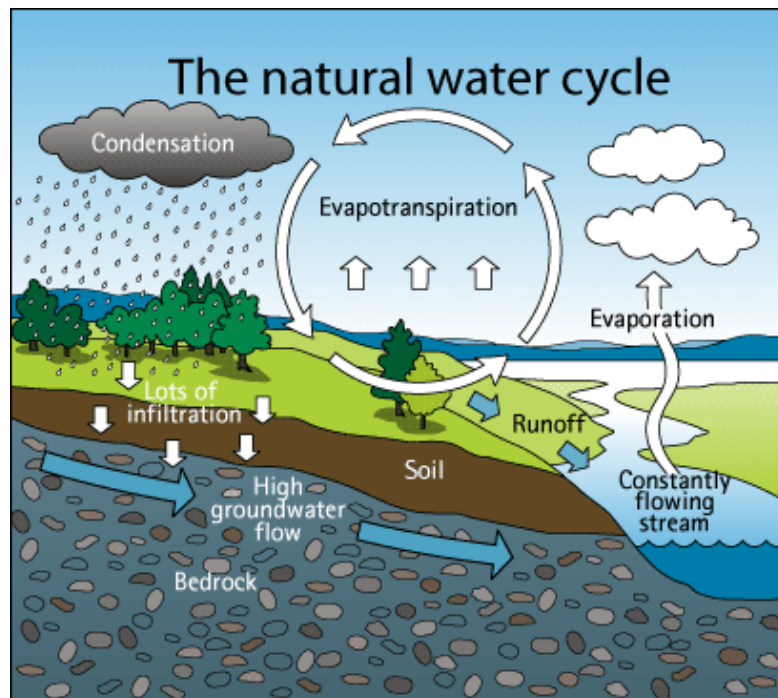

How rainwater behaves effect our drinking
Appendix A-2
water supply & water quality



How do we use our water resources in NJ?

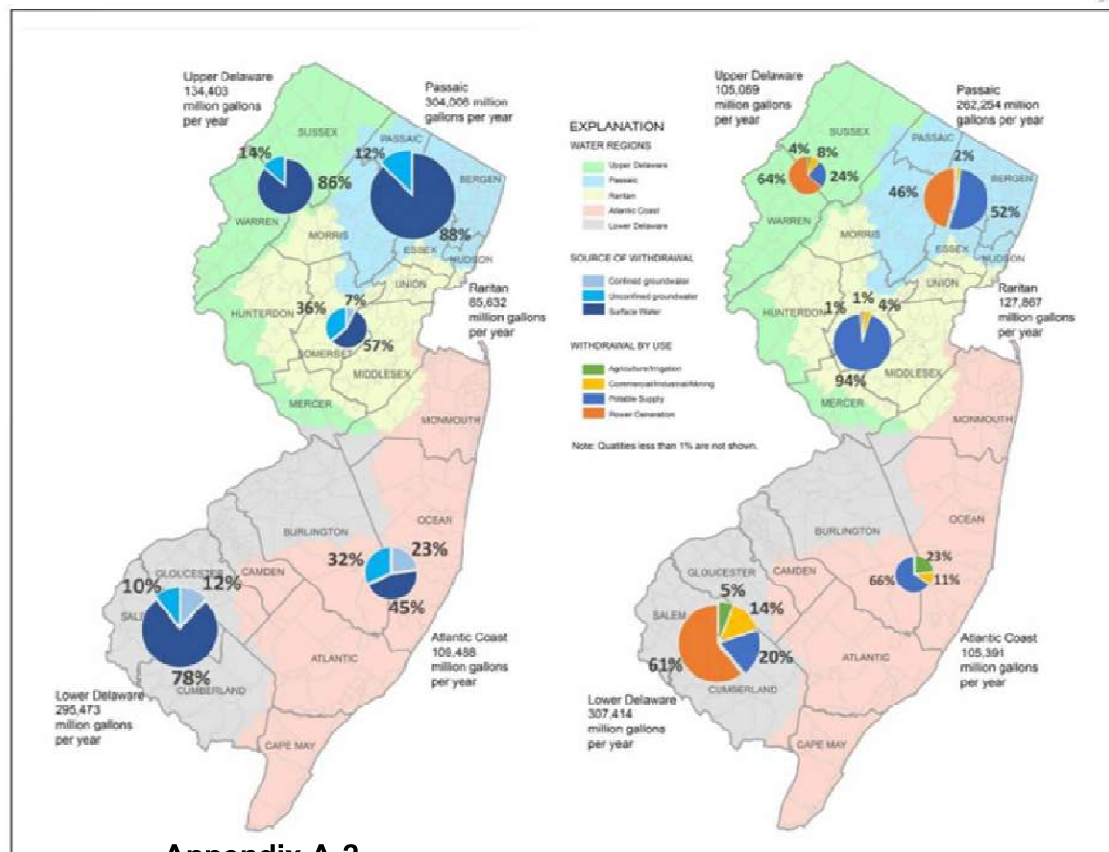

Appendix A-2

Figure 2.4 (a) Average annual source of water withdrawal by water region, 1990-2015 (millions of gallons).


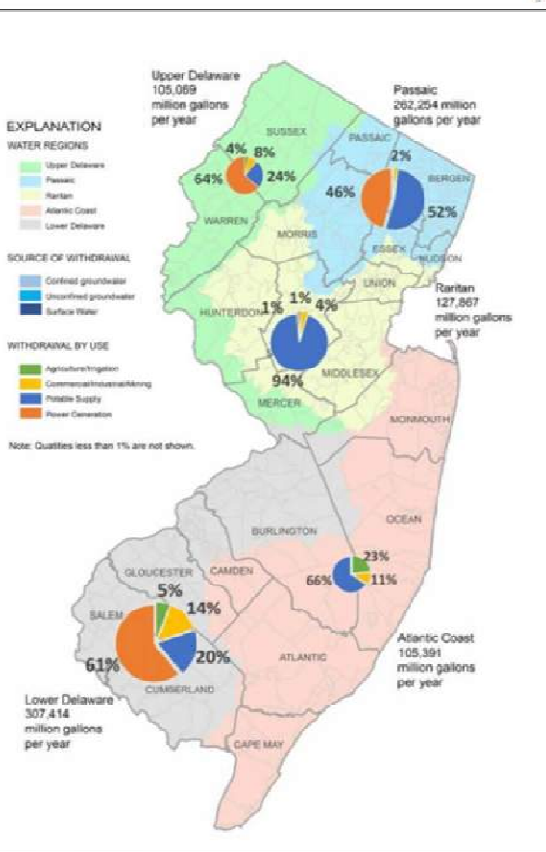


Figure 2.4 (b) Average annual use of water by water region, 1990-2015 (millions of gallons).





Lead Awareness

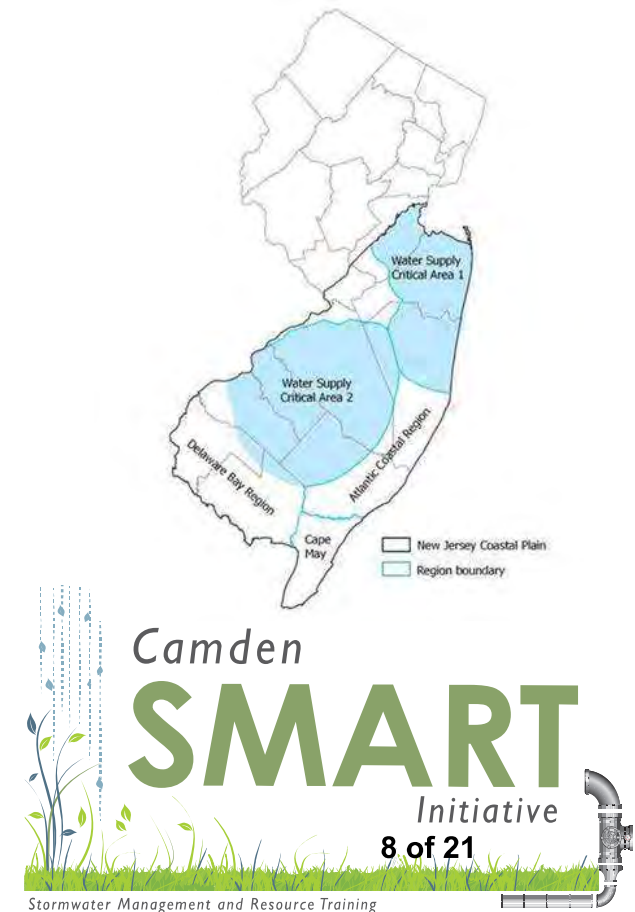

Appendix A-2





Sewage and Stormwater Runoff

- What is sewage?
- What is stormwater runoff?
 - Pervious vs impervious surfaces
 - Pervious: Football field
 - Impervious: Parking lot
- Combined sewer system

Appendix A-2





Formation of Camden SMART Initiative

- What is the Camden SMART (Stormwater Management and Resource Training) Initiative?
 - Combined sewer system
 - Combined sewer overflows
 - Green vs grey infrastructure

Appendix A-2





Green Infrastructure – Rain Barrel



Appendix A-2

- Rain water harvesting
- 50-gallon barrel
- Uses: watering plants, washing car, etc.
- Reducing water uses for outdoor chores





Green Infrastructure – Rain Garden



Appendix A-2

- Waterfront South Rain Garden
- Captures stormwater runoff from the street






Green Infrastructure – Trees



Appendix A-2

- Trees help with stormwater management!
- Absorb extra water during rain events
- Filter pollutants
- Increase rain infiltration into ground water
- Works well with rain gardens and barrels



Green Infrastructure – Park Creation



Appendix A-2



Completed Projects



Appendix A-2

- 53 completed green infrastructure projects citywide
- 1,700+ trees planted
- 63+ million gallons






Cramer Hill

<https://www.youtube.com/watch?v=rULgne7stg4>



Appendix A-2

- History of Cramer Hill
 - How Von Nieda Park became a Park
- What problems do we see in Cramer Hill?
- What are the resident's top priorities?
- Von Nieda Park – Baldwin's Run 50 million gallons of stormwater annually





Green Infrastructure – Daylighting Stream



Appendix A-2





What types of green infrastructure do we have at Brimm?

Rain Garden	81,000 gallons managed annually
Stormwater Planter Box and Porous Pavement	121,774 gallons managed annually
Rain Barrel	50 gallons managed per rainfall event
Total gallons of stormwater captured annually	202,824



How can YOU help?



- Report instances of flooding and illegal dumping to Camden SMART Partners by visiting www.CamdenReports.com

<https://www.youtube.com/watch?v=Qrie7lyNR8k&t=28s>

Appendix A-2





What's Next?

- Today, you will help Camden SMART Partners:
 - Plant Brimm's stormwater planter box
 - Re-fresh Brimm's rain garden (weeding, mulching, and planting)
 - Pledge to report instances of flooding via the Camden Reports application

Appendix A-2



List of CSO Supplemental Information Distributed

Link to 2020 Rain Barrel Virtual Workshop Program: <https://youtu.be/yHXXfHLD RKk>

Rain Barrel Meeting 6/20/18, English & Spanish, 1,000 copies distributed

Rain Barrel Meeting 5/31/18, English & Spanish, 800 copies distributed

Rain Barrel Meeting for National Community Development Week 4/3/18, 4/4/18 and 4/5/18, 1,200 copies distributed.

Rain Barrel Meeting 4/24/18, English & Spanish, 1,000 copies distributed

Rain Barrel Meeting 4/7/18, English & Spanish, 900 copies distributed

Rain Barrel Meeting 3/20/18, English & Spanish, 1,100 copies distributed

Lead Exposure Information, 20,000 mailed with bill 4/1/18, English & Spanish

Listing of Treatment Plant tours, 11/20/15 through 3/15/18

Audit Report on Environmental Communication 1/20/17

Environmental Policy 1/10/18, 160 copies distributed

Rain Barrel Meeting 2/21/18, English & Spanish, 240 copies distributed

Rain Barrel Meeting 12/12/17, English & Spanish, 1,000 copies distributed

Rain Barrel Meeting 10/17/17, English & Spanish, 1,200 copies distributed

Rain Barrel Meeting 10/07/17, Vietnamese, 500 copies distributed

Rain Barrel Meeting 9/26/17, English & Spanish, 1,400 copies distributed

Rain Barrel Meeting 8/22/17, English & Spanish, 1,100 copies distributed

Rain Barrel Meeting 8/01/17, English & Spanish, 1,100 copies distributed

Rain Barrel Meeting 6/28/17, English & Spanish, 1,200 copies distributed

Circuit Trails 160,000 mailed with bill 3/1/18 & 4/1/18

Gloucester City CSO insert 4,000 mailed with bill 3/1/17

Hidden Treasures Delaware River, 160,000 mailed with bill 12/1/16 & 1/1/17

Fishing Day South Camden flyer 800 distributed 9/1/17

Toilets Are Not Trash Cans, 160,000 mailed with bill 6/1/16 & 7/1/16

EPA Safe Drinking Water Tips, 20,000 mailed with bill 4/1/16

Circuit Trails, 160,000 mailed with bill 3/1/16 & 4/1/16

Camden County Conserves, 160,000 mailed with bill 12/1/15 & 1/1/16

Wonders of the Watershed, 160,000 mailed with bill 3/1/15 & 4/1/15



What is the Camden SMART Initiative?

The objective of the Camden SMART (Stormwater Management and Resource Training) Initiative is to develop a comprehensive network of green infrastructure programs and projects for the City of Camden.

The Initiative is a collaboration between the City of Camden, Camden County Municipal Utilities Authority, Cooper's Ferry Partnership, Rutgers Cooperative Extension Water Resources Program, New Jersey Tree Foundation, NJ Department of Environmental Protection, our public-private partners, community organizations, and most importantly, Camden residents to restore and revitalize our neighborhoods.

The Initiative includes neighborhood green and grey infrastructure projects, stormwater management policy development, and green infrastructure training programs.

Camden SMART Initiative:

- Reduce neighborhood flooding
- Reduce combined sewer overflows
- Improve air, water and climate quality
- Develop sustainable environmental policy
- Enhance economic development opportunities
- Add recreational amenities and open space
- Beautify neighborhoods



A former gas station is now home to four rain gardens at Broadway and Chelton Ave.



Visit Us at www.camdensmart.com



To reduce neighborhood
flooding and improve
stormwater management

Did you know?

- Camden has a combined sewer system which makes it more susceptible to backups and flooding. A combined sewer system collects sewage and rainwater in a single pipe system.
- Trash and debris block storm drainage systems, which can lead to flooding. Trash and debris also pollute our local streams and waterways, which can harm the habitat for many species of plants and animals.

Think SMART!

Everyone must do their part!



Rain garden on Park Blvd., Parkside neighborhood

Be SMART! Take Action!

1. Keep Camden Clean

Keep the street clean. Don't throw litter into the street. Take an active role by reporting illegal dumping.

*To report dumping call:
PUBLIC WORKS HOTLINE 856-757-7034*

2. Clean Your Yard Regularly

Bag, compost or recycle grass, tree limbs, leaves and other yard waste. Uncollected yard waste can clog storm drains when carried by rainwater.

3. Adopt a Drain

Keep your nearest storm drain clear of any debris or trash (including yard waste). Debris blocking the storm drain can easily result in flooding.

4. Collect and Reuse Rainwater

Take an active role in recycling rainwater and install a rain barrel at your home. By collecting rainwater, homeowners can help reduce flooding and pollution in local waterways.

*For more information, visit:
www.water.rutgers.edu*

5. Plant a Rain Garden

A rain garden allows about 30% more water to soak into the ground than a patch of lawn! Rain gardens also help to remove pollutants from stormwater runoff, protecting local waterways.

*For more information, visit:
www.water.rutgers.edu*

6. Flood Proof Your Home

Install rain gutters and direct downspouts away from the house. Keep rain gutters clear to prevent blockage. Also grade soil away from your home to prevent basement flooding.

7. Plant Trees and Shrubs

Trees, shrubs, and perennial plants absorb up to fourteen times more rainwater than a typical lawn, and they help to reduce rainwater flow into the sewer system by 35% or more.

*Trees available for Camden residents.
For more information, visit:
www.newjerseytreefoundation.org
or call 856-287-4488*

How To Prevent Stormwater Pollution

What is stormwater?

Stormwater is water from rain or melting snow that does not soak into the ground. It flows from rooftops, over paved areas, bare soil, and sloped lawns. As it flows, stormwater runoff collects and transports soil, animal waste, salt, pesticides, fertilizers, toxic metals, oil and grease, debris and other potential pollutants. In general, untreated stormwater is unsafe.

What is the problem?

Rain and snowmelt wash pollutants from streets, construction sites, and land into storm sewers. Eventually, the storm sewers empty the polluted stormwater directly into streams and rivers without prior purification or treatment. In Camden and Gloucester City, the sewage and stormwater are combined in the same pipe. During a storm when the flow exceeds the sewers' capacity the untreated sewage and stormwater overflow into the city's waterways and streets.

Polluted stormwater degrades our lakes, rivers, wetlands and other waterways. Untreated stormwater discharging to the ground can contaminate aquifers that are used for drinking water. Nutrients such as phosphorous and nitrogen can cause the overgrowth of algae, resulting in oxygen depletion in waterways. Toxic substances from motor vehicles and careless application of pesticides and fertilizers threaten water quality and can kill fish and other aquatic life. Bacteria from animal wastes and improper connections to storm sewer systems can make lakes and waterways unsafe for wading, swimming and fish consumption. Eroded soil is a pollutant as well. It clouds the waterway and interferes with the habitat of fish and plant life.



People really can make a difference when it comes to reducing stormwater runoff and the problems and costs that go with it. Because we all contribute to the problem, we all can be a part of the solution. It starts with paying attention to stormwater; at home, at work and in our communities.

Tips to prevent stormwater pollution:

- Pick up animal waste.
- Look for ways to keep runoff out of the stormwater system so it can soak into the ground.
- Compost or mulch leaves and yard debris.
- Plant rain gardens, use rain barrels.
- Remove litter from streets, sidewalks, and storm drains adjacent to your property.
- Sweep debris from driveways and parking lots rather than hosing debris into storm drains.
- Water the lawn, not the sidewalk and driveway.
- Reduce paved surfaces.
- Do not drain swimming pools into storm drains or road ditches.
- Reduce winter salt application.
- Triple rinse and recycle empty pesticide and fertilizer containers.
- Reconsider using toxic asphalt sealers, seal cracks only.
- Avoid using chemicals near waterways or storm drains.
- Dispose of automotive fluids appropriately. Fix vehicle fluid leaks immediately.
- Clean up spills immediately and properly dispose of cleanup materials.
- Avoid spraying pesticides/fertilizers in windy conditions or when rain is in the forecast.
- Cover and contain topsoil and mulch during installation.
- Reduce fertilizers, turf builders and pesticides on your lawn and garden. Use small amounts of slow-release fertilizer and environment-friendly products.



Water Conservation Ordinance Adopted by Camden City

Camden City Council recently approved a water conservation ordinance to help alleviate problems with reduced water pressure in times of drought. With the increasing effects of climate change and global warming felt throughout the world, long-term droughts are more likely to occur in the near future. It is critical to have a plan in place to deal with these conditions as they arise.

In addition, conserving water makes financial sense. Not only can you reduce your water bill, but the less water you use means the less water that needs to be treated at the wastewater treatment plant, thus keeping sewer rates in check.

Camden's water conservation ordinance states that, during a drought situation:

- Lawns may be watered two days per week. Properties with even number addresses may only water on Mondays and Thursdays. Properties with odd number addresses may only water on Tuesdays and Fridays.
- Watering may only be conducted between the hours of 6:00am and 9:00am or between 5:00pm and 8:00pm.
- No single area shall be watered more than 30 minutes per day.
- Flowers and shrubs may be watered as needed with a hand-held hose equipped with an automatic shut-off nozzle.
- No hose or hose-end watering shall be permitted when it is raining.
- Irrigation systems must only run between midnight and 10:00am.

We are asking for your support in adhering to these guidelines. The City is committed to water conservation and encourages residents to get on board. Start saving water and money now! And help us make Camden a sustainable community!

For more information on water conservation, visit www.epa.gov/watersense and www.cleanwaternj.org

For more information on sustainability in Camden, visit www.camdensmart.com





USING LESS WATER IS THE RIGHT THING TO DO!

- It's the right thing to do environmentally as water is a rare and precious resource. When we conserve water, we are saving the planet for our children and for future generations.
- Saving water reduces the potential for flooding of raw sewage during rain events in your town and for your neighbors upstream and downstream because you are using less of the sewer system's finite capacity.
- Saving water reduces sewage pumping costs for your town, which helps keep costs down.
- Saving water reduces pumping and treatment costs for the CCMUA, which helps us keep our rates down.
- Saving water helps save money for you, and keeps money in your pocket.



Flooding in the City of Camden after a typical rain event.

FOR MORE INFORMATION AND
WATER SAVING TIPS, VISIT:

www.epa.gov/watersense

www.njwatersavers.rutgers.edu

Camden County Municipal Utilities Authority

1645 Ferry Ave.
Camden, NJ 08104
(856) 541-3700

www.ccmua.org



CAMDEN COUNTY CONSERVES

Saving Water,
Saving Money

How much can you save?

Approximately 70 percent of water used in a household is used inside the home, with the bathroom utilizing more water than any other room. By replacing older, inefficient bathroom fixtures with WaterSense® labeled fixtures, your household can save in numerous ways.



WATER:
7,000 gallons annually

(enough to wash 6 months worth of laundry)



ELECTRICITY:
200 kilowatt hours annually

(enough to run a refrigerator for 2 months)




MONEY:
\$80 in utility bills annually

(fixtures pay for themselves in as little as 2 years)



SAVING WATER INDOORS:

- ◆ Fix household leaks.
- ◆ Always wash full loads for both laundry and dishes.
- ◆ Turn the water off while brushing teeth.
- ◆ Replace showerheads with low flow showerheads.
- ◆ Take shorter showers - five minutes or less is best.
- ◆ Avoid using running water to thaw meat or other frozen foods. Instead, defrost food overnight in the refrigerator.
- ◆ Purchase a water conservation kit and a leak detector kit. Many water companies offer them to customers at reduced prices.
- ◆ Install WaterSense® labeled products to conserve water.
- ◆ For commercial properties, refer to the best management practices for buildings that the Environmental Protection Agency (EPA) recommends for federal buildings.
- ◆ Refer to the Alliance for Water Efficiency Resource Library for more information regarding specific residential, commercial, and institutional water efficiency (www.allianceforwaterefficiency.org and www.home-water-works.org).



SAVING WATER OUTDOORS:

- ◆ Water only when needed; Camden County landscapes need approximately one inch of water per week.
- ◆ Water landscapes early or late in the day to reduce evaporation.
- ◆ Plant native plants; they are adapted to the region's conditions and require less water.
- ◆ Use a shut-off nozzle on your hose.
- ◆ Install a rain barrel to water flowers with rainwater collected from rooftops.
- ◆ Use fixed spray irrigation on turfgrass only. For all other plants, use drip or micro irrigation.
- ◆ Limit turfgrass to 40 percent or less of the total landscaped area.
- ◆ Wash vehicles at a car wash that recycles water.



Install a rain barrel at your house!

What is: “Flushable?”



When you flush your toilet or pour something down the drain of your sink or tub, what you send away disappears from sight and mind. But it's only begun its journey to the CCMUA's wastewater treatment plant in Camden, and beyond. If it's a harmful chemical, it may disrupt the treatment process, or some of it may not be removed, and will pass through into the Delaware River. If it's a solid, greasy, or sticky material that isn't designed to pass through the sewer system, it may not even make it to the plant. That can result in a clog somewhere along the line, and back sewage up into the streets, into your house, or into streets and homes in neighborhoods miles away elsewhere in the county as it travels toward the treatment plant. Clogs from these materials can also happen at the plant itself, creating problems for the whole system.

By giving a little thought to what goes down the toilet and drain, and by disposing of materials properly, you can save yourself from some repair bills; save the environment from unnecessary pollutants; and reduce potential damage to the public wastewater treatment system whose costs end up being charged back to the users—including you.

Just because you can do something doesn't mean that you should do it. You could claim that anything that fits through the hole at the bottom of the toilet bowl is “flushable,” technically. Parents of young children may have experienced keys, golf balls, toys, or clothing go down. But that doesn't mean they're going to be carried through the complicated network of pipes (potentially many miles) until they reach the wastewater treatment plant at the end of the line. Toilet paper is manufactured to disintegrate quickly in water. Paper tissues and towels, sanitary products, and diapers are not. Material can get caught at a sharp turn, or snag on the pipe lining, or tangle with other debris and make a bigger mess that impedes the flow in the pipe and cause partial or complete blockage and backups. The problems can be even bigger as material tries to pass through pumps or other machinery in its travels, and it stops or even damages equipment. Even material that starts out as liquid fats, oils, and greases (“FOG” in the industry lingo) can solidify and clog up the system.

So just because something can disappear down the toilet with a flush, that doesn't mean you should put it there.

These days, the biggest offender is personal hygiene materials advertised as “flushable” **baby or adult wipes**. Sure, it's physically possible to flush them down and out of sight, but once sent on their way through the sewers, “flushable” wipes can do a tremendous amount of damage! Rather than disintegrate, they manage to attach to other material and grow into agglomerations that the sewer systems are not designed to handle. You may have seen the headlines from London over the last few years, where what they call “fatbergs” of fat, wipes, waste, and other items were cleaned out of the London sewer system. The separate instances were described as “the size of a bus,” “the size of a 747,” and “40-metre long fatberg.” The problem has been covered by the New York Times, Washington Post,

the major media networks, and the major national wastewater treatment organizations have instituted campaigns to raise awareness of this real problem. The general rule to follow is **“don’t flush any personal hygiene products other than toilet paper.”**

Drugs and Medications

The US Food and Drug Administration states that disposal by flushing down the toilet is not advised for most drugs because of concerns that trace amounts of drugs can end up in the water supply and in rivers and lakes. That means potentially into the food chain, and ultimately into you and me. Not only humans can be affected. For example, a recent study found that fish whose brains held trace amounts of human anti-anxiety drugs were less effective at seeking shelter from predators. Antibiotic waste, which is associated with antibiotic-resistant bacteria, is also a problem in the wild. The best solution is to bring unwanted pharmaceuticals to a designated drug collection drop off point. Alternatively, you may discard some drugs in household trash after first making them difficult to recover by children, pets, or others seeking drugs. You can do this by first mixing pills or tablets with coffee grounds, kitty litter, dirt, or sawdust, then placing them in a non-leaking container such as a sealable plastic bag before placing them in the regular trash. But they may eventually land up in a landfill and return to the environment anyway. So it’s best to bring them to bring the unwanted drugs to an approved collection point.

New Jersey’s **Project Medicine Drop Program (800-242-5846)** has placed secured drop boxes in the headquarters of local police departments. Consumers from anywhere in New Jersey can visit these boxes seven days a week, to drop off unneeded and expired medications and keep them away from those at risk of abusing them. www.njconsumeraffairs.gov/meddrop

The Camden County Board of Freeholders’ **Addiction Awareness Task Force** aims to provide a safe, convenient, and responsible means of disposing of prescription drugs. No longer needed or outdated prescription drugs in homes are the same drugs that have unfortunately become the target of theft and misuse, oftentimes by people who have access to the residence. America’s 12 to 17 year olds have made prescription drugs the number one substance of abuse for their age group, and much of that supply is coming from the medicine cabinets of their parents, grandparents, and friends. Help us end medicine abuse by disposing of unneeded prescription drugs at a drug drop box near you. The web site list local police departments that provide drop boxes for unneeded or expired drugs: www.addictions.camdencounty.com

More information

To learn more about the problem, visit the CCMUA’s education web page: www.CCMUA.org

(0516) Toilets Are Not Trash Cans logo courtesy of NACWA



Appendix A-5: Media Mentions

Publication	Source	Web URL (to online source)
Fix a Leak Week 2015, March 16–22, 2015 (3/1/2015)	CCMUA	http://www.ccmua.org/?page_id=1759
Executive Director Andy Kricun to discuss “Promoting Environmental Justice as an Essential Best Management Practice for Utilities in Economically Distressed Communities” (3/11/2015)	AWRA	http://awra-pmas.memberlodge.org/event-1867270
CCMUA joins Value of Water Coalition (3/16/2015)	Value of Water Coalition	http://www.ccmua.org/wp-content/uploads/2015/03/VOW-Relaunch-Press-Release-FINAL.pdf
CCMUA Receives WAVE award from Association of Environmental Authorities of NJ for forward thinking and innovation (3/25/2015)	Camden County	http://sustainable.camdencounty.com/ccmua-wins-aea-wave-award-for-innovation/
Camden SMART partnership to receive NJ Future’s 2015 Smart Growth Award for green and gray stormwater infrastructure program (4/15/2015)	NJ Future	http://www.njfuture.org/smart-growth-101/smart-growth-awards/2015-smart-growth-award-winners/grassroots-collaboration-on-green-infrastructure/
Camden SMART projects highlighted in Earth Week celebration (KYW, 4/21/2015)	KYW	http://philadelphia.cbslocal.com/video/category/latest-videos/11412412-earth-week-celebrations-underway-in-camden-nj/
US EPA recognizes Camden SMART stormwater management program with Environmental Champion Award (4/23/2015)	EPA	https://19january2017snapshot.epa.gov/newsreleases/epa-honors-new-jersey-environmental-champions_.html
Phoenix Park opens on South Camden waterfront (Courier Post, 6/2/2015)	Courier Post	http://www.courierpostonline.com/story/news/local/south-jersey/2015/06/02/phoenix-park-opens-south-camden-waterfront/28371393/
Phoenix Park rises from crumbling industry to create oasis for Camden residents (NJ.com, 6/3/2015)	NJ.com	http://www.nj.com/camden/index.ssf/2015/06/phoenix_park_rises_from_crumbling_industry_to_crea.html

Freeholders Open Park in Camden City (6/4/2015)	Camden County	http://www.camdencounty.com/cou-nty-news/freeholders-open-phoenix-park-camden-city
US EPA releases video on CCMUA adaptation for climate change (Courier Post, 8/4/2015)	Courier Post	http://www.courierpostonline.com/s-tory/news/local/south-jersey/2015/08/04/ccmua-featured-climate-change-video-series/31101889/
CCMUA Net Zero Energy program featured in US EPA video (8/10/2015)	EPA	https://youtu.be/_no2kKYt6w
CCMUA completes project funded by NJ Environmental Infrastructure Trust to capture 30 tons of solids per year that used to go to Delaware River, Cooper River, and Newton Creek (8/29/2015)	CCMUA	http://www.ccmua.org/?p=165
Rutgers professor highlights CCMUA as a model utility, using capital investment to reduce costs (NJ Spotlight, 9/6/2015)	NJ Spotlight	http://www.njspotlight.com/stories/15/09/02/opinion-nj-should-require-water-utilities-to-spend-more-now-so-they-will-cost-less-later/
National Association of Clean Water Agencies (NACWA) awards CCMUA third consecutive Gold Peak Performance Award for outstanding effluent/water quality performance (9/25/2015)	NACWA	http://www.nacwa.org/about-us/awards/peak-performance-awards/peak-past-honorees
NJ Section of American Water Resources Association presents Excellence in Water Resources Protection and Planning Award to Phoenix Park Project (10/1/2015)	NJAWRA	http://www.ccmua.org/wp-content/uploads/2015/10/NJAWRA-CCMUA-Web-site-display-package.pdf
Association of NJ Environmental Commissions awards CCMUA 2015 Environmental Achievement Award for Phoenix Park project (10/9/2015)	ANJEC	http://anjec.org/pdfs/Congress2015-AchievementAwardWinnersProjects.pdf
"Promoting Environmental and Community Service Leadership as an Essential Best Practice for the Clean Water Utility of the Future," presented by CCMUA Executive Director Andy Kricun to The Funders Network (11/11/2015)	CCMUA	http://www.ccmua.org/wp-content/uploads/2015/11/Environmental-Community-Service-Leadership-11-11-2015-Funders-Network.pdf

CCMUA Honored by Federal Environmental Council for one of most innovative uses of the US EPA's Federal State Revolving Fund in the history of the program (1/13/2016)	Camden County	http://sustainable.camdencounty.com/ccmua-honored-federal-environmental-council/
National Association of Clean Water Agencies (NACWA) Features CCMUA Role Shown In New EPA Video On Sustainable Communities (2/22/2016)	NACWA	http://www.nacwa.org/news-publications/clean-water-current-archives/clean-water-current---february-19
New EPA Video highlights Camden Collaborative Initiative sustainability efforts (2/22/2016)	EPA	https://www.youtube.com/watch?v=vzIJmHhSC3M&feature=youtu.be
CCMUA featured as example in NACWA call for federal action to institute measures to help water utilities transition into 'Utility of the Future' (3/15/2016)		http://www.ccmua.org/wp-content/uploads/2016/03/Trifold.pdf
NJ DEP Water Resource Management quarterly highlights CCMUA's innovative use of state revolving fund for green and grey infrastructure projects (5/2/2016)	NJ DEP	http://www.ccmua.org/wp-content/uploads/2016/05/wrm-quarterly-update-spring2016c.pdf
CCMUA begins upgrade of biosolids treatment with cogeneration technology (Water Online, 5/2/2016)	Water Online	http://www.wateronline.com/doc/new-jerseys-camden-county-municipal-its-wastewater-facility-0001
Article draws sharp contrast between Camden's forward-looking water infrastructure policies and Flint, Michigan's water supply disaster (Water Online, 5/9/2016)	Water Online	http://www.wateronline.com/doc/w-wema-window-a-tale-of-two-cities-flint-mi-and-camden-nj-0001
CCMUA Executive Director Andy Kricun comments to WHYY's Newsworks on importance of rehabilitating Camden's infrastructure (WHYY, 5/13/2016)	WHYY	http://www.newsworks.org/index.php/local/healthscience/93664-renewed-attention-to-water-supply-infrastructure-starting-to-impact-cities-like-camden-nj
Camden Collaborative Initiative awarded EPA's 2016 Environmental Champion Award (5/13/2016)	EPA	https://19january2017snapshot.epa.gov/newsreleases/epa-honors-new-jersey-environmental-champions-0_.html

"Clean water a priority at the CCMUA" (article; must scroll down to page 10) (Cherry Hill Sun, 5/18/2016)	Cherry Hill Sun (scroll down to page 10)	https://www.scribd.com/doc/312524040/CherryHill-0518
NJTV broadcast discusses green infrastructure approach with CCMUA Executive Director Andy Kricun (NJTV, 5/25/2016)	NJTV	http://www.njtvonline.org/news/video/group-eyes-ways-rebuild-preserve-states-old-brittle-water-infrastructure/
CCMUA featured in US EPA blog highlighting successful efforts of utilities to become climate-ready (6/15/2016)	EPA	https://blog.epa.gov/blog/2016/06/protecting-drinking-water-by-becoming-climate-ready/
CCMUA is awarded grant by National Fish and Wildlife Foundation and William Penn Foundation to implement rain barrel program (7/21/2016)	NFWF	http://www.nfwf.org/whoweare/mediacenter/pr/Pages/delaware_16-0720.aspx
WPVI (Philadelphia Channel 6) coverage of NFWF and William Penn Foundation grant to CCMUA for rain barrel program (WPVI, 7/21/2016)	WPVI	http://6abc.com/society/delaware-river-restoration-fund/1435474/
KYW (Philadelphia Channel 3) coverage of NFWF and William Penn Foundation grant to CCMUA for rain barrel program (KYW, 7/21/2016)	KYW	http://philadelphia.cbslocal.com/video/category/spoken-word-kywtv/3434416-grant-will-fund-conservation-projects-in-2017/
CCMUA Executive Director speaks in Washington on infrastructure funding strategies (7/25/2016)	NACWA	http://www.nacwa.org/news-publications/clean-water-current-archives/clean-water-current---july-25
CCMUA awarded with recognition as a Utility of the Future Today (8/2/2016)	Water Resources Utility of the Future Today	http://www.ccmua.org/wp-content/uploads/2016/08/Utility-of-the-Future-Today-Recognitions-Press-Release-8-9-16-with-Recipients-list.pdf
CBS 3 News report on CCMUA's Cramer Hill Nature Preserve (KYW, 8/15/2016)	KYW	http://philadelphia.cbslocal.com/2016/08/15/camden-sewerage-nature/
35-Acre Cramer Hill Nature Preserve to be created in Camden by CCMUA (Courier Post, 8/16/2016)	Courier Post	http://www.courierpostonline.com/story/news/local/2016/08/12/camden-waterfront-access-preserve/88626726/

New Waterfront Park Coming to Camden City (8/23/2016)	Camden County	https://web.archive.org/web/20160831161501/http://www.camdencounty.com:80/county-news/new-waterfront-park-coming-camden-city
From wastewater treatment plant to nature preserve (Philly.com, 8/25/2016)	Philadelphia Inquirer	http://www.philly.com/philly/news/new_jersey/20160824_From_wastewater_treatment_plant_to_nature_preserve.html?mc_cid=6c15a851e6&mc_eid=e8a2df0487
National water industry magazine highlights Camden green stormwater infrastructure program as example for other economically stressed cities (Water World, 8/29/2016)	Water World	http://www.waterworld.com/articles/print/volume-32/issue-8/features/aren-t-you-swale.html
CCMUA featured in Government Technology magazine article on planning for climate change consequences (Government Technology, 9/2/2016)	Government Technology	http://www.govtech.com/fs/Predicting-the-Unpredictable-How-Data-Based-Forecasting-Helped-One-Town.html
Cramer Hill Camden property to become nature preserve (Philadelphia Inquirer, 9/26/2016)	Philadelphia Inquirer	http://www.philly.com/philly/columnists/kevin_riordan/20160925_Where_the_bald_eagle_and_owl_dwell_in_Camden.html
CCMUA noted as EPA CREAT case study (10/3/2016)		http://www.nacwa.org/news-publications/clean-water-current-archives/clean-water-current---october-3
CCMUA's Phoenix Park Phase 1 project featured in Delaware Valley Green Building Council Green Stormwater Infrastructure precedent library (dvgbc.org, 1/8/2017)	Delaware Valley Green Building Council	https://dvgbc.org/sites/default/files/images/policyflipbook/index.html?page=52
Camden SMART Stormwater Management Projects featured in New Jersey League of Municipalities conference session (1/8/2017)	Sustainable Jersey	http://www.sustainablejersey.com/fileadmin/media/Events_and_Trainings/Awards_Ceremony/NJLM_Sessions/2016/FINAL_SW_Mgmt_Role_in_Comm_Health.pdf

CCMUA implementation of CSO Long Term Control Plan is listed among top commitments in statewide water infrastructure effort (JerseyWaterWorks.org, 1/8/2017)	Jersey Water Works	http://www.jerseywaterworks.org/our-work/2017-commitments/
NJ Department of Environmental Protection recognizes CCMUA for Environmental Stewardship (2/7/2017)	NJ DEP	http://www.ccmua.org/wp-content/uploads/2017/02/NJDEP-Envir-Stewardship-Recognition.pdf
CCMUA and Rutgers Cooperative Extension Water Resources Program collaborate on Camden green infrastructure projects (2/7/2017)	Rutgers Cooperative Extension Water Resources Program	http://www.water.rutgers.edu/Water_Pages/Enewsletters/E-Newsletter_V38_20170119.pdf
CCMUA Executive Director Andy Kricun to receive 2017 Leadership in GSI (Green Stormwater Infrastructure) award from Sustainable Business Network of Philadelphia (4/19/2017; updated 1/23/2018)	Sustainable Business Network of Philadelphia	http://gsipartners.sbnphiladelphia.org/leadership-in-gsi-2017-excellence-in-gsi-awards-ceremony/
Water Utility of the Future Today compendium highlights CCMUA achievements (4/19/2017)	WEF	http://www.wef.org/globalassets/assets-wef/3---resources/for-the-public/utility-of-the-future/2016-summary-uotf-today-honorees-final.pdf
Water Resources Association of the Delaware River Basin awards 2017 Achievement Award to Camden SMART Initiative (4/19/2017)	Water Resources Association of the Delaware River Basin	http://www.wradrb.org/calendar_dtl.php?id=23&d=2017-04-19
Board of Public Utilities funds CCMUA community microgrid feasibility study (7/10/2017)	Military-Technologies.net (NO LONGER AVAILABLE)	http://www.military-technologies.net/2017/07/05/n-j-board-of-public-utilities-highlights-development-of-town-center-distributed-energy-resource-microgrids-with-tour-of-proposed-downtown-trenton-microgrid/

Clean water industry group releases report on environmental justice and community service featuring CCMUA efforts (7/24/2017)	NACWA	http://www.nacwa.org/news-publications/clean-water-current-archives/clean-water-current/2017/07/18/nacwa-releases-environmental-justice-community-service-compedium
US Senate Hears Testimony from CCMUA Executive Director Andy Kricun on need to fund improvements to nation's aging water infrastructure (7/24/2017)	Camden County	http://www.camdencounty.com/us-senate-hears-testimony-ccmua/
CCMUA receives 2016 NACWA Gold Peak Performance award (7/25/2017)	NACWA	http://www.nacwa.org/about-us/awards/peak-performance-awards/peak-2017-honorees
State announces study of microgrid to connect CCMUA with other facilities for energy resiliency (9/8/2017)	SNJ Today	http://www.snjtoday.com/story/36315005/state-officials-announce-start-of-camden-microgrid-study
CCMUA Executive Director Andy Kricun stresses critical need for independent power source in planning for microgrid (9/12/2017)	Daily Energy Insider	https://dailyenergyinsider.com/news/7752-new-jersey-board-public-utilities-approves-feasibility-study-camden-county-microgrid/
Camden Sewage Treatment Plant To Go Off Power Grid By 2019 (9/28/2017)	KYW	http://philadelphia.cbslocal.com/2017/09/28/camden-sewage-treatment-plant-to-go-off-power-grid-by-2019/
US Water Alliance spotlights CCMUA commitment to local revitalization through partnerships (9/30/2017)	US Water Alliance	http://uswateralliance.org/resources/one-water-spotlight-camden-county-municipal-utilities-authority-september-2017
CCMUA keeping rates stable and building the local workforce (in new EPA Report "Water Infrastructure Financial Leadership: Successful Financial Tools for Local Decision Makers," p. 32) (10/2/2017)	EPA	https://www.epa.gov/sites/production/files/2017-09/documents/financial_leadership_practices_document_final_draft_9-25-17_0.pdf
CCMUA Becomes First Authority in State to be Energy Independent (CamdenCounty.com) (10/3/2017)	Camden County	http://www.camdencounty.com/ccmua-becomes-first-authority-state-energy-independent/
Camden County Utilities Authority Goes Off-Grid with \$40M Sustainability Loop (NJ Pen) (10/3/2017)	NJ Pen	http://www.njpen.com/camden-county-utilities-authority-goes-off-grid-with-40m-sustainability-loop/

Camden County Takes Steps to Get Off the Grid (SNJ Today) (10/3/2017)	SNJ Today	http://www.snjtoday.com/story/36477983/camden-county-takes-steps-to-get-off-the-grid
Camden Sewage Treatment Plant To Go Off Power Grid By 2019 (CBSPhilly.com) (10/3/2017)	KYW	http://philadelphia.cbslocal.com/2017/09/28/camden-sewage-treatment-plant-to-go-off-power-grid-by-2019/
Camden County MUA Moves To Be Energy Independent by 2019 (10/3/2017)	NACWA	http://www.nacwa.org/news-publications/news-detail/2017/10/03/camden-county
Camden County MUA says energy independent in 2019 (Courier Post) (10/3/2017)	Courier Post	http://www.courierpostonline.com/story/news/2017/09/28/camden-county-utilities-authority-savings/711842001/
Wastewater for electricity: South Jersey utility in swap deal with trash-to-energy plant (Philly.com) (10/3/2017)	Philadelphia Inquirer	http://www.philly.com/philly/business/energy/wastewater-for-electricity-south-jersey-utility-in-swap-deal-with-trash-to-energy-plant-20170928.html
Article on Green Infrastructure Investment Analysis for Camden (Urban Planning) (10/12/2017)	Urban Planning	https://www.cogitatiopress.com/urbanplanning/article/view/1038
CCMUA mentioned in NAPA report on Community Affordability of Clean Water Services (11/15/2017)	NACWA	http://www.nacwa.org/docs/default-source/conferences-events/Hot-Topics-in-Clean-Water-Law-Webinar/2017-11-15napa_report.pdf?sfvrsn=2
CCMUA addresses Camden City sewer overflow problem (12/11/2017)	NJ Pen	http://www.njpen.com/a-plan-to-end-sewer-overflow-in-camden/
Phoenix Park 'Rises from the Ashes,' Opens in Camden (12/12/2017)	SNJ Today	http://www.snjtoday.com/story/37051571/phoenix-park-rises-from-the-ashes-opens-in-camden
In the shadow of a Camden waste treatment plant, a park opens (12/12/2017)	Courier Post	http://www.courierpostonline.com/story/news/local/south-jersey/2017/12/12/shadow-camden-waste-treatment-plant-park-opens/941599001/

Final phase of Phoenix Park in Camden opens (12/12/2017)	Camden County	http://www.camdencounty.com/free-holders-open-final-phase-phoenix-park-camden/
Access Opened Up to Riverfront and Parks (12/29/2017)	Camden County	http://www.ccmua.org/wp-content/uploads/2018/01/Nash-Retrospect-Riverfront-Access-Column-2017-12-29.pdf
Study shows that optimal maintenance of Camden City's sewer system would reduce 90% of community and street flooding (1/10/2018)	Jersey Water Works	http://www.jerseywaterworks.org/resource/impact-proper-maintenance-combined-sewer-overflow-system-flooding-city-camden/
CCMUA projects highlighted in "New Report Analyzes the Financial Benefits of Investing in Water Infrastructure" (New Jersey Municipalities) (2/21/2018)	Jersey Water Works	http://www.jerseywaterworks.org/wp-content/uploads/2018/02/NJ-Municipalities-Magazine-February-2018-David-Zimmer.pdf
US EPA report highlights CCMUA in A Wet Weather Case Study of Incorporating Community Interests into Effective Infrastructure Decision-Making (3/2/2018)	EPA	https://www.epa.gov/sites/production/files/2018-01/documents/camden_case_study-1-16-18.pdf
Camden SMART Initiative Revitalizes, Extends City's Open Spaces (3/19/2018)	NJ Spotlight	http://www.njspotlight.com/stories/18/03/18/camden-smart-initiative-revitalizes-extends-city-s-open-spaces/?mc_cid=b755c9fe6d&mc_eid=e8a2df0487
Park Projects Connect Camden to Delaware River (3/23/2018)	Camden County	http://www.ccmua.org/wp-content/uploads/2018/04/Retrospect-article-2018-03-23.pdf
Camden Finds Strength in Its Partners (4/2/2018)	NJ Spotlight	http://www.njspotlight.com/stories/18/04/01/camden-finds-strength-in-its-partners/
Camden's Vision for a Sustainable Future (4/9/2018)	NJ Spotlight	http://www.njspotlight.com/stories/18/04/08/camden-s-vision-for-a-sustainable-future/

National study on affordability of utility rates highlights CCMUA (4/25/2018)	Univ. of NC Environmental Finance Center	https://efc.sog.unc.edu/project/navigating-legal-pathways-rate-funded-customer-assistance-programs
US Water Alliance designates CCMUA to lead Camden Taskforce (one of only six in the nation for this initial year) to develop and promote equitable water management (5/11/2018)	US Water Alliance	http://uswateralliance.org/initiatives/water-equity/taskforce
Brookings Institution recognizes CCMUA's lead role in Camden Collaborative Initiative to strengthen the city's infrastructure and economy (5/14/2018)	Camden County	https://www.brookings.edu/blog/the-avenue/2018/05/14/the-water-workforce-opportunity-how-camden-is-driving-collaborative-solutions-around-its-infrastructure-and-economy/
Camden SMART Initiative to hold free rain barrel workshop	TAPintoCamden	https://www.tapinto.net/towns/camden/articles/camden-smart-initiative-to-hold-free-rain-barrel
Camden's Free Rain Barrel Program Will Help You Conserve Water	SJ Magazine	https://sjmagazine.net/news-features/camdens-free-rain-barrel-program-will-help- conserve-water



Compendium of Successful Water Workforce Practices

Green Ambassadors Program

Name of Utility: Camden County Municipal Utilities Authority

Municipality/State: Camden, New Jersey

Contact Person/Information: Timothy Feeney tfeeney@ccmua.org Camden County Municipal Utilities Authority

Year of Inception of Program: 2014

Purpose and Goals of Workforce Program:

To introduce Camden City high school students to environmental issues, solutions and careers through a summer internship program consisting of educational tours, classroom-style learning and community service projects.

Case Study Summary

The Green Ambassadors is an environmentally focused youth internship program offered at the Camden County Municipal Utilities Authority since 2014. Over the six cohorts of the program so far, 84 youths have participated. The participants are aged 14-18 and are drawn from all the high schools in the treatment plant's host city of Camden New Jersey.

The interns are exposed to the most critical environmental topics by some of the leading government agencies and nonprofit organizations in the field including NJ Department of Environmental Protection, US Environmental Protection Agency, New Jersey Audubon, South Jersey Land and Water Trust, the Partnership for the Delaware Estuary, and the Delaware Valley Regional Planning Commission. Through both classroom-style education and site tours, these high school students are taught by true experts and leaders in environmental protection. In addition, the Green Ambassadors tour the facilities of permittees such as a water treatment plant, trash-to-steam facility and the CCMUA's own wastewater treatment plant to see technologies and processes required to meet environmental permits and protect public health.

The program is typically five weeks long, three days per week paying 10 dollars an hour. Early cohorts consisted of 10 participants and a single counselor. In 2017 the program was expanded, with two counselors and 20 participants. It was found that a

seven-hour workday, three days per week is the optimal schedule for this type of program.

The Green Ambassadors also benefit from a creative variety of teaching experiences such as canoe tours and ecology hikes conducted by local environmental nonprofits. They also use their own creativity to accomplish projects that beautify and strengthen their own community, while being advocates for a clean and healthy environment to their friends and neighbors. Typical examples of community service projects include riverbank cleanups, recycling promotion and outreach, community garden or park cleanup and beautification, and tree plantings.

Personal Story/Anecdote from Workforce Program Employee

In order to continually improve the program, year after year, a great effort is made to collect detailed feedback from the participants through surveys and exit interviews. The input and insights of each cohort is used to craft the program of the following summer.

Tahee Purnell was 15 years old, a rising sophomore at Camden County Technical School in the summer of 2017 when he participated in the Green Ambassadors Program. He was enrolled in the Technical School's Academy of Law and Public Safety, and his career goal at the time was to become a law enforcement officer.

In his exit interview, he discussed how his view of the environment and personal decisions changed as a result of the program.

"I used to litter every day 'cause at the end of the day, it didn't affect me. Before the program I would be like everyone else and just throw trash on the ground not knowing. But after the program I realized there's parts of Camden that's beautiful, but it's not open to people because there's so much trash there. So really, what we do, it does affect us."

Year after year, UrbanPromise Ministries' Cooper River Ecology History Paddle is voted a top favorite activity by the Green Ambassadors. While out on the water, every summer without fail, at least one Green Ambassador will say something very close to "I can't believe we're in Camden right now." Of that day, Tahee said:

"My favorite part? There was a lot of good things going on, but I have to say the canoe ride, because you would never get to do that. Not unless you were in this program. It was really nice just to paddle through. It was calm too, like peaceful. There's not bad stuff out there."

When asked how the program affected his academic and/or career goals, Tahee said:

"I do school for law and public safety, so I didn't really ever look into environmental science. But after the program, I realized there's like, people in the DEP that solve

environmental cases, they carry a gun and a badge. Really they do the same thing as a cop, it's just a different perspective."

Benefits of Workforce program

The principal benefit of the program is to introduce high school students to the myriad careers dedicated to protecting the environment as well as the health and safety of the public. Especially because these students reside in Camden New Jersey, a heavily industrial city with a large number of brownfield sites and many environmental justice concerns. They learn how various government agencies, scientific institutions, environmental advocacy groups and industries interact, sometimes amicably and sometimes with conflict, and the ways in which that interaction improves or degrades the natural resources upon which we all rely.

A person cannot aspire to nor pursue a career path they are unaware of, and cannot work to rectify environmental injustices they do not understand. The Green Ambassador program gives students an in-depth look, through both learning and experience, at environmentally based careers at a formative time in their lives when critical career and academic choices are being made.

Outside Financial Support and/or program partners

The Green Ambassadors Program is self-funded by the Camden County Municipal Utilities Authority, with enormous help and cooperation from our partners:

- Camden Collaborative Initiative
- New Jersey Department of Environmental Protection
- Environmental Protection Agency
- UrbanPromise Ministries, Inc.
- Partnership for the Delaware Estuary
- The Salvation Army Kroc Center in Camden
- PowerCorps Camden
- Forest Resource Education Center
- New Jersey American Water
- South Jersey Land & Water Trust
- Rutgers University-Camden
- Camden Lutheran Housing, Inc.
- Camden Block Supporter Initiative
- Covanta Camden Energy Recovery Center
- After-School All-Stars
- New Jersey Audubon Society
- New Jersey Tree Foundation
- Delaware Valley Regional Planning Commission

Greatest Obstacles Encountered

Finding enough students to sign up for the program and follow through with the full process of obtaining the employment certificate to be employed as a minor is a challenge every year. Proper “marketing” strategies must be used to attract students in the first place. Students taking a cursory glance at the job application, or doing a brief internet search, might be turned off at the prospect of working at a waste treatment facility. A good relationship with, and outreach to the local schools and educators is essential for success.

After they have expressed interest and signed up, the onerous and convoluted process of obtaining a physician’s certification, personal documents, bouncing back and forth between their prospective employer, the school, the doctor, and the school board issuing officer can be daunting. Especially for families with limited resources and transportation options. Luckily, Camden high schools are often staffed with extraordinary guidance counselors and teachers that go the extra mile to help guide students through the process.

Links to Additional Information on Workforce Program

<https://bit.ly/cairns-ga>



Forming and Utilizing Your Supplemental CSO Team

For New Jersey's Combined Sewer Overflow (CSO) Permits and Long Term Control Plans

The Supplemental CSO Team is a resource to you. The Supplemental CSO Team will be beneficial in soliciting input from the public throughout the Long Term Control Plan (LTCP) process, and will enable you to better develop an outreach program that reaches a broad base of citizens. Through the Supplemental CSO Team, you, as the permittee will gain a public perspective on CSOs, local water quality issues and sewer system problems, and the public's willingness to participate in efforts to eliminate CSOs.

The members of the Supplemental CSO Team are not expected to be experts on CSOs or have extensive engineering backgrounds to participate. Members should be representative of the permitted communities or areas served by the sewage treatment plant. The Supplemental CSO Team can provide local information on flooding issues, neighborhood priorities, and community willingness to accept or participate in CSO alternatives (such as building or maintaining green infrastructure).

The Supplemental CSO Team, as part of your public participation process, is a two way dialogue and an opportunity for you to share information about your work and an opportunity for the team to provide input.

The Supplemental CSO Team should be provided with information to help it better understand the issues, costs, and operation of the collection and treatment systems. The Supplemental CSO Team should be aware of the various permit milestones and due dates. These milestones include installation of signs, public participation plan, the characterization of the combined sewer system, evaluation of alternatives analysis to reduce or eliminate CSOs, selecting alternatives, and implementation schedule, for example.

**Excerpt from Section G.2.c of the NJPDES CSO Permit (see <http://www.nj.gov/dep/dwq/cso.htm>)
describing the Supplemental CSO Team**

The permittee shall invite members of the affected/interested public to establish a Supplemental CSO Team to work with the permittee's assigned staff from Section F.1 and to work as an informal work group as a liaison between the general public and the decision makers for the permittee. The goals of the Supplemental CSO Team could consist of the following elements:

- i. Meet periodically to assist in the sharing of information, and to provide input to the planning process;*
- ii. Review the proposed nature and extent of data and information to be collected during LTCP development;*
- iii. Provide input for consideration in the evaluation of CSO control alternatives; and*
- iv. Provide input for consideration in the selection of those CSO controls that will cost*



Should a regional Supplemental CSO Team be formed that incorporates several hydraulically connected communities or would multiple supplemental teams be more effective?

It is up to you. Regional teams, if created, should be reflective of the various communities, populations, and social and environmental needs of the areas served by the sewage treatment plant.

Community-based Supplemental CSO Teams, as opposed to a regional Supplemental CSO Team, may be more effective if the communities in the hydraulically connected region:

- are unique;
- are geographically distant;
- are large in size or population;
- have widely diverse or various priorities; and/or
- have many active groups.

Both community-based and regional Supplemental CSO Teams may be needed in some cases. Community-based teams can be utilized to reach a more localized population, while a representative from the community-based team can participate in the regional Supplemental CSO Team as well.

Justification regarding the composition of the Supplemental CSO Team or Teams should be articulated in the public participation plan, as well as a discussion of the goals of the Supplemental CSO Team, feedback received so far from the Supplemental CSO Team, and frequency and type of team interaction.

Who should be involved in the Supplemental CSO Team?

The Supplemental CSO Team should be customized to meet your needs and the needs of your community. Consider inviting individuals or group representatives to participate in the Supplement CSO Team who have been involved in your past public participation efforts or who are currently involved with or concerned about CSOs and related issues (such as redevelopment, environmental improvement, waterfront access, community engagement, stormwater, or economic development).

The structure, organization and responsibilities of the Supplemental CSO Team should be representative of the issues and possible alternatives. The Supplemental CSO Team should represent the community's diverse perspectives and address the needs of the affected public. When considering the makeup of your Supplemental CSO Team you should keep in mind that pursuant to Section II.C.2 of the National CSO Policy, the affected public includes rate payers, industrial users of the sewer system, persons who reside downstream from the CSOs, persons who use and enjoy these downstream waters, and any other interested person.

Consider including representatives from the following interest groups:

- Community/neighborhood groups
- Environmental groups
- Recreational Water Users
- Business, Industry, and Redevelopment community
- Local Institutions (ex: academic, business, healthcare)
- Representatives of Local Government
- Faith based and social service based organizations

The optimum size of the Supplemental CSO Team can be determined by you but each team should be diverse and representative of the population served while still small enough to have effective meetings and dialog among the team members.



When inviting the public to participate on the Supplemental CSO Team, share with them what they should expect by participating and how much time they should plan to dedicate to this effort. Keep in mind that the public participation process will involve more than the Supplemental CSO Team. Therefore, if there are members of the public that are unable to commit to the Supplemental CSO Team, they should be invited to participate in the broader public participation effort.

Several CSO communities may have teams formed around issues related to CSOs, such as a community based green infrastructure team, municipal action team, or green team. These teams may or may not include the diversity of representatives that are needed for the Supplemental CSO Team. Evaluate how best to utilize and build off of these existing teams.

What frequency should my Supplemental CSO Team meet?

The role of the Supplemental CSO Team may differ among permittees and their participation in the LTCP development process should correlate with the area impacted; the number of people impacted; and resources needed to implement the LTCP. The Supplemental CSO Team should meet as often as needed for the team to ultimately be able to meaningfully provide input on the evaluation of CSO alternatives. However, the Department would expect the Supplemental CSO Team to meet in person no less than when important milestones and reports are completed throughout the LTCP development process. The Supplemental CSO Team may need to meet frequently in the beginning of the LTCP development process in order to establish goals and learn about the LTCP and less frequently while studies and reports are being conducted and developed. As the time approaches to evaluate and provide input on alternatives, the Supplemental Team may need to again meet more frequently. Meeting types and locations may differ from one permittee to another as well as from one task to another throughout the LTCP process. In person meetings might be the primary way for the Supplemental CSO Team to operate. There are other methods that may be helpful to share information and gain feedback from the Supplemental CSO Team, such as conference calls, emails, online surveys and website updates, among others.

Meetings held on a consistent schedule and at a convenient location enable continued participation. Weekend and evening meetings may work best for your team members. When selecting a meeting location think about if the location is accessible via public transportation, has free parking, and does not require extensive security checks.

Who should facilitate the Supplemental CSO Team?

It is ultimately your responsibility to ensure that the Supplemental CSO Team is conducted and facilitated so that all permit requirements are met. The Supplemental CSO Team could be led by staff within your organization or municipality or by hired professionals. Whomever you choose to lead your Supplemental CSO Team, you should seek individuals that have the following facilitation skills:

- experience engaging with the public;
- ability to translate complex issues;
- facilitate and encourage active listening and;
- accepting of different perspectives and ideas.



What's the Supplemental CSO Team's role in public participation?

The Supplemental CSO Team will be a great asset for developing and implementing parts of the public participation process. Members of your Supplemental CSO Teams are likely to be members of other networks and can be conduits for sharing information with their peers and neighbors. Providing feedback on community reaction, effective ways to share information, and input on your public participation strategy are great ways to utilize the Supplemental CSO Team. You may find that your Supplemental CSO Team will assist you in public participation activities.

The Supplemental CSO Team will be beneficial in soliciting input from the public throughout the planning process, and will enable you to better develop an outreach program through public meetings and public hearings that reaches a broad base of citizens. By using the Supplemental CSO Team to develop and implement a larger public engagement process, you will gain a public perspective on local water quality issues and sewer system problems, the amount of public concern about CSOs in particular, and the public's willingness to participate in efforts to eliminate CSOs.



Supplemental Team Examples

CSO communities in other states have implemented networks similar to Supplemental CSO Teams. The following two examples can provide helpful information on how to organize and utilize these teams. Links are provided for additional information on Philadelphia and Nashville's public participation process for developing their Long Term Control Plans and engaging the public.

Philadelphia, PA



Business

- Building Industry Association

Citizen Groups

- Northern Liberties Neighborhood Association
- Passyunk Square Neighbors Association
- Washington West Civic Association

Interest Groups

- Community Legal Services, Inc.
- Delaware River City Corporation
- Impact Services Corporation
- PennFuture (Next Great City)
- Pennsylvania Environmental Council
- Tookany/Tacony-Frankford Watershed Partnership
- Schuylkill River Development Corporation
- Sierra Club

Regulatory Agencies

- Pennsylvania Department of Environmental Protection (PADEP)

Local Government Agencies

- Fairmount Park Commission
- Mayor's Office of Sustainability
- Philadelphia Water Department

See table 2-1 at the following link for the advisory committee membership:

http://www.phillywatersheds.org/ltcp/LTCPU_Section02_Public%20Participation.pdf

The Public Participation Program Team assembled a diverse group of stakeholders to comprise the *Green City, Clean Waters* Advisory Committee. The committee consists of key city, state and community representatives (including civic organizations in neighborhoods affected by sewage backups during intense rainstorms), as well as leaders of local, regional and national environmentally -minded organizations. Targeted efforts were made to invite civic leaders of the impacted neighborhoods (and who represent ratepayers), industrial users, and organizations that represent people that live near and use the impacted areas. A majority of the representatives who actively participate on the advisory committee belong to organizations whose missions concentrate on civic and environmental issues. (Section 2.2.1, page 2-4)

This is an example of an advisory committee or local stakeholder team. Your Supplemental CSO Team is likely to include many of these sub-groups and it is important for local decision makers (City Council, Planning Boards, Zoning Boards, Redevelopment Committees, to name a few) to either be a part of this group or ensure its involvement in the LTCP development through other methods.



Nashville, TN

Nashville developed a Citizens Advisory Committee along with many other public engagement activities. Their Citizen Advisory Committee was designed “to extend the public engagement initiative far into communities, and to generate the most thorough input from residents, businesses, neighborhood associations, and other organizations. These were individuals who were recognized as leaders and experienced conveners in their respective neighborhoods. In this case, these leaders and their respective organizations were located throughout the urban core, the most affected areas of the LTCP Update.” (Section 8.3) Members included representatives from faith based organizations, academia, historic committee, metropolitan council, neighborhood and park organizations, transit authority, health department, and business groups to name a few.

<http://www.cleanwaternashville.org/content/resources/pdfs/pdr/LongTermControlPlan.pdf>

8.2 Public Engagement Highlights

From fall of 2009 through the spring 2011, MWS, supported by its consultant team, conducted a public engagement and input campaign, the highlights of which include:

- Created a Citizens Advisory Committee (CAC) to participate and be the primary community voice in the campaign on an ongoing basis. This group includes representatives from neighborhood and business organizations, professional experts, river users, and community stakeholders.
- Developed the “Clean Water Nashville” theme for the campaign.
- Organized a series of ongoing community meetings throughout Nashville’s urban core, which is the combined sewer system (CSS) area. These meetings introduced the community to the LTCP Update program and provided ongoing updates; the final report will be the subject of a future meeting.
- Made presentations to Nashville’s leading environmental groups.
- Engaged more than a dozen leading neighborhood associations, and more than ten major Nashville area business organizations.
- Involved all district Metro Council members in the affected CSS areas.
- Involved the Public Works Committee Chairman of the Metro Council as a leader in the public process.
- Developed Web and Public Access Television programming, including an on-line catalog of LTCP Committee and CAC activity.
- Collected meaningful input from stakeholder groups that has helped shape the overall LTCP plan and its recommendations.

Scott Schreiber

From: Caldarelli, Adriana <Adriana.Caldarelli@dep.nj.gov>
Sent: Monday, March 20, 2017 2:58 PM
To: Scott Schreiber
Cc: Andy Kricun; Doug Burns; Pepe, Rachael; Feltis, Jennifer
Subject: RE: CSO Supplemental Team

Scott,

The revisions look great. I ran it by our experts and they agree that the supplemental team can and should evolve as the process does, so I think you should go ahead and schedule a kickoff meeting to get the process started. We could throw out as a discussion point during the kickoff meeting whether the invitee list is inclusive enough and take suggestions. For instance, Jennifer Feltis suggested that we may want to engage large property owners near outfalls, like marinas, etc., so perhaps the group could provide suggestions and feedback.

Let me know if you need anything else.

Sincerely,

Adriana Caldarelli

NJDEP Division of Water Quality
Office of the Assistant Director, Water Pollution Management Element
401 E. State St
PO Box 420, Mail Code 401-2B
Trenton, NJ 08625
609-422-7671
609-777-0432 (fax)



From: Scott Schreiber [mailto:sschreiber@ccmua.org]
Sent: Monday, March 20, 2017 11:59 AM
To: Caldarelli, Adriana <Adriana.Caldarelli@dep.nj.gov>
Cc: Andy Kricun <andy@ccmua.org>; Doug Burns <doug@ccmua.org>
Subject: CSO Supplemental Team

Adriana,

Andy, Doug and I wanted to follow up on the previous comments offered by you and the public participation experts at the NJDEP by submitting a revised roster of potential Camden City CSO Supplemental Team participants (below). Our goal is to be responsive to the NJDEP guidance document *Forming and Utilizing Your Supplemental CSO Team* and the aforementioned NJDEP comments offered after our initial submission of potential participants. We made every effort to be more inclusive of the types of individuals and entities that are represented while creating this revised potential roster. Further, it is our intention to have an initial meeting with this group of community leaders and ask them to reach

out to colleagues and/or residents who live in the City of Camden and invite them to all future meetings. In other words, we do not view the CSO Supplemental Team as a static group of individuals or entities but rather an evolving one which aims to address the concerns of residents and rate payers of the City. We very much look forward to receiving your comments. Thank you.

Best Regards,
Scott Schreiber

<u>Entity</u>	<u>Individual(s)/Organizations</u>
Camden City	Uzo Ahirakwe, Patrick Keating, Joe Thomas
American Water	James Cowley
Camden City Public Schools	Brendan Lowe
Camden SMART	Camden City, CCMUA, Cooper's Ferry, Rutgers, NJ Tree Foundation, NJDEP
NJ Conservation Foundation	Olivia Glenn
Camden Redevelopment Agency	James Harveson
Center for Aquatic Sciences	Brian DuVall and/or Angela Wenger
Urban Trekkers/Urban Boat Works	Jim Cummings
Camden Block Supporter Initiative	Pino Rodriguez
Kroc Center – Camden	Demetrius Marlowe
Center for Environmental Transformation	Teresa Niedda
The Neighborhood Center	Christa Galvin
Rutgers University	Student Recommended from Faculty/Staff

Scott Schreiber
Director of Administrative Operations
Camden County MUA
1645 Ferry Avenue
Camden, NJ 08104
P - 856-583-1261
F - 856-964-1829


Supplemental CSO Team Invitees

Entity

American Water
Camden City
Camden City Public Schools
Camden Kroc Center
Camden Redevelopment Agency
Center for Aquatic Sciences
Center for Environmental Transformation
Cooper's Ferry Partnership
New Jersey Conservation Foundation
NJ Tree Foundation
NJDEP
Rutgers University
Rutgers Water Resource Program
The Neighborhood Center
Urban Promise

Individuals

James Cowley
Uzo Ahirakwe, Patrick Keating, Joe Thomas
Brendan Lowe
Demetrius Marlowe
James Harveson
Brian DuVall
Teresa Niedda
Meishka Mitchell, Sarah Bryant, Caroline Gray
Olivia Glenn
Lisa Simms
Franklin McLaughlin, Adriana Caldarelli, Armando Alfonso
Larry Gaines
Jeremiah Bergstrom
Amelia Kaselaan
Jim Cummings



THE CAMDEN COUNTY MUNICIPAL UTILITIES AUTHORITY

1645 Ferry Avenue • Camden, NJ 08104
Phone (856) 541-3700 • Fax (856) 964-1829
www.ccmua.org

April 7, 2017

Delivered via Email

Olivia Glenn
Regional Manager, South Jersey Metro
New Jersey Conservation Foundation
170 Longview Road
Far Hills, NJ 07931

Re: Combined Sewer Overflow Supplemental Team

Dear Ms. Glenn:

The New Jersey Department of Environmental Protection has issued new permits to all entities which own combined sewer outfalls. One of the goals of these new permits is to significantly reduce the frequency and volume of combined sewage overflows (CSO) that enter receiving streams and rivers during wet weather. The City of Camden and the Camden County MUA (CCMUA) are working together on a Long Term Control Plan which, when completed, will provide a blueprint that will allow the City and the CCMUA to be in compliance with the permit, reduce or eliminate CSO events, improve the water quality of the receiving streams and, most importantly, eliminate combined sewage street flooding.

An integral part of the Long Term Control Plan is to solicit public participation via a CSO Supplemental Team. Through the CSO Supplemental Team, the City and the CCMUA will gain a public perspective on CSOs, local water quality issues and sewer system problems including flooding. Members of the CSO Supplemental Team are not expected to be experts or engineers but will be expected to provide information on neighborhood priorities and input on possible CSO alternatives like green infrastructure.

Are you willing to be a CSO Supplemental Team Member?

If so, the City of Camden and the CCMUA will invite you to several meetings over the next year and will also ask you to invite other members of the community you feel should be included in the process of creating the Long Term Control Plan. It is my hope that upon completing this voluntary service all CSO Supplemental Team members will have a better understanding of the combined sewer system, the permitting process, the goals of the Long Term Control Plan and, most importantly, will help guide the City and the CCMUA on selecting ways that meet both the local needs and desires and that effectively control CSOs and flooding.

Please let me know if you would like to join by emailing me at andy@ccmua.org. Thank you very much for considering this important community service.

Best Regards,

A handwritten signature in blue ink, appearing to read "AK", is written over a horizontal line.

Andrew Kricun, P.E., BCEE
Executive Director/Chief Engineer
Camden County Municipal Utilities Authority

Camden City - CCMUA CSO Supplemental Team

Kick Off Meeting

May 25, 2017

CCMUA Administration Building

Agenda

- ▶ -Combined Sewer Systems
- ▶ -Combined Sewer Overflows
- ▶ -Combined Sewage Flooding
- ▶ -The Long Term Control Plan
- ▶ -The Role of the CSO Supplemental Team
- ▶ -Topics for Future Meetings
- ▶ -Inviting Community Members to Future Meetings

What is a Combined Sewer System (CSS)?

The Environmental Protection Agency Defines a CSS as:

- ▶ A combined sewer system (CSS) collects rainwater runoff, domestic sewage, and industrial wastewater into one pipe. Under normal conditions, it transports all of the wastewater it collects to a sewage treatment plant for treatment, then discharges to a water body. The volume of wastewater can sometimes exceed the capacity of the CSS or treatment plant (e.g., during heavy rainfall events or snowmelt). When this occurs, untreated stormwater and wastewater, discharges directly to nearby streams, rivers, and other water bodies.
- ▶ Combined sewer overflows (CSOs) contain untreated or partially treated human and industrial waste, toxic materials, and debris as well as stormwater. They are a priority water pollution concern for the nearly 860 municipalities across the U.S. that have CSSs.

CSSs Used to be State of the Art




www.alamy.com - D97W2K

But Not Anymore



Combined Sewer Overflows

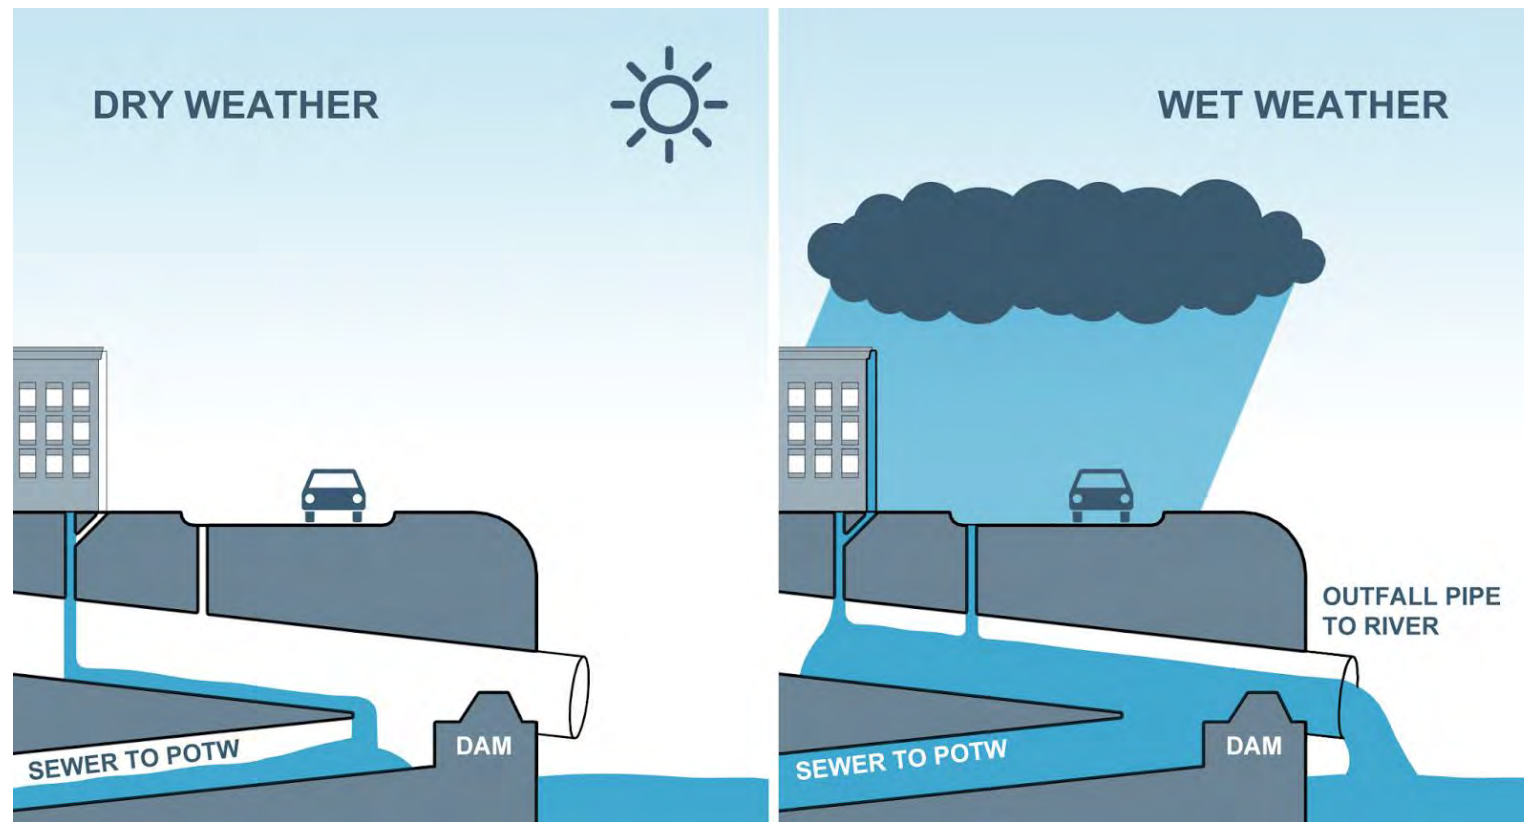

Total Overflow - Camden City & CCMUA


- ▶ 833 Millions of Gallons per Year Overflow into Cooper River, Delaware River and Newton Creek
- ▶ 23 Outfalls Overflow on Average 37 Times Per Year

Overflows by Receiving Stream

- ▶ Cooper River
 - ▶ 9 CSO Outfalls
 - ▶ 274 MGY
 - ▶ Average of 46 Events per Outfall
- ▶ Delaware River
 - ▶ 12 CSO Outfalls (11 Camden City, 1 CCMUA)
 - ▶ 509 MGY
 - ▶ Average of 36 Events per Outfall
- ▶ Newton Creek
 - ▶ 2 CSO Outfalls
 - ▶ 50 MGY
 - ▶ Average of 30 Events per Outfall

Combined Sewage Flooding

► <https://youtu.be/m2j8UGGZqGY>

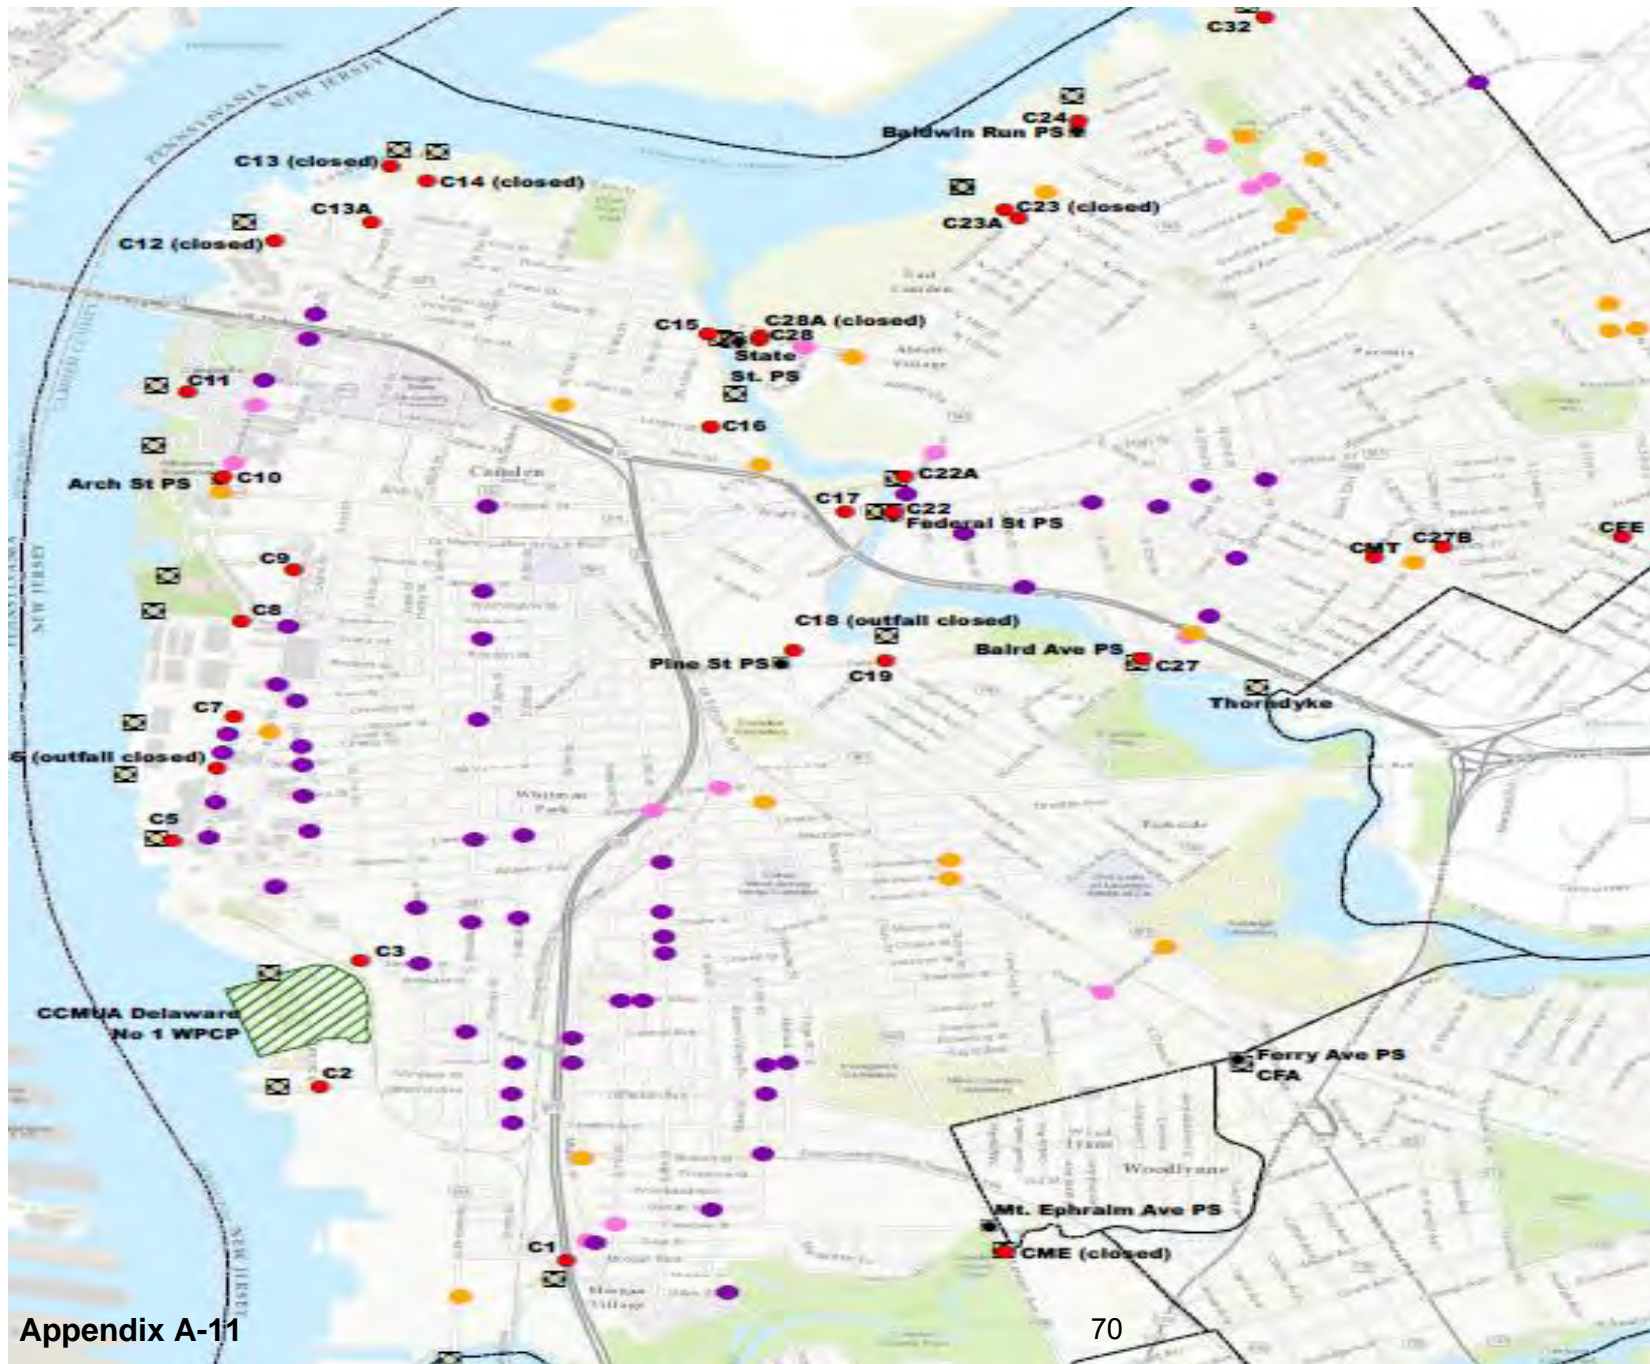

The Long Term Control Plan



Characterization, monitoring,
and modeling of the combined
sewer system



Public participation



Consideration of
sensitive areas



Evaluation of
alternatives to meet
CWA requirements



Cost/performance
considerations



Operational Plan



Maximizing treatment at
the existing wastewater
treatment plant



Implementation
schedule



Post-construction
compliance
monitoring program

Public Participation

The CSO Supplemental Team

Excerpt from Section G.2.c of the NJPDES CSO Permit (see <http://www.nj.gov/dep/dwg/cso.htm>) describing the Supplemental CSO Team

The permittee shall invite members of the affected/interested public to establish a Supplemental CSO Team to work with the permittee's assigned staff from Section F.1 and to work as an informal work group as a liaison between the general public and the decision makers for the permittee. The goals of the Supplemental CSO Team could consist of the following elements:

- i. Meet periodically to assist in the sharing of information, and to provide input to the planning process;*
- ii. Review the proposed nature and extent of data and information to be collected during LTCP development;*
- iii. Provide input for consideration in the evaluation of CSO control alternatives; and*
- iv. Provide input for consideration in the selection of those CSO controls that will cost*

Topic for Next Meeting:

Section 7 - Sensitive Areas

CCMUA will evaluate the receiving stream reaches to which its CSOs discharge to identify any areas which may be defined as sensitive areas pursuant to the 1994 CSO Control Policy (59 FR 75-18692):

- i. Outstanding National Resource Waters;
- ii. National Marine Sanctuaries;
- iii. Waters with threatened or endangered species or their designated critical habitat;
- iv. Primary contact recreation waters, such as bathing beaches;
- v. Public drinking water intakes or their designated protection areas;
- vi. Shellfish beds.

The locations of CSOs vis-à-vis the sensitive areas, the nature of the sensitive areas and the available information regarding CSO impacts on any sensitive areas that are identified will be detailed in the System Characterization Report. The databases and records searches used to identify sensitive areas will be documented in the report. Sources will include the published reports and databases identified in Table 1, as well as information from the municipalities, stakeholders and public comments to identify any conditions which may include those of sensitive areas as defined in the CSO Policy, e.g. primary contact recreation.

Please Invite Community
Members to
Future Meetings

Thank you!

<u>List of Supplemental CSO Team Meeting #2 Attendees</u>	
Sensitive Areas Meeting: 12/13/17	
Name	Organization
Jose Santiago	Block Supporters Initiative
Destiny Wilson	Urban Promise Academy
Hope Lugo	Urban Promise Academy
Jeremiah Bean	Urban Promise OEL
Jim Cummings	Urban Promise OEL
Meredith Brown	NJ Tree Foundation
Jessica Franzini	Camden Lutheran Housing
Jeremiah Bergstrom	Rutgers Camden
Carlos Morales	Heart of Camden
Teresa Nieda	Center for Environmental Transformation
Demetrius Marlowe	Salvation Army Kroc Center
Olivia Glenn	NJ Conservation Foundation
Pat Keating	Camden City
Armando Alfonso	NJDEP
Shaza Qizvi	NJDEP
Susan Rosenwinkel	NJDEP
Josie Horowitz	NJDEP
Tim Feeney	CCMUA
Doug Burns	CCMUA
Scott Schreiber	CCMUA
Andy Kricun	CCMUA

Appendix A-12

<u>List of Supplemental CSO Team Meeting #2 Attendees</u>	
Sensitive Areas Meeting: 12/13/17	
Name	Organization
Jose Santiago	Block Supporters Initiative
Destiny Wilson	Urban Promise Academy
Hope Lugo	Urban Promise Academy
Jeremiah Bean	Urban Promise OEL
Jim Cummings	Urban Promise OEL
Meredith Brown	NJ Tree Foundation
Jessica Franzini	Camden Lutheran Housing
Jeremiah Bergstrom	Rutgers Camden
Carlos Morales	Heart of Camden
Teresa Nieda	Center for Environmental Transformation
Demetrius Marlowe	Salvation Army Kroc Center
Olivia Glenn	NJ Conservation Foundation
Pat Keating	Camden City
Armando Alfonso	NJDEP
Shaza Qizvi	NJDEP
Susan Rosenwinkel	NJDEP
Josie Horowitz	NJDEP
Tim Feeney	CCMUA
Doug Burns	CCMUA
Scott Schreiber	CCMUA
Andy Kricun	CCMUA


Appendix A-12

CSO Supplemental Team

Sensitive Areas Identification

12/13/17 Meeting

Combined Sewer Overflows

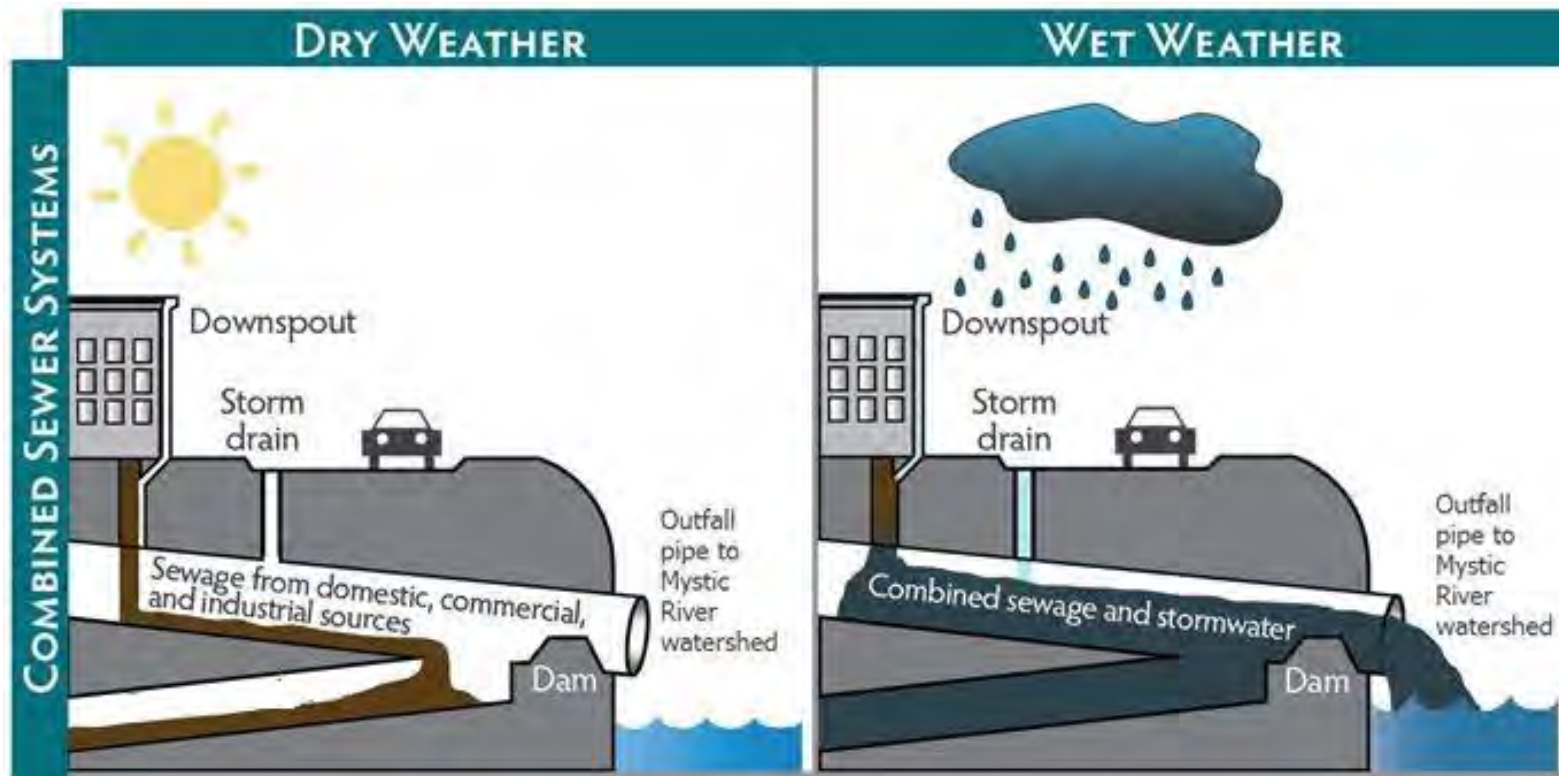

Long Term Control Plan



Characterization, monitoring,
and modeling of the combined
sewer system



Public participation




Consideration of
sensitive areas




Evaluation of
alternatives to meet
CWA requirements



Cost/performance
considerations



Operational Plan



Maximizing treatment at
the existing wastewater
treatment plant



Implementation
schedule



Post-construction
compliance
monitoring program


Supplemental CSO Team


- “Members should be representative of the permitted communities or areas served by the sewage treatment plant. The Supplemental CSO Team can provide local information on flooding issues, neighborhood priorities, and community willingness to accept or participate in CSO alternatives (such as building or maintaining green infrastructure).”



Sensitive Areas


- 1) Outstanding National Resource Waters
- 2) National Marine Sanctuaries
- 3) Threatened or Endangered Species Habitat
- 4) Public Drinking Water Intakes
- 5) Shellfish Beds
- 6) Primary Contact Recreation

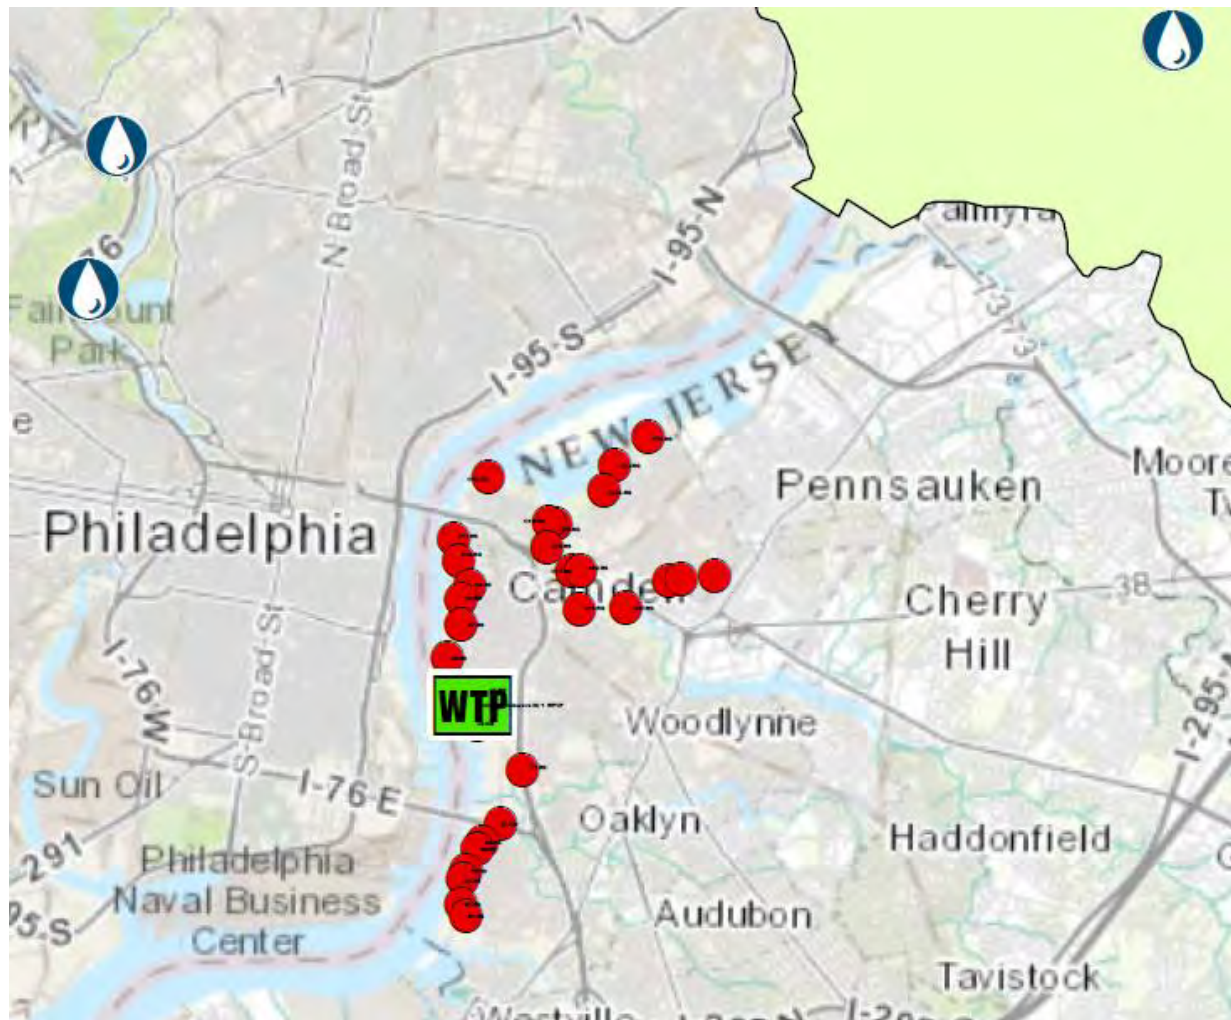

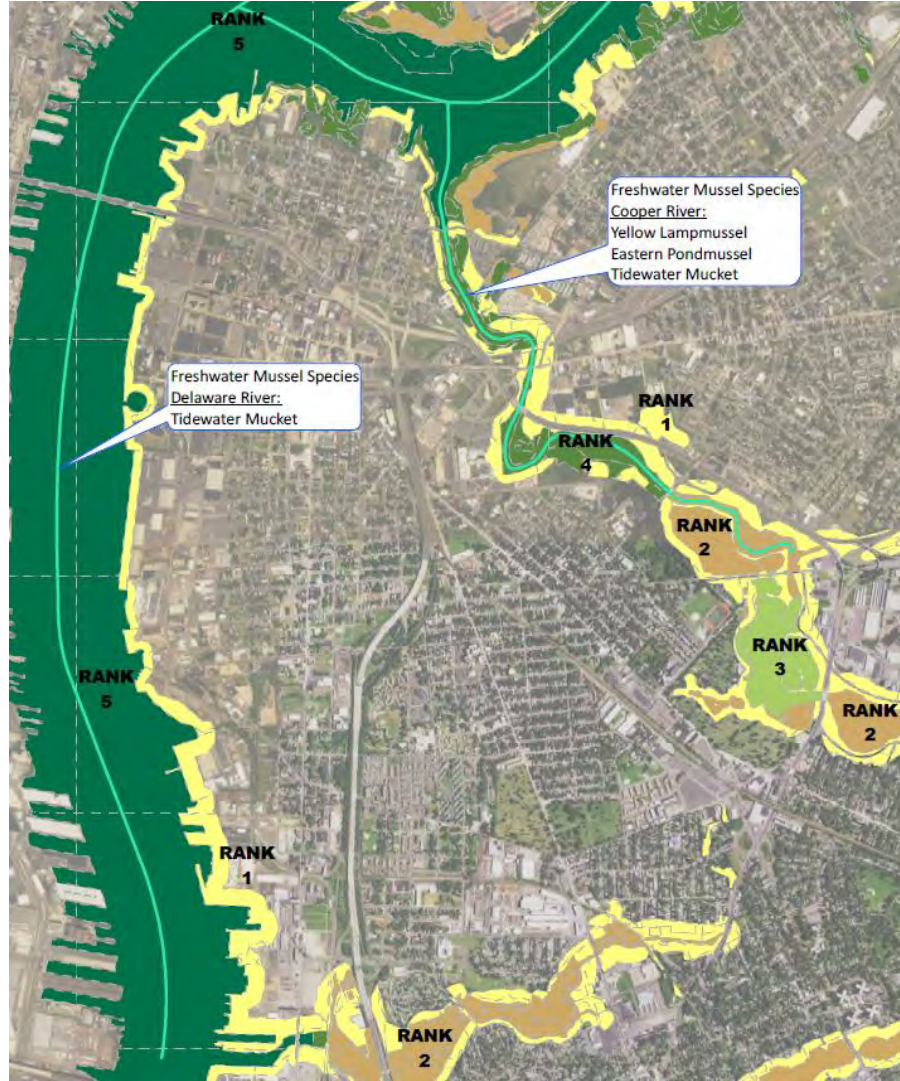

Primary Contact Recreation

- Swimming, Boating, Fishing etc.
- Philadelphia Control Plan Example:
 - “An annual triathlon is held in the Schuylkill River above Fairmount Dam. This area is upstream of PWD’s CSO outfalls on the Schuylkill River. Occasional primary contact recreation occurs in Cobbs Creek and Tacony-Frankford Creek. These activities are unsafe in addition to exposing recreators to potentially unsafe levels of pathogens in wet weather. The City is addressing these concerns through education, signage, and enforcement.”

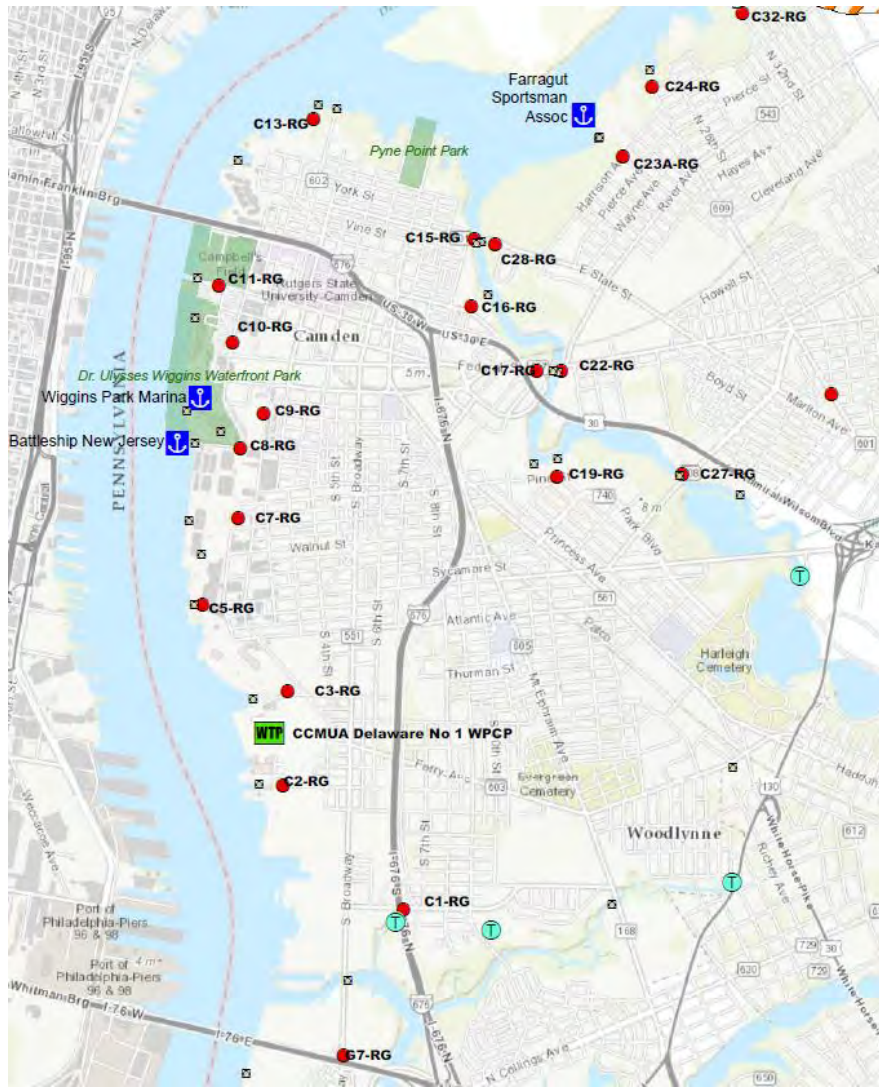

Questions for us:

- Where do people canoe/kayak?
- Where do people fish?
- Where do people swim?
 - Official/Annual Events? Informally?



Map of Primary Contact Recreation Areas






Newton Creek Access Points

-  Johnson Blvd Recreation Dev Canoe Access
-  Reverend Evers Park Access Point
-  Gloucester City Little League Majors Field






Cooper River Access Points

-  Cramer Hill Waterfront Park
-  Kaighn Ave Dam Access
-  Gateway Park Proposed Access



Back Channel Access Points

-  Pyne Poynt Park
-  36th St

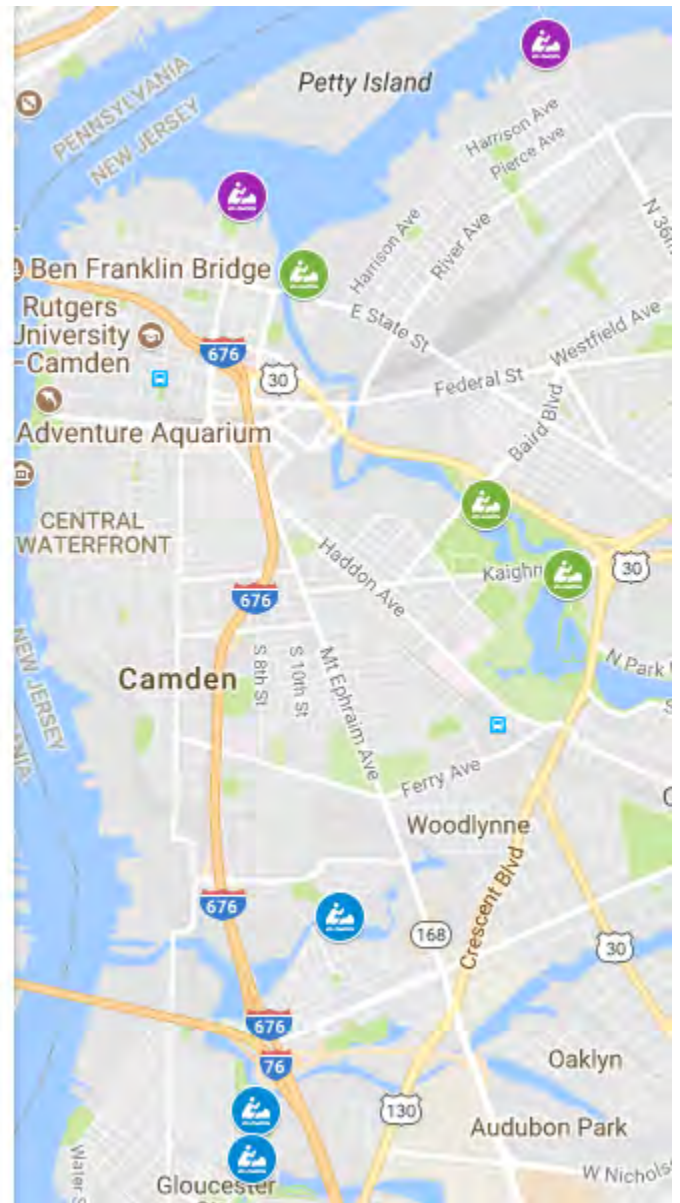

Invitee List of Camden CSO Supplemental Team – June 20th 2019

Vince Quarles	American Water	vincent.quarles@amwater.com
Caroline Gray	American Water	Caroline.Gray@amwater.com
Dalvin Krug	American Water	dalvin.krug@amwater.com
Pino Rodriguez	Block Supporters Initiative	secondstepinc@yahoo.com
Joe Thomas	Camden City	jothomas@ci.camden.nj.us
Pat Keating	Camden City	pakeatin@ci.camden.nj.us
James Rizzo	Camden City	JaRizzo@ci.camden.nj.us
Brendan Lowe	Camden City Public Schools	blowe@camden.k12.nj.us
Donna Pettigrew	Camden Redevelopment Agency	DoPettig@ci.camden.nj.us
Peter Kroll	CCMUA	pkroll@ccmua.org
Doug Burns	CCMUA	doug@ccmua.org
Scott Schreiber	CCMUA	sschreiber@ccmua.org
Tim Feeney	CCMUA	tfeeney@ccmua.org
Brian DuVall	Center for Aquatic Sciences	bduvall@njaas.org
Angela Wenger	Center for Aquatic Sciences	AWenger@aquaticsciences.org
Teresa Niedda	Center for Environmental Transformation	director@cfet.org
Jon Compton	Center for Environmental Transformation	farmer@cfet.org
Alyssa Ward	CFS - PowerCorps	alyssa.ward@centerffs.org
Terrence Thompson	CFS - PowerCorps	terrance.thompson@centerffs.org
Onna Jones	CFS - PowerCorps	onna.jones@centerffs.org
Jahtieh Postell	CFS - PowerCorps	jahtieh.postell@centerffs.org
Meishka Mitchell	Cooper's Ferry Partnership	meishka@coopersferry.com
Sarah Bryant	Cooper's Ferry Partnership	bryant@coopersferry.com
Christoff Lindsey	CUAC / Community Member	krslnz@aol.com
Lew Bivona	CUAC / PBCIP	lewis.bivona@gmail.com
Eric Fooder	Gloucester City	ericfooder@cityofgloucester.org
Carlos Morales	Heart of Camden	cmorales@heartofcamden.org
Justin Dennis	New Jersey Conservation Foundation	justin.dennis@njconservation.org
Lisa Simms	NJ Tree Foundation	lsimms@njtreefoundation.org
Meredith Brown	NJ Tree Foundation	mbrown@njtreefoundation.org
Armando Alfonso	NJDEP	armando.alfonso@dep.nj.gov
Josie Horowitz	NJDEP	Josie.Horowitz@dep.nj.gov
Shaza Qizvi	NJDEP	
Susan Rosenwinkel	NJDEP	susan.rosenwinkel@dep.nj.gov
Franklin McLaughlin	NJDEP	frank.mclaughlin@dep.nj.gov
Monique Phillips	NV5	monique.phillips@nv5.com

Jonathan Wetstein	PBCIP	manager@parksidertm.com
Tobiah Horton	Rutgers	tah148@sebs.rutgers.edu
Larry Gaines	Rutgers	gaines@camden.rutgers.edu
Matthew Leconey	Rutgers	matthew.leconey@rutgers.edu
Hope Lugo	Urban Promise Academy	
Jim Cummings	Urban Promise OEL	jcummings@urbanpromiseusa.org
Orion Joyner		orionj@ci.camden.nj.us
Betsy Clifford		bclifford@clhi.org
Rachel Pepe		rachael.pepe@dep.nj.gov
Gregory Gamble		gambleg@camden.rutgers.edu
Keith Walker		kewalker@ci.camden.nj.us
Rachel Abbott		rabbott@urbanpromiseusa.org
Joanne Higgins		jhiggins@urbanpromiseusa.org
Enrique Rivera	St. Joseph Carpenter	erivera@sjcscamden.org
Pilar Closkey	St. Joseph Carpenter	phogan@sjcscamden.org

LTCP Supplemental Team - 1/16/20 Sign-In Sheet

NAME	ORGANIZATION	EMAIL
Alyssa Ward	PowerCorps Camden (Center for Family Services)	alyssa.ward@centkffs.org
Eric G. Foulis	Gloucester C. Ty Dept of utilities	ericfoulis@cityofgloucester.org
Monique Phillips	NVS inc	monique.phillips@NVS.com
Michael English	PowerCorps Camden	Mike.english0420@gmail.com
PK ROLL	CCMVA	PKROLL@CCMVA.ORG
S. Rosenwinkle	NJDEP	susan.rosenwinkle@dep.nj.gov
Molly Jacoby	NJDEP	molly.jacoby@dep.nj.gov
Sherry Preisig	NJDEP	sherry.preisig@dep.nj.gov
MARCUS RAO	NJDEP	MARCUS.RAO@dep.nj.gov
Erin Riva	SSCS	erivern@sjcscamden.org
Gary A Brooks	AM water	gary.brooks@amwater.com
Jim Hopkins	BH - City of Camden	jhopskins@buchanathoen.com
Matthew Leconeg	Rutgers WRP	matthew.leconeg@rutgers.edu
Sarah Bryant	CFP	bryant@coopersferry.com
Veronica Sanchez	PowerCorps Camden	v.sanchez8201@icloud.com
DABBERS BURAS	CCMVA	DAB@CCMVA.ORG
Shaila Martinez	PowerCorps Camden	
Kiey Hunley	PowerCorps Camden	
Terrance Thompson	PowerCorps Camden	Terrance.Thompson@centkffs.org
Lew Bivona	PRCIP	lew@parksidestm.com
Tim Feeney	CCMVA	tfeeney@ccmva.org
